AECOM
303 E. Wacker Drive, Suite 900
Chicago, Illinois 60601

312-938-0300 tel
312-938-1109 fax

November 13, 2012

Mr. Narendra Prasad
People's Gas Light & Coke Co.
Environmental Services Department
130 East Randolph, 22nd Floor
Chicago, IL 60601

RE: Radiological Survey of Right-of-Way Utility Excavation
Permit No.: 281094044
Permit Address: 201 East North Water Street
AECOM Project No. 60157647

Dear Mr. Prasad:

Pursuant to conditions specified in a permit (see attached) issued by the City of Chicago, radiation monitoring was required to be performed at the above referenced site. AECOM Technical Services, Inc. (AECOM) provided the required radiation surveillance completed on the day of November 9, 2012 for an excavation to inspect a cutoff of existing gas service piping.

Surveying was performed for the soil removed from a 3-foot by 4-foot excavation along East North Water Street (see sketch) to a depth of 3.5-feet below ground surface required for inspection of a cutoff of existing gas service piping. The monitoring revealed no indication of soils above the specified clean-up value established by the U. S. Environmental Protection Agency (USEPA) for the Streeterville area of Chicago. The USEPA clean-up value for Chicago's Streeterville area is 7.1 picocuries per gram (pCi/g total radium (Ra-226 + Ra-228).

Gamma radiation count measurements for the project were made using Ludlum Model 2221 survey meter and an unshielded 2 x 2 inch NaI probe (Model 44-10). For the instrument used, the gamma count threshold equivalent to the 7.1 pCi/g clean-up value was 20,356 counts per minute (cpm) unshielded (7,567 cpm shielded). The field gamma background for the area was measured at approximately 3,800 cpm unshielded. The field gamma measurements within the excavation did not exceed the respective field instrument threshold value previously stated and ranged from a minimum of 5,800 cpm to a maximum of 7,100 cpm unshielded. Thus, there was no indication of the presence of radiologically-contaminated material and/or an exceedance of the USEPA cleanup value of 7.1 pCi/g total radium.

As part of the permit conditions this letter has been forwarded to:

Chicago Department of Public Health
Attention: Ms. Rahmat Begum
333 South State Street, Rm. 200
Chicago, Illinois 60604

Please contact us with any questions you have regarding this letter or the reported results.

Regards,

Joshua J. Rowe
Project Scientist II

Steven C. Kornder, Ph.D.
Senior Project Geoscientist

cc: Rahmat Begum, Chicago Department of Public Health
Verneta Simon, USEPA

Attachments: Permit
Sketch

Permit # 281094044

Received Date: Nov 5, 2012 9:44:51

PEOPLES GAS LIGHT & COKE CO
130 EAST RANDOLPH DRIVE
CHICAGO, IL 60601

HERMAN 773-542-7830

City of Chicago
Department of Transportation
(312) 744-4652

ACTIVITY HOURS

See RESTRICTIONS for permitted hours

DATES

Nov 5, 2012 through Nov 16, 2012

ACTIVITIES

Street Opening (Traffic Lane): **Dig #: TBD**

There will be 1 opening(s) in the public way for the purpose: INACTIVE CUT OFF.

3 Feet x 5 Feet x 5 Feet

Excavation may commence on - NO SOONER.

201 - 217 E NORTH WATER ST

9 AM - 4 PM, MONDAY - FRIDAY
8 AM - 5 PM, SAT - SUN

MUST BE RESTORED & COMPLETED BY: 11/16/12

OK M SIMON

Restrictions:

1. A copy of the permit must remain on-site for inspector's review.

5207301831

Restrictions:

2. Permit fees must be paid within 24 hours of the date of issuance. Failure to pay will result in you being considered in violation of the terms and agreement of the permit and subject to any applicable fine and fees as if you never attained a permit. Additionally, you will still be responsible for the cost of the original permit. Monthly billing accounts are not applicable to the 24 hour payment criteria but failure to pay the monthly bill by the due date will result in the same penalties applying.
3. All directional boring must be pre-approved by the Office of Underground Coordination.
4. Contractor must secure plating over all openings in the roadway and secure all sidewalk/parkway openings during non-working hours until such time when the road surface is restored.
5. All traffic control will be the responsibility of the contractor and must comply with all MUTCD standards.
6. Restore all lanes to normal operation during non-working hours.
7. Must use flagmen and/or arrow boards to maintain traffic operations through the work zone.
8. Contractor must notify DIGGER at 312-744-7000 no less then 48 hours (exclusive of Saturdays, Sundays and Holidays) but no more then 14 calendar days in advance of the start of the excavation or demolition, unless the excavation date was provided with the application and remains unchanged. Prior to 26 calendar days the Contractor must notify DIGGER to renewal the dig date!
9. It is the Excavator's responsibility to request refreshing of marks when needed, but no longer than 28 calendar days after the last requested date.
10. When applicable, all excavation areas are to be clearly marked in safety white paint prior to calling DIGGER. White paint is not required for joint meets or emergency work.
11. Excavators requesting dig tickets are responsible for the protection of utility markings at the job site. Any markings of underground utilities utilizing utility colors, must be done by facility owners or authorized agents only.
12. Permittee must provide a sign which identifies the telephone number and company or person performing the work. Signage may be affixed to barricades.
13. Use of pneumatic equipment must not begin before 8:00 A.M. or continue after 8:00 P.M.
14. Permanent base pavement restoration to follow within 5 days after the completion of underground work.
15. All pavements and pavement markings are to be restored in accordance with CDOT Construction Standards.
16. All street openings must be restored with concrete base to grade.
17. Streets recently resurfaced must be restored to proper standards (resurface to nearest 1/4 pt, see CDOT Construction Standards for further details).
18. Maintain vehicular traffic at all times.
19. Work area to be backfilled to grade or plated when site is unattended.
20. Work to be performed as per plans and specifications.
21. Contractors to post signs to indicate: BIKE LANE CLOSED - SHARED LANE YIELD TO BIKES.

Restrictions:

It is also the permit holder's responsibility to restore to original condition any damage to any bikeway, including replacement pavement markings and signage. You must contact Ben Gomberg (312) 744-8093 48 hours in advance of any activity.

22. No work in or use of the public right of way is to be done when a special event is taking place. It is up to the applicant to determine if an event is scheduled. To obtain a listing of programs or events within the City of Chicago please dial 311 when you are within the City boundaries.
23. It is the responsibility of the applicant to fund Traffic Control Aides if the City deems it necessary due to heavy congestion situations.
24. Pursuit to City Ordinances 10-20-150 and 10-28-281.3 a re-inspection fee of $100 may be assessed for each inspection conducted after the initial inspection.
25. All metal plates used for public way construction or placed within the right-of-way must indicate Ownership!

Street Opening (Traffic Lane)

11-05-2012 - Fee Pavement Opening

CBD:	N	Cost Per EA: $	391.00	CAPS:	300-84-2135-256
Tiered:	N	# Of EA:	1.00	Late charge: $	.00
Mora:	N			Amount: $	391.00

Total Fees: $ 391.00

Grand Total Fees: $ 391.00

Affected CUAN Sites: 1, 2, 3, 4, 5, 6, 9, 11, 12, 15, 16, 17, 18, 20, 21, 22, 23, 24, 27, 28, 29, 31, 34, 35, 36, 38, 41, 42, 46, 49, 53, 55, 60, 61, 62, 65, 66, 67, 68, 69, 70, 71, 72, 73, 74, 84, 86, 87, 90, 155, 156

EFFECTIVE DATES OF PERMIT

Current: Nov 05, 2012 through Nov 16, 2012 (Input date: Nov 05, 2012 9:44:51 a.m.)

END OF PERMIT

AECOM

JOB TITLE Integrys - 201 E North Water
JOB NO. 60157647 CALCULATION NO.
ORIGINATOR Joshua Rove DATE 11/9/12
REVIEWER Steve Kornder DATE 11/9/12
SCALE not to scale SHEET NO. 1 OF 1

Meter S/N 172039
cut off 20,356 cpm unshielded

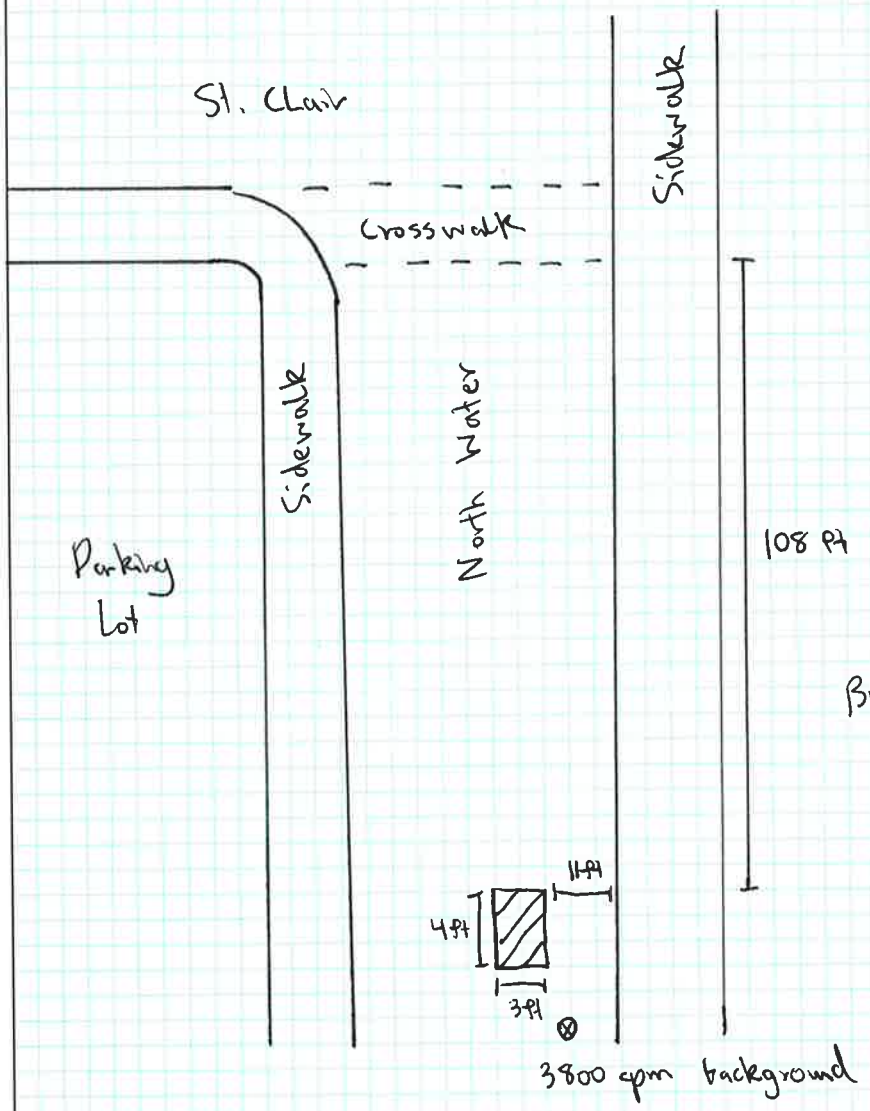

Depth	Counts per Minute
0-12"	asphalt
12-24"	5800
24-42"	6500
42-60"	7100

Grid: 6x6 = 2 cm
