Naval Facilities Engineering Command Southwest
BRAC PMO West
San Diego, CA

DRAFT
FOURTH FIVE-YEAR REVIEW

HUNTERS POINT NAVAL SHIPYARD, SAN FRANCISCO, CA

July 2018

Approved for public release; distribution is unlimited

DCN: IEJV-4804-0000-0006

Naval Facilities Engineering Command Southwest
BRAC PMO West
San Diego, CA

DRAFT
FOURTH FIVE-YEAR REVIEW

HUNTERS POINT NAVAL SHIPYARD, SAN FRANCISCO, CA

July 2018

Prepared for:

Department of the Navy
Naval Facilities Engineering Command Southwest
BRAC PMO West
33000 Nixie Way, Bldg. 50
San Diego, CA 92147

Prepared by:

Innovex-ERRG Joint Venture

Innovex-ERRG Joint Venture
2300 Clayton Road, Suite 1435
Concord, CA94520
(925) 429-5555

Contract Number: N62473-17-C-4804
DCN: IEJV-4804-0000-0006

Draft
Fourth Five-Year Review
Hunters Point Naval Shipyard
San Francisco, California

Submitted by:
Innovex-ERRG Joint Venture

	July 9, 2018
Signature	Date
John Sourial, P.E., C.Q.E.	Project Manager
Name	Title

Executive Summary

This report presents the fourth five-year review conducted under the Comprehensive Environmental Response, Compensation, and Liability Act (CERCLA) at Hunters Point Naval Shipyard (HPNS) in San Francisco, California. The review was conducted in accordance with the "Navy and Marine Corps Policy for Conducting CERCLA Statutory Five-Year Reviews" (Department of the Navy [Navy], 2011b) and the U.S. Environmental Protection Agency's (EPA) "Comprehensive Five-Year Review Guidance" (EPA, 2001), including supplemental documents (EPA, 2011, 2012a, and 2012b) and the "Five-Year Review Recommended Template, OLEM 9200.0-89" (EPA, 2016).

HPNS is a closed military base located in southeastern San Francisco on a peninsula that extends to the east into San Francisco Bay. HPNS currently consists of 846 acres: 403 acres on land and 443 acres under water in the San Francisco Bay. HPNS is currently divided into nine parcels and two independent installation restoration (IR) sites: Parcels B-1, B-2, C, D-1, E, E-2, F, G, and UC-3 and IR-07 and IR-18. HPNS formerly included Parcels A, D-2, UC-1, and UC-2, but they were transferred out of federal ownership to the City and County of San Francisco's Office of Community Investment and Infrastructure, which is the successor agency to the San Francisco Redevelopment Agency.

Records of Decision (RODs) have been completed for all parcels except Parcel F. This fourth five-year review focuses on the parcels (specifically, B-1, B-2, C, D-1, D-2, E, E-2, G, UC-1, UC-2, and UC-3) where remedial actions (RAs) have been completed or are under way, including parcels that transferred out of Navy ownership within the last 5 years, and includes summary status information for all parcels, except former Parcel A. Parcel A is not discussed in this report because the parcel required no action under CERCLA.

This five-year review included interviews of personnel and community members, review of relevant documents and data, site inspections, and development of this Five-Year Review Report. The purpose of this review was to evaluate the performance of remedies that have been implemented at HPNS to verify they remain protective of human health and the environment. This Five-Year Review Report also states whether each remedy is or will be protective, identifies any deficiencies, and recommends actions for improvement if the remedy has not performed, or is not performing, as designed.

This statutory five-year review is required by, and conducted according to, CERCLA Section (§) 121(c) and the National Oil and Hazardous Substances Pollution Contingency Plan at Title 40 Code of Federal Regulations § 300.430(f)(4)(ii) because the selected remedies will not reduce contaminant concentrations to levels allowing for unlimited use and unrestricted exposure, and because RODs were signed after October 17, 1986. The trigger

date for this five-year review is the date of the third five-year review: November 8, 2013 (TriEco-Tetra Tech Sustainable Resources Joint Venture, 2013b).

The following five-year review summary form provides additional information on the results of the review assessment and the effectiveness of the remedies implemented at HPNS.

SITE IDENTIFICATION		
Site Name: Hunters Point Naval Shipyard		
EPA ID: CA1170090087		
Region: 9	**State:** CA	**City/County:** San Francisco/San Francisco
SITE STATUS		
NPL Status: Final		
Multiple OUs? Yes	**Has the site achieved construction completion?** No	
REVIEW STATUS		
Lead agency: Other Federal Agency ***[If "Other Federal Agency", enter Agency name]*:** Department of the Navy		
Author name (Federal or State Project Manager): John Sourial		
Author affiliation: Innovex-ERRG Joint Venture		
Review period: 11/1/2013 - 11/30/2018		
Date of site inspection: 1/29/2018		
Type of review: Statutory		
Review number: 4		
Triggering action date: 11/8/2013		
Due date *(five years after triggering action date)*: 11/8/2018		

Table of Contents

EXECUTIVE SUMMARY ES-1

SECTION 1. INTRODUCTION 1-1

SECTION 2. SITE BACKGROUND 2-1

2.1. Location and Physical Characteristics 2-1

2.2. Geography 2-2

2.3. Topography 2-2

2.4. Hydrostratigraphy 2-3

2.5. Land and Resource Use 2-4

2.5.1. Past and Present Land Uses 2-4

2.5.2. Future Land Uses 2-5

2.5.3. Surface Water and Groundwater Use 2-5

SECTION 3. RESPONSE ACTION SUMMARY 3-1

3.1. Basis for Taking Action 3-1

3.2. Response Actions 3-1

3.2.1. Pre-ROD Activities and Remedy Selection at Parcel B (IR-07/18 and Parcels B-1 and B-2) 3-3

3.2.2. Pre-ROD Activities and Remedy Selection at Parcel C (Parcels C and UC-2) 3-3

3.2.3. Pre-ROD Activities and Remedy Selection at Parcel D (Parcels D-1, D-2, G, and UC-1) 3-4

3.2.4. Pre-ROD Activities and Remedy Selection at Parcel E (Parcels E, E-2, and UC-3) 3-5

3.2.5. Pre-ROD Activities and Remedy Selection at Parcel F 3-6

3.3. Status of Implementation 3-6

3.3.1. IR-07/18 3-6

3.3.1.1. RA Activities and Implementation of ICs 3-6

3.3.1.2. LTM and Maintenance Activities 3-8

3.3.2. Parcels B-1 and B-2 3-10

3.3.2.1. RA Activities and Implementation of ICs 3-10

3.3.2.2. LTM and Maintenance Activities 3-12

3.3.3. Parcel C 3-15

3.3.3.1. RA Activities and Implementation of ICs 3-15

3.3.3.2. LTM and Maintenance Activities 3-18

3.3.4. Parcel D-1 3-19

3.3.4.1. RA Activities and Implementation of ICs 3-19

3.3.4.2. LTM and Maintenance Activities 3-21

Table of Contents *(continued)*

3.3.5. Parcel D-2 3-22
3.3.5.1. RA Activities and Implementation of ICs 3-22
3.3.5.2. LTM and Maintenance Activities 3-22
3.3.6. Parcel E 3-22
3.3.6.1. RA Activities and Implementation of ICs 3-22
3.3.6.2. LTM and Maintenance Activities 3-25
3.3.7. Parcel E-2 3-26
3.3.7.1. RA Activities and Implementation of ICs 3-26
3.3.7.2. LTM and Maintenance Activities 3-28
3.3.8. Parcel F 3-30
3.3.9. Parcel G 3-30
3.3.9.1. RA Activities and Implementation of ICs 3-30
3.3.9.2. LTM and Maintenance Activities 3-32
3.3.10. Parcels UC-1 and UC-2 3-34
3.3.10.1. RA Activities and Implementation of ICs 3-34
3.3.10.2. LTM and Maintenance Activities 3-35
3.3.11. Parcel UC-3 3-36
3.3.11.1. RA Activities and Implementation of ICs 3-36
3.3.11.2. LTM and Maintenance Activities 3-38

SECTION 4. PROGRESS SINCE LAST REVIEW 4-1
4.1. IR-07/18 4-1
4.2. Parcels B-1 and B-2 4-1
4.3. Parcel C 4-2
4.4. Parcel D-1 4-3
4.5. Parcel D-2 4-3
4.6. Parcel G 4-3
4.7. Parcel UC-1 4-4
4.8. Parcel UC-2 4-4

SECTION 5. FIVE-YEAR REVIEW PROCESS 5-1
5.1. Community Notification, Involvement, and Site Interviews 5-1
5.2. Document and Data Review 5-2
5.3. Site Inspections 5-3

SECTION 6. TECHNICAL ASSESSMENT 6-1
6.1. Question A 6-1
6.1.1. Excavation and Offsite Disposal of Soil Hot Spots 6-2
6.1.2. Durable Covers 6-3
6.1.3. SVE 6-4

Table of Contents *(continued)*

6.1.4. In-Situ Groundwater Treatment 6-5
6.1.5. MNA and LTM of Groundwater 6-6
6.1.6. Radiological Surveys and Remediation 6-6
6.2. Question B 6-8
6.2.1. Changes in Standards and TBC Criteria 6-9
6.2.2. Changes in Toxicity and Other Contaminant Characteristics 6-9
6.2.3. Changes in Risk Assessment Methods 6-11
6.2.4. Changes in Exposure Pathways 6-13
6.2.5. Expected Progress Toward Meeting RAOs 6-14
6.3. Question C 6-15

SECTION 7. ISSUES, RECOMMENDATIONS, AND OTHER FINDINGS 7-1

SECTION 8. PROTECTIVENESS STATEMENT 8-1
8.1. IR-07/18 8-1
8.2. Parcel B-1 8-1
8.3. Parcel B-2 8-1
8.4. Parcel C 8-2
8.5. Parcel D-1 8-2
8.6. Parcel D-2 8-3
8.7. Parcel G 8-3
8.8. Parcel UC-1 8-3
8.9. Parcel UC-2 8-3
8.10. Parcel UC-3 8-4

SECTION 9. NEXT REVIEW 9-1

List of Figures

Figure 1. Parcel Map
Figure 2. Installation Restoration Sites
Figure 3. Overview of Remedy Components for IR-07/18
Figure 4. Overview of Remedy Components for Parcel B-1
Figure 5. Overview of Remedy Components for Parcel B-2
Figure 6. Overview of Remedy Components for Parcel C
Figure 7. Overview of Remedy Components for Parcel D-1
Figure 8. Overview of Remedy Components for Parcel E
Figure 9. Overview of Remedy Components for Parcel E-2
Figure 10. Overview of Remedy Components for Parcel G
Figure 11. Overview of Remedy Components for Parcel UC-1
Figure 12. Overview of Remedy Components for Parcel UC-2
Figure 13. Overview of Remedy Components for Parcel UC-3

List of Tables

Table 1. Chemicals of Concern and Contaminated Media
Table 2. Pre-ROD Response Actions for Parcel B (i.e., IR-07/18 and Parcels B-1 and B-2)
Table 3. Remedial Action Objectives and Remedy Components for Parcel B (i.e., IR-07/18 and Parcels B-1 and B-2)
Table 4. Pre-ROD Response Actions for Parcel C (i.e., Parcels C and UC-2)
Table 5. Remedial Action Objectives and Remedy Components for Parcel C
Table 6. Remedial Action Objectives and Remedy Components for Parcel UC-2
Table 7. Pre-ROD Response Actions for Parcel D (i.e., Parcels D-1, D-2, G, and UC-1
Table 8. Remedial Action Objectives and Remedy Components for Parcels D-1 and UC-1
Table 9. Remedial Action Objectives and Remedy Components for Parcel G
Table 10. Pre-ROD Response Actions for Parcel E (i.e., Parcels E, E-2, and UC-3)
Table 11. Remedial Action Objectives and Remedy Components for Parcel E
Table 12. Remedial Action Objectives and Remedy Components for Parcel E-2
Table 13. Remedial Action Objectives and Remedy Components for Parcel UC-3
Table 14. Pre-ROD Response Actions for Parcel F
Table 15. Soil Cleanup Levels
Table 16. Groundwater Cleanup Levels

List of Appendices

Appendix A. List of References and Documents Reviewed
Appendix B. Interview and Survey Records
Appendix C. Site Inspection Checklists and Photographic Logs

Abbreviations and Acronyms

Alliance	The Alliance Compliance Group Joint Venture
Amec Foster Wheeler	Amec Foster Wheeler Environment & Infrastructure, Inc.
APTIM	APTIM Federal Services, LLC
ARARs	applicable or relevant and appropriate requirements
ARCADIS	ARCADIS U.S., Inc.
ARICs	areas requiring institutional controls
AST	aboveground storage tank
BCT	BRAC Cleanup Team
BGMP	Basewide Groundwater Monitoring Program
bgs	below ground surface
BRAC	Base Realignment and Closure
CalEPA	California Environmental Protection Agency
CDPH	California Department of Public Health
CERCLA	Comprehensive Environmental Response, Compensation, and Liability Act
CES	Construction Engineering Services, LLC
COCs	chemical of concern
COECs	chemicals of ecological concern
CRUPs	covenants to restrict the use of the property
CVOCs	chlorinated volatile organic compounds
DTSC	Department of Toxic Substances Control
DTSC-SLs	DTSC-modified screening levels
EPA	U.S. Environmental Protection Agency
ERRG	Engineering/Remediation Resources Group, Inc.
ESD	Explanation of Significant Differences
FFA	Federal Facility Agreement
FS	feasibility study
FSC	federal screening criterion
HHRAs	human health risk assessments
HI	hazard index
HQ	hazard quotient
HPAL	Hunters Point ambient level
HPNS	Hunters Point Naval Shipyard

ICs	institutional controls
IR	Installation Restoration
ISB	in-situ bioremediation
IEJV	Innovex-ERRG Joint Venture
ITSI	Innovative Technical Solutions, Inc.
JEM	Johnson and Ettinger model
JV	Joint Venture
KCH	CH2M HILL Kleinfelder, A Joint Venture
LLRW	low-level radioactive waste
LOQs	limits of quantitation
LTM	long-term monitoring
LUC	land use control
MARSSIM	Multi-Agency Radiation Survey and Site Investigation Manual
MCLs	maximum contaminant levels
MCP	Monitoring and Control Plan
MNA	monitored natural attenuation
msl	mean sea level
NAPL	nonaqueous-phase liquids
NAVSEA	Naval Sea Systems Command
Navy	Department of the Navy
NCP	National Oil and Hazardous Substances Pollution Contingency Plan
ng/L	nanograms per liter
NMOCs	nonmethane organic compounds
NRDL	Naval Radiological Defense Laboratory
OCII	Office of Community Investment and Infrastructure
O&M	operation and maintenance
PAHs	polycyclic aromatic hydrocarbons
PCBs	polychlorinated biphenyls
PCE	tetrachloroethene
PFAS	per- and polyfluoroalkyl substances
PFOA	perfluorooctanoic acid
PFBS	perfluorobutane sulfonate
PFOS	perfluorooctane sulfonate
PQL	practical quantitation limit
PRC	PRC Environmental Management, Inc.
PRGs	preliminary remediation goals

RAs	remedial actions
RAOs	remedial action objectives
RACR	Remedial Action Completion Report
RAWP	Remedial Action Work Plan
RBC	risk-based concentration
RCPs	representative concentration pathways
RD	Remedial Design
RGs	remediation goals
RIs	remedial investigations
RODs	Records of Decision
RSL	Regional Screening Level
RU	Remedial Unit
SES	Sealaska Environmental Services, LLC
SFRA	San Francisco Redevelopment Agency
SGALs	soil gas action levels
SVE	soil vapor extraction
SVOCs	semivolatile organic compounds
SWRCB	State Water Resources Control Board
TBC	to be considered
TCE	trichloroethene
TCRA	time-critical removal action
TLs	trigger levels
TtEC	Tetra Tech EC, Inc.
TtEMI	Tetra Tech EM Inc.
TriEco-Tt	TriEco-Tetra Tech Sustainable Resources Joint Venture
Triple A	Triple A Machine Shop, Inc.
TPH	total petroleum hydrocarbons
UST	underground storage tank
VC	vinyl chloride
VISLs	Vapor Intrusion Screening Levels
VOCs	volatile organic compounds
Water Board	San Francisco Bay Regional Water Quality Control Board
ZVI	zero-valent iron
µg/L	micrograms per liter
§	Section

Section 1. Introduction

This report documents the results of the fourth five-year review conducted for Hunters Point Naval Shipyard (HPNS) in San Francisco, California. The purpose of the fourth five-year review is to provide an update on the status of remedial actions (RAs) and post-RA activities implemented since the third five-year review, evaluate whether these RAs and post-RA activities are protective of human health and the environment, and assess the progress toward meeting the recommendations made in the third five-year review. This fourth five-year review report also identifies issues found during this fourth five-year review and recommendations to address them. The five-year review applies to all RAs selected pursuant to the Comprehensive Environmental Response, Compensation, and Liability Act (CERCLA) Section (§) 121(c) and the National Oil and Hazardous Substances Pollution Contingency Plan (NCP). CERCLA § 121(c) states:

> *"If the President selects a remedial action that results in any hazardous substances, pollutants, or contaminants remaining at the site, the President shall review such remedial action no less often than each five years after the initiation of such remedial action to assure that human health and the environment are being protected by the remedial action being implemented. In addition, if upon such review it is the judgment of the President that action is appropriate at such site in accordance with section [104] or [106], the President shall take or require such action. The President shall report to the Congress a list of facilities for which such review is required, the results of all such reviews, and any actions taken as a result of such reviews."*

This requirement is further interpreted in the NCP [Title 40 Code of Federal Regulations § 300.430(f)(4)(ii)], which states:

> *"If a remedial action is selected that results in hazardous substances, pollutants, or contaminants remaining at the site above levels that allow for unlimited use and unrestricted exposure, the lead agency shall review such action no less often than every five years after the initiation of the selected remedial action."*

Consistent with Executive Order 12580, the Secretary of Defense is responsible for ensuring that five-year reviews are conducted at all qualifying U.S. Department of Defense cleanup sites. The Department of the Navy (Navy) is authorized to conduct the five-year review for HPNS in accordance with CERCLA § 121 and the NCP.

This fourth five-year review was conducted for all parcels at HPNS (except Parcel A), and summarizes the significant work conducted by the Navy in collaboration with the regulatory agencies, including the U.S.

Environmental Protection Agency (EPA), the Department of Toxic Substances Control (DTSC), and the San Francisco Bay Regional Water Quality Control Board (Water Board). This five-year review focuses on parcels (specifically, B-1, B-2, C, D-1, D-2, E, E-2, G, UC-1, UC-2, and UC-3) where RAs have been completed or are under way, including parcels that transferred out of Navy ownership within the last 5 years, and includes summary status information for all parcels, except former Parcel A. Parcel A is not discussed in this report because the parcel required no action under CERCLA.

This review is triggered by the date of the third five-year review: November 8, 2013 (TriEco-Tetra Tech Sustainable Resources Joint Venture [TriEco-Tt], 2013). The review was conducted from December 2017 through November 2018.

Five-year reviews are required for HPNS because (1) ongoing and completed RAs have left contaminants in place above concentrations that would allow for unlimited use and unrestricted exposure and (2) the Records of Decision (RODs) were signed on or after October 17, 1986 (the effective date of the Superfund Amendments and Reauthorization Act). This five-year review was conducted in accordance with the following guidance documents:

- "Navy/Marine Corps Policy for Conducting Comprehensive Environmental Response, Compensation, and Liability Act Statutory Five-Year Reviews" (Navy, 2011b)
- "Comprehensive Five-Year Review Guidance" (EPA, 2001)
- "Five-Year Review Recommended Template, OLEM 9200.0-89" (EPA, 2016)
- "Recommended Evaluation of Institutional Controls: Supplement to the 'Comprehensive Five-Year Review Guidance,' OSWER Directive 9355.7-18" (EPA, 2011)
- "Memorandum: Clarifying the Use of Protectiveness Determinations for Comprehensive Environmental Response, Compensation, and Liability Act Five-Year Reviews" (EPA, 2012a)
- "Assessing Protectiveness at Sites for Vapor Intrusion, Supplement to the 'Comprehensive Five-Year Review Guidance,' OSWER Directive 9200.2-84" (EPA, 2012b)

Following this introduction, this five-year review report is organized in the following sections:

- Section 2, Site Background, describes background information for HPNS, including location and physical characteristics, geography, topography, hydrostratigraphy, and land and resource use
- Section 3, Response Action Summary, describes the basis for taking action, response actions taken before the RODs, and the status of implementation of RAs in each parcel
- Section 4, Progress Since Last Five-Year Review, summarizes actions since the 2013 five-year review
- Section 5, Five-Year Review Process, describes the components of the five-year review process, including community notification, involvement, and site interviews; document and data review; and site inspections

- Section 6, Technical Assessment, presents the analysis of whether the remedies are functioning as intended; whether the standards and to be considered (TBC) criteria, toxicity data, risk assessment methodology, and exposure assumptions are still valid, as well as whether the remedy is progressing as expected; and whether any other information has come to light that could call into question the protectiveness of the remedies
- Section 7, Issues, Recommendations, and Other Findings, presents issues and provides recommended actions based on the technical assessment
- Section 8, Protectiveness Statements, lists the protectiveness statement for each parcel
- Section 9, Next Review, provides the schedule for the next five-year review

Figures and tables are presented after Section 9. Appendices containing supporting information are presented after the figures and tables. Appendix A contains the list of references cited in this report and the documents that were reviewed in support of this five-year review. Appendix B contains the regulatory agency interview and community member survey records. Appendix C contains the checklists and photographic logs documenting the observations made during the site inspections.

Section 2. Site Background

This section provides background information on HPNS. General site conditions are discussed, including location and physical characteristics, geography, topography, hydrostratigraphy, and land and resource use. All background information summarized in this section is from the Third Five-Year Review Report (TriEco-Tt, 2013), unless otherwise noted.

2.1. LOCATION AND PHYSICAL CHARACTERISTICS

HPNS is located in the City and County of San Francisco, California (Figure 1). HPNS encompasses 846 acres (403 acres on land and 443 acres under water in San Francisco Bay) in southeastern San Francisco on a peninsula that extends east into San Francisco Bay (Figure 1). HPNS is currently divided into nine parcels and two independent Installation Restoration (IR) sites: Parcels B-1, B-2, C, D-1, E, E-2, F, G, and UC-3 and IR-07 and IR-18 (Figure 2). HPNS formerly included Parcels A, D-2, UC-1, and UC-2, but they have been transferred out of federal ownership to the City and County of San Francisco's Office of Community Investment and Infrastructure (OCII), which is the successor agency to the San Francisco Redevelopment Agency (SFRA). The approximate area of each parcel and IR site is listed below.

Parcel or IR Site (Navy Property)	Approximate Area (acres)
B-1	27
B-2 (including IR-07 and IR-18)	27
C	74
D-1	49
E	126
E-2	47
F	443
G	40
UC-3	12
Former Parcel (Non-Navy Property)	**Approximate Area (acres)**
A	75
D-2	6.04
UC-1	4
UC-2	4

2.2. GEOGRAPHY

In 1992, the Navy divided HPNS into five contiguous parcels (Parcels A through E). In 1996, the Navy added a sixth parcel (Parcel F), which encompasses immediately adjacent areas of San Francisco Bay; Parcel F is referred to as the "offshore area." In 2004, the Navy divided Parcel E into two parcels (E and E-2) to facilitate closure of the Parcel E-2 landfill and its adjacent areas and transferred Parcel A to the OCII. In 2008, the Navy subdivided Parcel D into four separate parcels (D-1, D-2, G, and UC-1) and separated the western edge of Parcel C to create Parcel UC-2; these changes were made to expedite closure and transfer of the new parcels. In 2008, the Navy also separated the IR-07 and IR-18 (hereinafter referred to as "IR-07/18") from the rest of Parcel B to expedite the remedy completion and transfer of these sites. In 2012, the Navy separated the Crisp Road roadway and adjacent areas of Parcel E to create Parcel UC-3. The UC-series parcels encompass mostly roadways and were created to facilitate the overall transfer and development of HPNS. In 2013, following the issuance of the third five-year review report, the Navy subdivided Parcel B, excluding IR-07/18, into two separate parcels (B-1 and B-2) to accommodate varying property transfer schedules for different portions of the original parcel (Engineering/Remediation Resources Group, Inc. [ERRG], 2017). In 2015, the Navy transferred Parcels D-2, UC-1, and UC-2 to the OCII.

At each HPNS parcel, contaminated sites were designated as IR sites based on information developed during previous investigations. IR sites were in most cases identified by a two-digit number (e.g., IR-02). Site characterization activities and sampling data were mostly planned and organized by IR site. Figure 2 shows the locations of the IR sites across HPNS.

2.3. TOPOGRAPHY

The topography of HPNS is characterized by a central hill (former Parcel A) and surrounding areas extending radially out to San Francisco Bay. At the current parcels, ground surface elevations range from about 30 to 60 feet above mean sea level (msl) near their landward edges and slope down to 0 feet above msl as they meet the bay. Large areas of HPNS are flat lowlands with elevations of about 10 to 15 feet above msl, where most of the base roads, buildings, and operating areas were built. The Navy created most of the dry land portion of HPNS in the 1940s by excavating the hills surrounding the shipyard and using the resulting spoils to expand the shoreline into San Francisco Bay. Some additional shoreline filling operations continued into the 1960s.

Most of the shoreline at HPNS is constructed seawalls or dry docks. The shorelines at all of IR-07 and portions of Parcels B-1 and B-2 are covered by shoreline protection materials consisting of engineered riprap (ERRG, 2012a and 2017; Innovex-ERRG Joint Venture [IEJV], 2018a). The shorelines at most of Parcel E and all of Parcel E-2 are either unimproved or partially to completely covered by shoreline protection materials consisting of irregularly placed concrete rubble and debris. Most upland areas are paved or covered by buildings, and the remaining unpaved areas support a ruderal habitat characterized by scattered to moderately dense growths of grasses and shrubs. Small wetland areas exist in intertidal areas

at Parcels E and E-2 (Navy, 2013d and 2012, respectively). The Remedial Action Completion Reports (RACRs) for IR-07/18 and Parcels B-1, B-2, C, and G and the RODs for Parcels D-1, E, and E-2 (see Appendix A) further describe the current topography of these parcels.

Shoreline and offshore areas at HPNS are considered environmentally sensitive areas, and effects to wildlife in environmentally sensitive areas were considered during the remedy selection and design process. Specifically, the selected remedies at Parcels B, E, and E-2 involve varying degrees of excavation of contaminated sediment to protect human health and the environment that require minor filling of onsite wetlands, the loss of which would be mitigated by the Navy (on site at Parcel E-2). The Final Remedial Design (RD) Package for Parcel E-2 (ERRG, 2014f) details the Navy's wetlands mitigation approach at HPNS.

2.4. HYDROSTRATIGRAPHY

The hydrostratigraphic units at HPNS include (1) the A-aquifer, (2) the B-aquifer, and (3) the bedrock water-bearing zone. An aquitard composed of Bay Mud separates the A-aquifer from the B-aquifer across most of HPNS. The hydrostratigraphic units at HPNS are generally described below.

The A-aquifer primarily consists of heterogeneous Artificial Fill but may, in select areas of HPNS, also include the following underlying layers: (1) Undifferentiated Upper Sands; (2) sandy units within the uppermost Bay Mud; and (3) the upper weathered bedrock zone. The A-aquifer covers most of HPNS and ranges in thickness from a few feet to more than 50 feet. The A-aquifer is generally unconfined throughout most of HPNS, but semi-confined conditions may exist in places where fine-grained sediments below the water table overlie more permeable materials. Depths to groundwater range from about 5 to 20 feet below ground surface (bgs), with an average depth to groundwater of approximately 10 feet bgs.

Bay Mud acts as an aquitard that typically separates the A-aquifer from the underlying B aquifer. The Bay Mud deposits consist of highly plastic clay to sandy clay and generally thicken from 0 feet near the historical shoreline to more than 50 feet thick near the bay margin. The Bay Mud aquitard is absent in several locations across HPNS and in areas of bedrock highs.

The B-aquifer consists of Undifferentiated Sediments, in a sequence of relatively thick (about 30 to 40 feet), laterally continuous layers of sand and silty and clayey sand, which are separated by laterally continuous layers of silt and clay. Layers of silts and clay overlie the lower portions of the B-aquifer; therefore, it is less likely to be affected by contamination from site activities. The uppermost B-aquifer generally corresponds to the upper 20- to 40-foot-thick layer of sand and silty sand of Undifferentiated Sedimentary deposits. The B-aquifer is generally confined by the Bay Mud aquitard, which separates it from the A-aquifer across most of HPNS. In areas where the aquitard is absent, the A- and B-aquifers are in hydraulic communication and behave as a single aquifer.

Deeper portions of saturated fractured bedrock that are not in direct contact with the A- or B aquifers are hydrostratigraphically classified as the bedrock water-bearing zone. The fractured, unweathered bedrock is not considered an aquifer because of its limited flow capability and low storage capacity.

Primary sources of recharge for the A-aquifer are infiltration of precipitation and runoff, intrusion of bay water, horizontal flow of groundwater from upgradient areas, and vertical flow of water from the B-aquifer. The primary sources of recharge for the B-aquifer include infiltration of precipitation and runoff and horizontal groundwater flow from upgradient areas. The bedrock water-bearing zone likely discharges into the B-aquifer at upgradient contacts and is recharged by infiltration of precipitation at landward outcrop areas.

2.5. LAND AND RESOURCE USE

This section discusses land and resource use at HPNS, including past and present land uses, anticipated future land uses, and surface water and groundwater use.

2.5.1. Past and Present Land Uses

Bethlehem Steel owned and operated HPNS as a commercial dry dock facility until 1939, when the Navy purchased the property. Quays, docks, and support buildings were built on an expedited wartime schedule to support the shipyard's mission of fleet repair and maintenance. After the end of World War II, the Navy used the berthing facilities at HPNS for ships returning from the Pacific. By 1951, HPNS shifted from operating as a general repair facility to specializing in submarine maintenance and repair. However, the Navy continued to operate Pacific Fleet carrier overhaul and ship maintenance repair facilities at HPNS through the 1960s. In addition to shipyard operations, the Naval Radiological Defense Laboratory (NRDL) occupied buildings at HPNS during the 1950s and 1960s to conduct practical and applied research on radiation decontamination methods and on the effects of radiation on living organisms and natural and synthetic materials. The NRDL ceased operations in 1969. Use of HPNS began to decline steadily in the late 1960s and early 1970s, and HPNS was disestablished as an active Naval facility in 1974 (Naval Sea Systems Command [NAVSEA], 2004).

In 1976, the Navy leased 98 percent of HPNS to a private ship repair company, Triple A Machine Shop, Inc. (Triple A). Triple A leased the property from July 1, 1976, to June 30, 1986. During the lease period, Triple A used dry docks, berths, machine shops, power plants, various offices, and warehouses to repair commercial and Navy vessels. Triple A also subleased portions of the property to various other businesses. In 1986, the Navy resumed occupancy of HPNS. Many of the subtenants under Triple A's lease remained tenants under the Navy's reoccupancy in 1986. Triple A vacated the property in March 1987. Only a few tenants remain at HPNS, primarily the San Francisco Police Department (in Parcel E) and an artist colony (in Parcel B-1).

Various industrial activities at HPNS, including shipbuilding and repair, metal working, degreasing, painting, foundry operations, radiological research, and other industrial operations, have resulted in a broad distribution of chemicals in soil, soil gas, sediment, groundwater, and structures. These chemicals include metals, volatile organic compounds (VOCs), semivolatile organic compounds (SVOCs) (including polycyclic aromatic hydrocarbons [PAHs]), pesticides, polychlorinated biphenyls (PCBs), total petroleum hydrocarbons (TPH), and radionuclides.

2.5.2. Future Land Uses

The anticipated future use of HPNS is described in the City and County of San Francisco's 2010 HPNS Redevelopment Plan (SFRA, 2010). The redevelopment plan delineates "land use districts" in the subdivision of HPNS and describes the allowable uses within each land use district. The principal uses within the various land use districts include residential; institutional; retail sales and services; office and industrial; multi-media and digital arts; athletic and recreational facilities; civic, arts, and entertainment; and parks and recreation and other open space uses (SFRA, 2010).

2.5.3. Surface Water and Groundwater Use

No permanent surface water features exist at HPNS. Surface water runoff flows to nearby San Francisco Bay or infiltrates into the ground. Groundwater beneath HPNS is not currently used for drinking water, irrigation, or industrial supply. The City and County of San Francisco supplies drinking water to HPNS through its municipal supply from the Hetch Hetchy watershed in the Sierra Nevada.

On September 25, 2003, Water Board staff concurred with the Navy that A-aquifer groundwater at HPNS meets the exception criteria in the State Water Resources Control Board (SWRCB) Resolution No. 88-63, "Sources of Drinking Water"[1]; therefore, groundwater in the A-aquifer is not suitable as a potential source of drinking water. Likewise, on July 29, 2008, Water Board staff concurred with the Navy that B-aquifer groundwater in the central and southern area of Parcel C at HPNS meets the exception criteria in SWRCB Resolution No. 88-63, "Sources of Drinking Water"; therefore, groundwater in the B-aquifer at those locations is not suitable as a potential source of drinking water.

Similar to the evaluation for SWRCB Resolution No. 88-63, the Navy concluded that maximum contaminant levels (MCLs) were not applicable or relevant and appropriate requirements (ARARs) for CERCLA cleanups at HPNS based on an evaluation of site-specific factors. Results of the evaluation of site-specific factors showed that:

- there is no historical or current use of groundwater as a water supply;
- the City and County of San Francisco will not allow the use of groundwater for drinking water because the city prohibits installation of domestic wells within city boundaries;

[1] https://www.waterboards.ca.gov/board_decisions/adopted_orders/resolutions/1988/rs1988_0063.pdf

- arsenic and other metals occur in A-aquifer groundwater at ambient levels that exceed MCLs, and the cost to reduce concentrations of these chemicals below MCLs would likely be prohibitive and it may be technically impracticable to do so; and
- the proximity of saline groundwater and surface water from San Francisco Bay creates a high potential for saltwater intrusion if significant quantities are produced from the aquifer.

Future drinking water is expected to continue to be supplied by the city's municipal system. The RODs for the various parcels that require RAs all require institutional controls (ICs) to prohibit the use of groundwater; and, consequently, future use of groundwater is expected to be prohibited, except for uses allowed by the RODs (e.g., maintenance of groundwater monitoring wells).

Section 3. Response Action Summary

This section provides the framework for the response actions that have been undertaken at HPNS. This section discusses the basis for taking action, summarizes the initial (pre-ROD) response actions that have occurred and the remedial action objectives (RAOs) and components of the selected remedy for each parcel, and describes the implementation status of the selected remedy for each parcel.

3.1. BASIS FOR TAKING ACTION

Chemicals of concern (COCs) in soil, sediment, soil gas, and groundwater pose potentially unacceptable risk to human health and the environment at HPNS. Human health risk assessments (HHRAs) for the major parcels (i.e., B through F) evaluated exposures to industrial and construction workers, as well as potential future residents and recreational users. Table 1 lists the COCs in contaminated media for each HPNS parcel (i.e., B through F) that have been found to pose a risk for carcinogens greater than 10^{-6} or for noncarcinogens with a hazard index (HI) greater than 1. Note that the COCs listed in Table 1 were found to pose risks at the time of publication of the remedial investigations (RIs) for each parcel (including IR-07/18), but may no longer pose risks following the various response actions.

Significant exposure pathways that resulted in the highest levels of risk to human health include exposure to metals and organic chemicals (especially PAHs and PCBs) in soil and exposure to VOCs in soil gas (from either soil or groundwater) via vapor intrusion into indoor air. Exposure to radionuclides in soil or structures via direct radiation or windblown dust and exposure to VOCs in groundwater if used for domestic use also resulted in potentially unacceptable risks. Exposure to metals, PAHs, PCBs, and pesticides in shoreline sediment resulted in the highest levels of risk to ecological receptors.

3.2. RESPONSE ACTIONS

The following is a chronology of the initial response actions that led up to the initiation of the CERCLA process at HPNS:

- Between 1946 and 1948, the Radiological Safety Section and NRDL decontaminated and surveyed Operation Crossroads ships and HPNS berths and dry docks.
- In 1955, the NRDL surveys to decommission NRDL buildings.
- In 1969, NRDL conducted a survey for disestablishment of the NRDL.
- Between 1984 and 1988, the Navy conducted multiple basewide investigations, including the initial assessment study, the confirmation study, and the Triple A investigation, to identify potential sources of contamination at HPNS.

- In January 1988, the predecessor to the DTSC (i.e., the Department of Health Services), issued a Remedial Action Order to the Navy and Triple A describing the storage and disposal of hazardous substances at HPNS and requiring them to prepare a scoping document, an RI and Feasibility Study (FS) Work Plan, and a Remedial Action Plan, and to implement the Remedial Action Plan. The order listed the 11 sites identified during the confirmation study, 19 Triple A sites, and a PCB spill area.
- In 1989, EPA placed HPNS on the National Priorities List, making it a Superfund site under CERCLA (as amended by the Superfund Amendments and Reauthorization Act).
- In 1990, the Navy conducted a basewide inventory for HPNS sites that had not been adequately assessed by previous investigations, including buildings, utility lines, equipment that contained PCBs, and other sites determined to be potentially contaminated. Forty sites were recommended for site inspections.
- In 1991, the U.S. Department of Defense listed HPNS for closure. Following remediation, the property was to be transferred to the City and County of San Francisco.
- Between 1987 and 1991, the Navy conducted two basewide air quality investigations to evaluate air quality at HPNS. The first study was a component of a risk assessment for a proposed housing area in Parcel A. The second study was focused on the IR sites defined as of 1991.
- In 1992, the Navy, EPA, and the California Environmental Protection Agency (CalEPA) signed a Federal Facility Agreement (FFA). In the FFA, the 11 sites proposed for characterization during the confirmation study were reclassified within the RI/FS framework of CERCLA into Operable Units, because the Navy's intent was to maintain HPNS as an active facility. The focus of the FFA was subsequently changed to expedite transfer and public reuse of HPNS, so the Navy and regulatory agencies divided HPNS into geographic parcels (A through E).

Several basewide response actions were started prior to the definition of the parcels in 1992, but completed after that time, as listed below.

- Phase II and Phase III Radiological Investigations: Between 1993 and 1997, the Navy conducted radiation surveys for soil, buildings, and structures across HPNS. These investigations provided recommendations for remediation that were considered during development of the RIs.
- Underground Storage Tank (UST) and Aboveground Storage Tank (AST) Closures: Between 1991 and 1993, the Navy removed or closed in place nearly 50 USTs and nearly 100 ASTs from across HPNS.
- Sandblast Grit Fixation: Between 1991 and 1995, the Navy collected nearly 5,000 tons of sandblast grit from multiple areas at HPNS. The material was sent to an asphalt plant for reuse in an asphalt mix.

Findings from these initial response actions were incorporated, as appropriate, into additional investigations and studies in each major parcel.

The remainder of this section briefly summarizes the primary pre-ROD activities for each of the major parcels (i.e., B through F) at HPNS. Parcel A is not discussed in this report because the parcel required no action under CERCLA.

3.2.1. Pre-ROD Activities and Remedy Selection at Parcel B (IR-07/18 and Parcels B-1 and B-2)

Activities associated with known or potential contaminant releases at Parcel B (which was later subdivided into IR-07/18 and Parcels B-1 and B-2) were identified, and environmental investigations were conducted to identify and assess the nature and extent of contaminants in the following media of concern: (1) soil, shoreline sediment, and soil gas; (2) groundwater; and (3) radiologically impacted media (i.e., soil and above ground and underground structures). Table 2 summarizes the pre-ROD response actions. The pre-ROD investigations and evaluations provided information to evaluate site risks, identify remediation goals (RGs), develop and evaluate remedial alternatives, and support the remedy selected in the original and amended RODs for Parcel B (Navy, 1997 and Navy 2009a).

The original ROD for Parcel B was amended and finalized in 2009 to address shortcomings in the original selected remedy recognized during implementation (Navy, 2009a). Amended RAOs were established to allow selection of a remedy that protects human health and the environment and is consistent with anticipated future land use. The selected remedy consists of actions to remove or treat significant amounts of contamination and actions to contain the remaining contamination and prevent contact through future monitoring, maintenance, and implementation of ICs. Table 3 summarizes the RAOs, as presented in the Amended ROD, and identifies the components of the selected remedy that address the RAOs.

3.2.2. Pre-ROD Activities and Remedy Selection at Parcel C (Parcels C and UC-2)

Activities associated with known or potential contaminant releases at Parcel C (which was later subdivided into Parcels C and UC-2) were identified, and environmental investigations were conducted to identify and assess the nature and extent of contaminants in the following media of concern at Parcel C: (1) soil, (2) soil gas, (3) groundwater, and (4) radiologically impacted media. Table 4 summarizes the pre-ROD response actions. Parcel C was subdivided into Parcels C and UC-2 in 2009, prior to the issuance of any RODs. As a result, there are multiple RODs to address the two parcels subdivided from the original Parcel C. The pre-ROD investigations and evaluations provided sufficient information to evaluate site risks, identify RGs, develop and evaluate remedial alternatives, and support the remedy selected in the RODs for Parcels C and UC-2 (Navy, 2009d and 2010b).

The ROD for Parcel C was finalized in September 2010 (Navy, 2010b). The selected remedy consists of actions to remove or treat significant amounts of contamination and actions to contain the remaining contamination and prevent contact through future monitoring, maintenance, and implementation of ICs. Table 5 summarizes the RAOs, as presented in the ROD, and identifies the components of the selected remedy that address the RAOs. In October 2014, the Navy prepared an Explanation of Significant

Differences (ESD) to the Final ROD to document changes to the approach for defining the extents of soil to be excavated from Parcel C (Navy, 2014b).

The ROD for Parcel UC-2 was finalized in October 2009 (Navy, 2009d). The selected remedy consists of actions to remove significant amounts of contamination and actions to contain the remaining contamination and prevent contact through future monitoring, maintenance, and implementation of ICs. Table 6 summarizes the RAOs, as presented in the ROD, and identifies the components of the selected remedy that will address the RAOs.

3.2.3. Pre-ROD Activities and Remedy Selection at Parcel D (Parcels D-1, D-2, G, and UC-1)

Activities associated with known or potential contaminant releases at Parcel D (which was later subdivided into Parcels D-1, D-2, G, and UC-1) were identified, and environmental investigations were conducted to identify and assess the nature and extent of contaminants in the following media of concern: (1) soil, (2) soil gas, (3) groundwater, and (4) radiologically impacted media. Table 7 summarizes the pre-ROD response actions. Parcel D was subdivided into Parcels D-1, D-2, G, and UC-1 in 2008, prior to the issuance of any RODs. As a result, there are multiple RODs to address the various parcels subdivided from the original Parcel D. The pre-ROD investigations and evaluations provided sufficient information to evaluate site risks, identify RGs, develop and evaluate remedial alternatives, and support the remedy selected in the RODs for Parcels D-1, D-2, G, and UC-1 (Navy, 2009b, 2009c, and 2010a).

The ROD for Parcels D-1 and UC-1 was finalized in July 2009 (Navy, 2009c). The selected remedy consists of actions to remove or treat significant amounts of contamination and actions to contain the remaining contamination and prevent contact through future monitoring, maintenance, and implementation of ICs. Table 8 summarizes the RAOs, as presented in the amended ROD for Parcels D-1 and UC-1, and identifies the components of the selected remedy that will address the RAOs.

The ROD for Parcel D-2 was finalized in August 2010 (Navy, 2010a). The ROD concluded that no further action was necessary for Parcel D-2. As a result, no RAOs were developed for Parcel D-2.

The ROD for Parcel G was finalized in February 2009 (Navy, 2009b). The selected remedy consists of actions to remove or treat significant amounts of contamination and actions to contain the remaining contamination and prevent contact through future monitoring, maintenance, and implementation of ICs. Table 9 summarizes the RAOs, as presented in the ROD for Parcel G, and identifies the components of the selected remedy that address the RAOs.

The Final ROD for Parcel G placed residential land use restrictions on the areas of Parcel G previously planned for non-residential land use in the SFRA's 1997 Redevelopment Plan, without determining whether residential land uses would be allowable. After approval of the Final ROD, the SFRA adopted an updated Redevelopment Plan in 2010 that includes mixed-use development (including residential use) throughout the entire parcel, provided the use is consistent with land use restrictions (SFRA, 2010).

To support implementation of the 2010 Redevelopment Plan, the OCII prepared a feasibility assessment in November 2016 that analyzed the residual concentrations of COCs in soil using health-based regulatory standards to identify whether the residential land use restrictions could be reduced. The feasibility assessment concluded that current site conditions are appropriate for residential use in most of Parcel G. The feasibility assessment also concluded that areas requiring residential land use restrictions could be reduced, provided that features of the selected remedy (e.g., durable covers and ICs with an operation and maintenance [O&M] plan) remain in place (Langan, 2016). An ESD to the Final ROD was prepared in April 2017 to document the reduction in areas requiring residential land use restrictions, based on the recommendations of the feasibility assessment (Navy, 2017c).

3.2.4. Pre-ROD Activities and Remedy Selection at Parcel E (Parcels E, E-2, and UC-3)

Activities associated with known or potential contaminant releases at Parcel E (which was later subdivided into Parcels E, E-2, and UC-3) were identified, and environmental investigations were conducted to identify and assess the nature and extent of contaminants in the following media of concern at Parcel E: (1) soil and shoreline sediment, (2) soil gas, (3) groundwater, (4) nonaqueous-phase liquid (NAPL) at IR-03, (5) landfill gas, and (6) radiologically impacted media. Table 10 summarizes the pre-ROD response actions. Parcel E-2 was subdivided from Parcel E in 2004. Parcel UC-3 was subdivided from the remainder of Parcel E in 2013. As a result, there are multiple RODs to address the various parcels subdivided from the original Parcel E. The pre-ROD investigations and evaluations provided sufficient information to evaluate site risks, identify RGs, develop and evaluate remedial alternatives, and support the remedies selected in the RODs for Parcels E, E-2, and UC-3 (Navy, 2013d, 2012, and 2014a, respectively).

The ROD for Parcel E was finalized in December 2013 (Navy, 2013d). The selected remedy consists of actions to remove or treat significant amounts of contamination and actions to contain the remaining contamination and prevent contact through future monitoring, maintenance, and implementation of ICs. Table 11 summarizes the RAOs, as presented in the ROD for Parcel E, and identifies the components of the selected remedy that address the RAOs.

The ROD for Parcel E-2 was finalized in November 2012 (Navy, 2012). The selected remedy consists of actions to remove or treat significant amounts of contamination and actions to contain the remaining contamination and prevent contact through future monitoring, maintenance, and implementation of ICs. Table 12 summarizes the RAOs, as presented in the ROD for Parcel E-2, and identifies the components of the selected remedy that will address the RAOs.

The ROD for Parcel UC-3 was finalized in January 2014 (Navy, 2014a). The selected remedy consists of actions to remove or treat significant amounts of contamination and actions to contain the remaining contamination and prevent contact through future monitoring, maintenance, and implementation of ICs. Table 13 summarizes the RAOs, as presented in the ROD for Parcel UC-3, and identifies the components of the selected remedy that address the RAOs.

3.2.5. Pre-ROD Activities and Remedy Selection at Parcel F

Activities associated with known or potential contaminant releases at Parcel F were identified, and environmental investigations were conducted to identify and assess the nature and extent of contamination. Table 14 summarizes the pre-ROD response actions at Parcel F. The Proposed Plan for Parcel F was published in April 2018 (Navy, 2018), but the ROD for Parcel F has not been published to date.

3.3. STATUS OF IMPLEMENTATION

This section describes the general status of the development, implementation, and operation (as applicable) of the selected remedies at each HPNS parcel.

3.3.1. IR-07/18

3.3.1.1. RA Activities and Implementation of ICs

The Navy published the Final RD Package for IR-07/18, which describes the basis of design for the final remedy, in January 2010 (ChaduxTt, 2010a). The remedy components for each contaminated medium at IR-07/18 are described below.

- **Soil, Sediment, and Soil Gas:** The selected remedy for soil consists of (1) construction of a durable cover consisting of a 3-foot soil cover over areas requiring institutional controls (ARICs) for radionuclides; (2) construction of a durable cover consisting of a 2-foot soil cover over non-radiological areas; (3) construction of a durable cover consisting of riprap revetment over the shoreline in IR-07; (4) long-term monitoring (LTM) of soil gas in areas where methane concentrations exceed RGs; and (5) ICs to restrict specific land uses and activities.
- **Groundwater:** The selected remedy for groundwater consists of (1) monitored natural attenuation (MNA) and (2) ICs to restrict specific land uses and activities.
- **Radiologically Impacted Media:** The selected remedy for radiologically impacted media consists of (1) conducting a surface scan for radioactive materials over all of IR-07/18; (2) excavation and offsite disposal of all radiological anomalies exceeding radiological RGs for residential soil to a depth of 1 foot; (3) installation of an orange demarcation layer (2 feet below the final cover surface) within the ARIC for radionuclides; (4) conducting a final surface scan for radioactive materials over the soil cover throughout IR-07/18; (5) short-term groundwater monitoring for radionuclides of concern; and (6) ICs to restrict specific land uses and restrict activities.

Figure 3 identifies the locations of the major remedy components at IR-07/18. Construction of the remedy at IR-07/18 began in June 2010 and was completed in September 2011 (ERRG, 2012a). Construction tasks included excavating shoreline debris and sediment and constructing a revetment structure; radiological scanning of the subgrade surface; installing a soil cover; radiological scanning of the final cover surface; radiological screening and sampling of shoreline debris, shoreline sediment, and excavated soil; and installing fencing and warning signs.

The Navy completed a Multi-Agency Radiation Survey and Site Investigation Manual (MARSSIM) Class 1 survey of the entire surface of IR-07/18, and the top 1 foot was remediated to levels specified in the Amended ROD (Navy, 2009a) to ensure a radiologically cleared surface prior to placement of the final cover.

The shoreline revetment includes, from the bottom up, filter fabric, 6 to 12 inches of filter rock, and 2.5 to 3 feet of riprap. The filter fabric is designed to prevent migration of soil and sediment to San Francisco Bay; the filter rock and riprap layers protect the fabric from damage by wave action.

A soil cover was constructed over most of the remaining surface of IR-07/18. In the area identified in the Amended ROD as radiologically impacted (Navy 2009a), the cover includes, from the bottom up, 1 foot of clean imported soil, a demarcation layer that includes an orange geotextile and metallic demarcation tape placed over the fabric in a 10- by 10-foot grid, and 2 feet of clean imported soil. In areas not identified as radiologically impacted, the cover is composed of 2 feet of clean imported soil. The final cover includes surface completions for groundwater monitoring wells and methane monitoring probes, as well as storm water drainage features.

An asphalt cover, rather than a 2-foot-thick soil cover, was constructed over a small area (about 60 feet by 130 feet) in the northeastern corner of IR-07 to allow for a more gradual transition to the final asphalt cover in the adjoining area of Parcel B-1. The asphalt cover included 2 inches of asphalt over 4 inches of aggregate base course.

About 470 cubic yards of soil from the inland areas and additional sediment and debris (concrete, brick, and metal) from the shoreline were removed because cesium or radium concentrations exceeded the stringent release criteria or because the waste was unable to be scanned and thus was assumed to be low-level radioactive waste (LLRW). No radiological releases were confirmed, and no radiological devices were discovered during any of the radiological surveys. In total, 109 LLRW bins (representing about 1,970 tons of waste) were removed and disposed of off site as LLRW. In addition, about 5,390 tons of nonhazardous waste and 2,940 tons of non-Resource Conservation and Recovery Act hazardous waste were removed and disposed of off site. The California Department of Public Health (CDPH) completed further surface scans at IR-07/18, before and after the soil cover was installed. CDPH concluded that there was no evidence or indication of radiological health and safety concerns based on surface gamma radiation in the surveyed areas of IR-07/18 (CDPH, 2013).

Methane was not detected in any gas monitoring probe in samples collected semiannually since the probes were installed in November 2008 (Innovative Technical Solutions, Inc. [ITSI], 2010c; ERRG, 2012a). The methane probes were decommissioned in 2012 (ERRG, 2012c).

Land use restrictions were designed to limit exposure of future landowners or users of the property to hazardous substances and to maintain the integrity of the remedy. The land use control (LUC) objectives will be met by controlling access to the property. The site is currently, and will remain, enclosed by a

perimeter fence with locked gates until transfer to the OCII. The activity and land use restrictions described in the LUC RD Report (ChaduxTt, 2010a) will be incorporated into the Quitclaim Deed and Covenant to Restrict Use of Property and will take effect upon transfer to OCII and issuance of those documents.

3.3.1.2. LTM and Maintenance Activities

Durable Cover Maintenance and IC Compliance

Long-term maintenance requirements are detailed in the O&M Plan for IR-07/18 (ERRG, 2012d). Major inspection items include:

- Security: Condition of fencing and signs, evidence of vandalism or unauthorized access, and condition of roads.
- Soil Cover: Evidence of settlement, cracking, or erosion; evidence of slope failure; signs of burrowing pests; adequacy of vegetative cover; signs of excessive traffic; obstructions in drainage swales and evidence of overflow or erosion; and demarcation layer not exposed.
- Revetment: Evidence of settlement, excessive traffic, or pests; evidence of vandalism or theft of armoring; evidence of wave overtopping; signs of scour or erosion at toe or flanks; and filter fabric not exposed.
- Asphalt Cover: Evidence of settlement, cracking, or holes; evidence of ponding; and evidence of excessive traffic.
- Groundwater Monitoring Wells: Evidence of damage or vandalism, presence of obstructions, and condition of locks and seals.
- ICs: No construction of residences or enclosed structures without authorization, no use of groundwater, no growing edible items, no land-disturbing activity or disturbance of remedy components (including no excavation beneath demarcation layer) without authorization, and no damage to security features. (Note: some restricted activities may be conducted provided the requirements of the LUC RD [ChaduxTt, 2010a] are followed.)

Quarterly inspections were conducted in October 2011, January 2012, April 2012, and July 2012 during the first year of LTM and maintenance (ERRG, 2012c). Quarterly inspections were conducted in October 2012, January 2013, April 2013, and July 2013 during the second year of LTM and maintenance (ERRG, 2013h).

The inspection frequency was reduced to semiannual following the second year of LTM and maintenance. Semiannual inspections were conducted in October 2013 and April 2014 during the third year of LTM and maintenance (ERRG, 2014i).

The Navy did not formally inspect IR-07/18 in 2015 (i.e., the fourth year of LTM and maintenance) because it was in the process of securing a new O&M contract for the sites. However, the Navy did perform informal inspections and maintenance to ensure the integrity of the remedy components.

In 2016, the Navy reduced the inspection and maintenance frequency to annually for IR-07/18. The annual inspection event was conducted in April 2016 during the fifth year of LTM and maintenance, but was not formally documented. No maintenance or repairs were performed in 2016.

In 2017, the Navy shifted the annual inspections from the month of April to the month of October to align the inspections with the start of the wet season in the local area. The Navy also revised its O&M procedures to distribute maintenance activities throughout the year, rather than just at the time of the annual inspections, to ensure the remedies are maintained appropriately. For example, (1) mowing of the durable cover is performed in May to reduce the risk of fire hazard in the summer, (2) swales are cleaned of sediment and debris both before and after the rainy season to ensure proper function, and (3) fences are repaired throughout the year to maintain site security. The most recent annual inspection was conducted in October 2017 during the sixth year of LTM and maintenance (IEJV, 2018a), with the maintenance event occurring throughout 2017. This approach was applied to all parcels in the O&M phase (i.e., Parcels B-1, B-2, C, and G).

Throughout the first 6 years of LTM and maintenance, inspections generally concluded that the remedies remain intact and in good condition and they are functioning as intended. Minor issues encountered included occasional vandalism of the fencing, identification of shallow animal burrows, and minor areas where poor vegetation growth occurred due to damage from site activities and drought. Each of these items was addressed in a timely manner and in accordance with the O&M Plan (ERRG, 2012d).

Each year since remedy completion, the Navy conducted inspections to verify continued compliance with the ICs applicable to IR-07/18. The inspection reports certify that the ICs related to land and groundwater use restrictions are being implemented in accordance with the LUC RD (ChaduxTt, 2010a).

Groundwater Monitoring

Groundwater monitoring is conducted throughout HPNS under the Basewide Groundwater Monitoring Program (BGMP) (CE2-Kleinfelder Joint Venture [JV], 2011b and 2012c; Trevet, Inc., 2017a). The BGMP includes quarterly monitoring of groundwater elevations to evaluate the direction and gradient of groundwater flow and sampling and analysis of COCs at varying frequencies. Periodic monitoring reports (referenced in Appendix A) are published that describe the monitoring results and compare the results to the RGs or trigger levels (TLs) to verify the RAOs for groundwater are being met. TLs were established for protection of the beneficial uses of the bay, including ecological receptors.

The current monitoring program includes semiannual sampling of two monitoring wells (IR07MW24 and IR07MW26A) near the San Francisco Bay margin. These wells are monitored to ensure that COCs in groundwater do not migrate to the bay at concentrations that adversely impact ecological receptors (Navy, 2009a).

The Amended ROD (Navy, 2009a) identified monitoring for the following COCs at IR-07/18: metals (chromium VI, copper, lead, mercury, nickel, and selenium) and radionuclides (cesium-137, plutonium-239, radium-226, and strontium-90). Since at least 2004, COC concentrations have generally remained below their respective TLs (Trevet, Inc., 2018). However, lead concentrations exceeded the RG of 14.44 micrograms per liter (µg/L) during one sampling event (September 2017). This is the first time lead concentrations have exceeded the RG in the past 10 years.

Monitoring will continue in IR-07/18 in accordance with the RAMP (ChaduxTt, 2010a) and any subsequent modifications made under the BGMP until RGs or TLs are met consistently or until RAOs have been met through other means.

3.3.2. Parcels B-1 and B-2

3.3.2.1. RA Activities and Implementation of ICs

The Navy published the Final RD Package for Parcels B-1 and B-2, which describes the basis of design for the final remedy, in December 2010 (ChaduxTt, 2010d). The RD was subsequently revised, including a revision to the LUC RD completed in July 2011 (ChaduxTt, 2011e and 2011f) and an amendment in September 2012 to address revisions to the revetment design based on an updated stability analysis using new geotechnical data (ChaduxTt, 2012c). The remedy components for each contaminated medium at Parcels B-1 and B-2 are described below.

- **Soil, Sediment, and Soil Gas:** The selected remedy for soil, sediment, and soil gas consists of (1) excavation of soil hot spots where COCs exceeded RGs; (2) construction of a durable cover consisting of a 2-foot soil cover; (3) construction of a durable cover consisting of riprap revetment; (4) construction of a durable cover consisting of 4 inches of aggregate base course overlain by 2 inches of asphaltic concrete; (5) restoration of cracks and penetrations in building foundations; (6) implementation of soil vapor extraction (SVE) at IR-10 to reduce VOC concentrations in soil; and (7) ICs to restrict specific land uses and activities.
- **Groundwater:** The selected remedy for groundwater consists of (1) treatment of VOCs in groundwater at IR-10 through injection of a biological amendment, (2) MNA for remaining VOCs and LTM for metals in groundwater, and (3) ICs to restrict specific land uses and activities.
- **Radiologically Impacted Media:** The selected remedy for radiologically impacted media consists of (1) decontamination or dismantling and offsite disposal of radiologically impacted structures; (2) excavation and offsite disposal of radiologically impacted storm drain and sanitary sewer lines and soil from adjacent impacted areas; and (3) survey and obtain unrestricted release of buildings, former building sites, and radiologically impacted areas.

Figures 4 and 5 identify the locations of major remedy components at Parcels B-1 and B-2. Construction of the remedies in Parcels B-1 and B-2 was phased. Hot spot removal was performed between August 2010 and May 2011 (ERRG, 2011). Other RA activities (durable cover construction, SVE in IR-10 and groundwater injection in IR-10) began in November 2012. The construction of durable covers was

completed in September 2013 at Parcel B-1 (ERRG, 2017) and in May 2015 at Parcel B-2 (IEJV, 2018b). The SVE system was constructed between December 2012 and May 2013, and operation of the SVE system is ongoing. Polylactate injection in groundwater at IR-10 was performed between February and March 2013, and post-injection performance monitoring is ongoing.

In total, 143 loose cubic yards of soil was excavated from three hot spot areas in Parcels B-1 and B-2, to address lead and PAHs in soil, and disposed of off site (ERRG, 2011). Excavations were backfilled with clean imported soil.

Shoreline revetment was constructed along approximately 1,800 linear feet of shoreline at IR-23 and IR-26 (ERRG, 2017; IEJV, 2018b). An unforeseen discovery of TPH contamination along a 230-foot section of the IR-26 shoreline (in Parcel B-2) delayed completion of the revetment to allow for the TPH contamination to be delineated and removed. The shoreline revetment includes, from the bottom up, filter fabric, 6 to 12 inches of filter rock, and 2.5 to 3 feet of riprap. The filter fabric is designed to prevent migration of soil and sediment to San Francisco Bay; the filter rock and riprap layers protect the fabric from damage by wave action.

A soil cover was constructed on the hillside portions of Parcel B-1 (ERRG, 2017). The soil cover is composed of 2 feet of clean imported soil. The soil cover includes surface completions for groundwater monitoring wells and stormwater drainage features.

An asphalt cover was constructed over the remaining upland areas of Parcels B-1 and B-2 (ERRG, 2017; IEJV, 2018b). The asphalt cover consists of 4 inches of aggregate base course overlain by 2 inches of asphaltic concrete. Drainage features such as swales, diversion berms, catch basins, and storm drain pipes were incorporated into the asphalt cover to convey stormwater off site.

Cracks and penetrations in building foundations were repaired using a variety of materials, such as concrete, non-shrink grout, and asphaltic concrete, to prevent access to underlying soil (ERRG, 2017; IEJV, 2018b). Additionally, access to soil under buildings (e.g., crawl spaces) was blocked with durable wire mesh.

The existing SVE system in Building 123 at IR-10 consists of a blower, blower motor, electrical panel, SVE wells, vapor monitoring wells, liquid/air separator, transfer pump, liquid storage tank, connection hoses, level switches, system interlocks and controls, and gauges. As part of the RA, the existing SVE system was expanded to include three new SVE wells to maximize the removal of VOCs from the subsurface beneath Building 123. The system was also repaired, tested, and recommissioned for operation prior to its startup in March 2013. The information will be documented in a future RACR for IR-10.

System operation is ongoing, and approximately 18.5 pounds of VOCs (including 18 pounds of trichloroethene [TCE]) have been removed from the subsurface to date. In 2017, the system was modified to include a variable frequency motor drive to improve control over the vacuum pressure applied by the system's blower. System operation is monitored and optimized, as required, to maximize its removal

efficiency. Optimization measures include targeted operation of SVE wells in the areas of highest contaminant concentrations, pulsed and cycled operations of extraction wells, and passive air venting. SVE operations to date have revealed that the system is operating in diffusion-limited soil conditions, which limits the efficacy of mass removal and results in long rebound times (IEJV, 2017).

Approximately 2,658 pound of polylactate hydrogen release compound primer and 5,490 pounds of polylactate hydrogen release compound were injected into 45 groundwater injection points in March 2013 using an injection tool drill rig. Approximately 152 pounds of polylactate substrate was injected at each location (approximately 7.6 pounds of polylactate substrate per vertical foot). Post-injection monitoring is currently ongoing under the BGMP. The information will be documented in a future RACR for IR-10.

The Third Five-Year Review Report identified an issue regarding mercury concentrations in groundwater within Parcel B-2 (at IR-26 wells IR26MW49A and IR26MW51A) (TriEco-Tt, 2013b). Mercury remained in groundwater at concentrations greater than the TLs despite (1) a removal action conducted from 2000 to 2001 to remove 5,178 cubic yards of mercury-contaminated soil from the area to a maximum depth of 10 feet bgs and (2) a time-critical removal action (TCRA) conducted in 2008 to remove 4,500 cubic yards mercury-contaminated soil to a maximum depth of 16 feet bgs. The Third Five-Year Review Report recommended that (1) groundwater at wells IR26MW49A and IR26MW51A should continue to be monitored semiannually for mercury to evaluate the trend in mercury concentrations, and (2) the mass flux of mercury into the bay in the vicinity of wells IR26MW49A and IR26MW51A should be evaluated (TriEco-Tt, 2013b). Since 2013, groundwater continues to be monitored for mercury at bay margin wells (including wells IR26MW49A and IR26MW51A) under the BGMP. Additionally, in 2015, an evaluation was conducted at IR-26 to estimate the mass discharge of mercury to the bay via groundwater transport (TriEco-Tt, 2016). In-situ treatment of mercury using a stabilizing agent is currently underway (KMEA MACTEC Joint Venture, 2017) to minimize migration of mercury in groundwater to the bay. The results of groundwater treatment and performance monitoring for mercury at IR-26 will be reported in a future Remedial Action Completion Report (RACR).

Radiological remediation was started in 2006 and completed in 2010 under a basewide TCRA (Navy, 2006). In total, 65,184 cubic yards of soil was removed from 24,826 linear feet of sanitary sewer and storm drain lines; approximately 2,910 cubic yards of soil was disposed of off site as LLRW. Six radiologically impacted buildings (103, 113, 113A, 130, 140, and 146), three former building sites (114, 142, and 157), and the Building 140 discharge channel were screened and remediated (Tetra Tech EC, Inc. [TtEC], 2012a). All radiological work is currently being reviewed to determine if current site conditions are compliant with the RAOs.

3.3.2.2. LTM and Maintenance Activities

Durable Cover Maintenance and IC Compliance

Long-term maintenance requirements are detailed in the O&M Plans for Parcels B-1 and B-2 (ERRG, 2016; IEJV, 2018c). Major inspection items include:

- Security: Condition of fencing and signs, evidence of vandalism or unauthorized access, and condition of roads.
- Soil Cover: Evidence of settlement, cracking, or erosion; evidence of slope failure; signs of burrowing pests; adequacy of vegetative cover; signs of excessive traffic; and obstructions in drainage swales and evidence of overflow or erosion.
- Revetment: Evidence of settlement, excessive traffic, or pests; evidence of vandalism or theft of armoring; evidence of wave overtopping; signs of scour or erosion at toe or flanks; and filter fabric not exposed.
- Asphalt Cover: Evidence of settlement, cracking, or holes; evidence of ponding; and evidence of excessive traffic.
- Groundwater Monitoring Wells: Evidence of damage or vandalism, presence of obstructions, and condition of locks and seals.
- ICs: No construction of residences or enclosed structures without authorization, no use of groundwater, no growing edible items, no land-disturbing activity or disturbance of remedy components without authorization, and no damage to security features. (Note: Some restricted activities may be conducted provided that the requirements of the LUC RD [ChaduxTt, 2011e and 2011f] are followed.)

Although RACRs were not published until January 2017 and April 2018 for Parcels B-1 and B-2, respectively, the Navy conducted quarterly inspections and maintenance events for constructed components of the durable covers remedy in January, April, July, and October 2014 (ERRG, 2014b, 2014d, 2014e, and 2014j). The inspection, maintenance, and monitoring programs were implemented early to ensure the durable cover components remained intact and operated as intended following their construction.

The inspection frequency was reduced to semiannually following the first year of LTM and maintenance. Inspections and maintenance were performed semiannually in April and October 2015 (ERRG, 2015g and 2015j).

The Navy did not formally inspect Parcels B-1 and B-2 in 2015 (i.e., the third year of LTM and maintenance) because it was in the process of securing a new O&M contract for the sites. However, the Navy did perform informal inspections and maintenance to ensure the integrity of the completed remedy components.

The inspection frequency was reduced to annually following the third year of LTM and maintenance. O&M activities were realigned to match those described for IR-07/18 in Section 3.3.1.2.

Throughout the first 4 years of LTM and maintenance, inspections generally concluded that the remedies remain intact and in good condition and they are functioning as intended. Minor issues encountered included occasional vandalism of the fencing, identification of shallow animal burrows in the soil cover, minor damage to the asphalt cover due to overgrowth of weeds and contractor activities, and minor areas of poor vegetation growth due to damage from site activities and drought. Each of these items was

addressed in a timely manner and in accordance with the O&M Plans for Parcels B-1 and B-2 (ERRG, 2016; IEJV, 2018c).

In 2017, the Navy conducted inspections to verify compliance with the ICs applicable to Parcels B-1 and B-2. The inspection reports certify that the ICs related to land use and activity restrictions are being implemented in accordance with the LUC RD (ChaduxTt, 2011e and 2011f).

Groundwater Monitoring

Groundwater monitoring is conducted throughout HPNS under the BGMP (CE2-Kleinfelder JV, 2011b and 2012c; Trevet, Inc., 2017a). The BGMP includes quarterly monitoring of groundwater elevation to evaluate the direction and gradient of groundwater flow and sampling and analysis of COCs at varying frequencies. Periodic monitoring reports are published that describe the monitoring results and compare the results to the RGs or TLs to verify the RAOs for groundwater are being met. TLs were established for protection of the beneficial uses of the bay, including ecological receptors.

For Parcel B-1, the COCs are identified as VOCs. The VOC plume (primarily TCE and its degradation product vinyl chloride [VC]) at IR-10 is being monitored for changes in concentrations and potential migration toward San Francisco Bay. Results from groundwater monitoring (since the injection of biological amendments in 2013) indicate an overall reduction in the concentrations of TCE over time, but more data collection is required to make any definitive determinations about long-term TCE concentration trends. The May 2017 groundwater sampling event was the first event where TCE concentrations were less than the RG for all monitoring wells sampled. VC concentrations continue to exceed the RG in Parcel B-1 but are generally stable. Performance monitoring for the in-situ treatment remedy at IR-10 continues, and more definitive results will be summarized in future technical publications.

The Navy conducted an investigation in August 2017 to evaluate whether per- and polyfluoroalkyl substances (PFAS) are present in groundwater at IR-10 within Parcel B-1 as a result of historical uses (Trevet, Inc., 2018). Monitoring wells IR10MW28A, IR10MW13A1, and IR10MW31A1 were analyzed for PFAS compounds, including perfluorooctanoic acid (PFOA), perfluorooctane sulfonate (PFOS), combined PFOA and PFOS, and perfluorobutane sulfonate (PFBS). PFOA and PFOS were detected in one monitoring well (IR10MW28A) at concentrations less than the federal screening criterion (FSC) of 70 nanograms per liter (ng/L). PFBS was detected in one monitoring well (IR10MW31A1) at an estimated concentration of 2.28 ng/L, well below the FSC of 380 ng/L. Concentrations of PFOA, PFOS, combined PFOA and PFOS, and PFBS were less than their respective FSCs during the PFAS groundwater investigation. Based on available data, groundwater at IR-10 has not been affected by PFAS.

For Parcel B-2, the COCs are identified as VOCs and metals. Dichlorodifluoromethane (Freon-12) is monitored in one monitoring well (IR26MW41A) to evaluate the potential risk to human health based on vapor intrusion. Freon-12, mercury, and copper have historically exceeded their respective RGs in groundwater. Mercury concentrations also consistently exceeded the TL of 0.6 µg/L in three monitoring

wells (IR26MW49A, IR26MW51A, and PA50MW02A). At IR-26, in-situ stabilization within the saturated zone is currently being performed to reduce mercury concentrations in groundwater and minimize migration of mercury in groundwater to San Francisco Bay (KMEA MACTEC Joint Venture, 2017). Performance monitoring of the in-situ treatment remedy in IR-26 is underway, and results will be summarized in future technical publications.

Monitoring will continue in Parcels B-1 and B-2 in accordance with the RAMP and subsequent modifications made under the BGMP until RGs or TLs are met consistently or until RAOs have been met through other means.

3.3.3. Parcel C

3.3.3.1. RA Activities and Implementation of ICs

The Navy published the Final RD Package for Parcel C, which describes the basis of design for the final remedy, in October 2012 (CH2M HILL Kleinfelder, A Joint Venture [KCH], 2012). Revisions to the design include an ESD completed in October 2014 that documented changes to soil excavation boundaries as a result of applying tiered action levels for select COCs based on risk identified in a screening-level HHRA rather than excavating to RGs in all excavation locations (Navy, 2014b). The remedy components for each contaminated medium are described below.

- **Soil and Soil Gas:** The selected remedy for soil and soil gas consists of (1) excavation of soil hot spots where COCs exceed RGs; (2) construction of a durable cover consisting of a 2-foot-thick vegetated soil cover; (3) construction of a durable cover consisting of shoreline armoring; (4) construction of a durable cover consisting of 4 inches of aggregate base course overlain by 2inches of asphaltic concrete; (5) restoration of cracks and penetrations in building foundations; (6) implementation of SVE at eight locations to reduce VOC concentrations in soil; and (7) ICs to restrict specific land uses and activities.
- **Groundwater:** The selected remedy for groundwater consists of (1) treatment of VOCs in groundwater plumes through injection of zero-valent iron (ZVI) or biological amendments, (2) MNA for remaining VOCs and LTM for metals in groundwater, and (3) ICs to restrict specific land uses and activities.
- **Radiologically Impacted Media:** The selected remedy for radiologically impacted media consists of (1) decontamination or dismantling and offsite disposal of radiologically impacted structures; (2) excavation and offsite disposal of radiologically impacted storm drain and sanitary sewer lines and soil from adjacent impacted areas; and (3) survey and obtain unrestricted release of buildings, former building sites, and radiologically impacted areas.

Figure 6 identifies the locations of the major remedy components at Parcel C. Implementation of the remedies in Parcel C is being phased and is still ongoing. Hotspot removal from 18 excavation areas was performed between 2013 and 2015 (APTIM Federal Services, LLC [APTIM], 2018b). The construction of durable covers began in June 2015 and was completed in May 2016 (TtEC, 2017c). Construction and operation of five SVE systems within Remedial Unit (RU)-C1, RU-C2, RU-C4, and RU-C5 began in 2013,

and operation of the SVE systems is ongoing, although operation has been temporarily suspended to allow for additional site characterization and remediation. ZVI and in-situ bioremediation (ISB) injections at groundwater plumes were performed between 2013 and 2017, and post-injection performance monitoring is ongoing (APTIM, 2018).

In total, 28,261 bank cubic yards of soil was excavated from 18 hotspot areas in Parcel C, to remove soil with COC concentrations greater than RGs, and disposed of at an offsite facility (APTIM, 2018b). During the RA, 10 previously remediated underground storage tanks were confirmed to be removed or closed in place. Excavations were backfilled with clean imported soil. To date, all hotspot excavation activities have been completed, except for excavations to be performed within Buildings 251.

Shoreline armoring was constructed along approximately 80 linear feet of deteriorated seawall northeast of Building 231 (TtEC, 2017c). The shoreline armoring includes, from the bottom up, filter fabric, a 6-inch minimum layer of filter rock, and a 3-foot minimum layer of riprap. The filter fabric is designed to prevent migration of soil to San Francisco Bay; the filter rock and riprap layers protect the fabric from damage by wave action.

A soil cover was constructed on the hillside in the northwest corner of Parcel C (TtEC, 2017c). The soil cover is composed of 2 feet of clean imported soil. The soil cover includes surface completions for groundwater monitoring wells.

An asphalt cover was constructed over the remaining areas of the site (TtEC, 2017c). Most of Parcel C was covered with degraded asphalt pavement prior to the durable covers RA, and the existing asphalt pavement was repaired or replaced as needed to create a continuous intact cover. Areas in which the existing asphalt cover required minor repair were typically overlain with new asphaltic concrete to achieve a 2-inch-thick cover. Asphalt replacement, where needed, consisted of 4 inches of aggregate base course overlain by 2 inches of asphaltic concrete. Drainage features such as swales, catch basins, and storm drain pipes were incorporated into the asphalt cover to convey stormwater off site.

Cracks and penetrations in building foundations were repaired using a variety of materials, such as concrete, non-shrink grout, and asphaltic concrete, to prevent access to underlying soil (TtEC, 2017c). Building foundations that could not be restored or repaired (e.g., historical buildings) were secured using a combination of steel plates, framed plywood walls, wire mesh, and/or chain link fence to prevent access. Additionally, access to soil under buildings (e.g., crawlspaces and vaults) was blocked with durable wire mesh or secured with steel ties.

Five SVE systems were installed to remediate eight soil vapor areas (1 through 8) that overlie groundwater VOC plumes (APTIM, 2018b). Each system includes a blower, blower motor, main control panel, SVE wells, vapor monitoring wells, liquid/air separator, transfer pump and liquid storage tank, conveyance piping and connection hoses, granular activated carbon vessels, level switches, system interlocks and controls, and gauges. The SVE systems were operated at Areas 1, 3, 6, 7, and 8 beginning in August 2014,

and system operation, monitoring, performance sampling, and optimization activities were performed through February 2016; at which time, operation was temporarily ceased to transfer SVE operations to a new contractor. The SVE system at Area 3 was expanded in March 2016 to also treat soil vapor in Areas 4 and 5. System operation has not yet been performed at Areas 2, 4, and 5. Additional operations are planned for Areas 1, 3, 6, 7, and 8, and the performance of these SVE systems to date is described below.

- Area 1: Approximately 2.5 pounds of VOCs (predominantly TCE) has been removed
- Area 3: Approximately 1.4 pounds of VOCs (predominantly tetrachloroethene [PCE] and TCE) has been removed
- Areas 6 and 7: Approximately 4 pounds of VOCs (predominantly TCE) has been removed
- Area 8: Approximately 21 pounds of VOCs (predominantly PCE and TCE) has been removed

Operation of the SVE systems is monitored and optimized, as required, to maximize its removal efficiency. Following asymptotic conditions, optimization measures include targeted operation of SVE wells in the areas of highest contaminant concentrations, pulsed and cycled operations of extraction wells, and adjusting operating vacuum pressures to minimize water entrainment from the SVE wells.

Between 2014 and 2017, active groundwater treatment using ZVI, anaerobic ISB, and/or aerobic ISB was implemented at plumes in RU-C1, RU-C4, and RU-C5 (APTIM, 2018b). Anaerobic ISB consisted of direct injection of (1) an anaerobic organic substrate (sodium lactate) with bioaugmentation (*Dehalococcoides*, specifically SDC-9™) or (2) food-grade molasses as a substrate. Aerobic ISB consisted of direct injection of an oxygen-releasing compound (PermeOx Ultra®). The following list summarizes the various active groundwater treatment methods that were implemented:

- Approximately 206,183 pounds of micro-scale ZVI powder mixed with water was injected into 40 points to primarily treat chlorinated VOCs (CVOCs)
- Approximately 114,500 gallons of sodium lactate and SDC-9™ mixture was injected into 122 points to primarily treat CVOCs
- Approximately 16,064 gallons of molasses and water solution was injected into 17 points to primarily treat chromium VI
- Approximately 5,795 pounds of PermeOx Ultra® mixed with water was injected into 8 points to primarily treat naphthalene, chlorobenzene, and dichlorobenzene compounds

The maximum injection depth varied from 25 feet bgs to as deep as 49 feet bgs with injections occurring at 3-foot intervals. Groundwater treatment was successfully conducted to achieve source reduction and partially meet RAOs as described in the Final ROD (Navy, 2010). Post-injection groundwater monitoring is currently being performed under the BGMP.

Treatment work in RU-C2 was initiated in 2014, but has not been completed. Currently, additional in-situ active groundwater treatment and source removal is planned for RU-C1 and RU-C2 (ECC-Insight, LLC and CDM Smith, 2017c). Active groundwater treatment will consist of additional ZVI and ISB injections to treat CVOCs and/or carbon tetrachloride. In addition, over-excavation is required to meet the residential RGs in soil in Building 251 and removal of sumps is planned in Building 253.

Radiological remediation at Parcel C began in 2007 under a basewide TCRA (Navy, 2006) and continued as part of the RA. Radiological surveys and remediation have been performed for all radiologically impacted buildings (203, 205 and discharge tunnel, 211, 214, 224, 241, 253, 271, and 272), storm drains, and sanitary sewers, except for Buildings 211 and 253. In total, 37,572 cubic yards of soil was removed from 19,260 linear feet of sanitary sewer and storm drain lines; approximately 987 cubic yards of soil was disposed off site as LLRW (TtEC, 2016d). All radiological work is currently being reviewed to determine if current site conditions are compliant with the RAOs.

3.3.3.2. LTM and Maintenance Activities

Durable Cover Maintenance and IC Compliance

Long-term maintenance requirements are described in the O&M Plan for Parcel C (TtEC, 2017b). The O&M Plan includes inspection items that are similar to those described for Parcels B-1 and B-2 (Section 3.3.2.2).

Although the Parcel C RACR for the durable covers was not published until March 2017, the Navy conducted quarterly inspections and maintenance events for constructed components of the durable covers remedy in July 2016, October 2016, January 2017, and March 2017 (TtEC, 2017c). The inspection, maintenance, and monitoring programs were implemented early to ensure that the durable cover components remained intact and operated as intended following their construction.

The inspection frequency was reduced to annually following the first year of LTM and maintenance. O&M activities were realigned to match those described for IR-07/18 in Section 3.3.1.2.

Throughout the first 2 years of LTM and maintenance, inspections generally concluded that the remedies remain intact and in good condition and they are functioning as intended. Minor issues encountered included occasional vandalism of the fencing, minor damage to the asphalt cover due to overgrowth of weeds and contractor activities, minor damage to the asphalt cover due to subsidence along seawalls, and minor areas of poor vegetation growth due to damage from site activities and drought. Each of these items was addressed in a timely manner and in accordance with the O&M Plan (TtEC, 2017b).

In 2017, the Navy conducted inspections to verify compliance with the ICs applicable to Parcel C. The inspection reports certify that the ICs related to land use and activity restrictions are being implemented in accordance with the LUC RD (KCH, 2012).

Groundwater Monitoring

Groundwater monitoring is conducted throughout HPNS under the BGMP (CE2-Kleinfelder JV, 2011b and 2012c; Trevet, Inc., 2017a). The BGMP includes quarterly monitoring of groundwater elevations to evaluate the direction and gradient of groundwater flow and sampling and analysis of COCs at varying frequencies. Periodic monitoring reports are published that describe the monitoring results and compare the results to the RGs or TLs to verify the RAOs for groundwater are being met.

Parcel C is currently monitored in support of the selected remedy specified in the ROD, with monitoring recommendations provided in the RD (Navy, 2010b; KCH, 2012). Groundwater samples are collected semiannually from 75 monitoring wells within Parcel C and analyzed for MNA parameters, metals, VOCs, SVOCs, and total TPH. Parcel C contains four RUs (C1, C2, C4 and C5). Each RU has a unique list of COCs and chemicals of ecological concern (COECs). In general, the COCs and COECs in Parcel C include metals (including chromium VI), VOCs, and TPH (added in 2017).

Additional in-situ treatment and performance monitoring for in-situ treatment remedies implemented at the RU plumes in Parcel C is underway, and monitoring results will be summarized in future technical publications (ECC-Insight, LLC and CDM Smith, 2017c).

3.3.4. Parcel D-1

3.3.4.1. RA Activities and Implementation of ICs

The Navy published the Final RD Package for Parcel D-1, which describes the basis of design for the final remedy, in February 2011 (ChaduxTt, 2011d). The remedy components for each contaminated medium are described below.

- **Soil and Soil Gas:** The selected remedy for soil and soil gas consists of (1) excavation of soil hot spots and removal of soil stockpiles where COCs exceed RGs; (2) repair of durable asphalt covers with minor damage; (3) construction of a durable cover consisting of 2 inches of new asphaltic concrete placed over new or existing aggregate base course; (4) restoration of cracks and penetrations in building foundations; (5) construction of a durable cover consisting of riprap stabilization in several small areas adjacent to existing seawalls; (6) soil gas surveys to evaluate vapor intrusion risks and assess the need for additional remedial activities or ARICs; and (7) ICs to restrict specific land uses and activities.
- **Groundwater:** The selected remedy for groundwater consists of (1) treatment of VOCs in groundwater at the IR-71 plume using ISB or ZVI, (2) MNA, and (3) ICs to restrict specific land uses and activities.
- **Radiologically Impacted Media:** The selected remedy for radiologically impacted media consists of (1) decontamination or dismantling and offsite disposal of radiologically impacted structures; (2) excavation and offsite disposal of radiologically impacted storm drain and sanitary sewer lines and soil from adjacent impacted areas; and (3) survey and obtain unrestricted release of buildings, former building sites, and radiologically impacted areas.

Figure 7 identifies the locations of major remedy components at Parcel D-1. Completion of the RA activities in Parcel D-1 occurred in phases. Soil hot spots and stockpiles were removed in two phases: the first phase was conducted between August 2010 and May 2011 (ERRG, 2011), and the second phase was conducted between May 2013 and July 2013 (ERRG, 2014c). A soil gas study was completed in 2013 (Sealaska Environmental Services, LLC [SES], 2013); results from the study were used to evaluate potential risk to human health via vapor intrusion and to assess the need for ARICs for VOC vapors. Radiological removals and subsequent construction of the durable covers at Parcel D-1 are being implemented in two phases. The Phase I radiological remediation was performed under a basewide TCRA between 2010 and 2014 (Shaw Environmental & Infrastructure, Inc., 2014a), and the Phase II radiological remediation was performed in 2016 as part of the RA (Gilbane Federal, 2018a). At the time this report was prepared, durable covers have been constructed over the Phase I area only. Construction of the durable cover over the Phase II area is scheduled to begin in 2018.

The pre-ROD groundwater treatability study included an assessment of risks to human health and the environment from metals and VOCs in two groundwater plumes at Parcel D-1. The two plumes (known as the IR-71 West and IR-71 East plumes) originate in Parcel G and extend into Parcel D-1. The treatability study concluded the IR-71 West plume required treatment with ZVI to address chloroform in groundwater. Approximately 136,000 pounds of ZVI was injected into 88 groundwater injection points in the IR-71 West plume between October and December 2008, prior to the publication of the ROD. A post-injection groundwater and soil vapor assessment was conducted between December 2008 and April 2009 to verify the effectiveness of the ZVI treatment (Alliance, 2010). The risk assessment completed during the treatability study demonstrated that the IR-71 East plume did not require treatment to address VOCs in groundwater (Alliance, 2010). Post-ROD groundwater monitoring for metals and VOCs is currently ongoing under the BGMP.

In total, approximately 237 loose cubic yards of soil was excavated from six hotspot areas in Parcel D-1 to address PAH contamination in soil. Four of the hotspot areas were removed during the first phase of the RA conducted between August 2010 and May 2011. At that time, two of the hotspot areas were inaccessible because they were located within an active radiological screening yard. The two remaining hotspot areas were removed during the second phase of the RA conducted between May 2013 and July 2013, when the radiological screening yard was inactive. All excavated soil was disposed of off site and the excavations were backfilled with clean imported soil (ERRG, 2011 and 2014c). One soil stockpile, totaling 75 cubic yards, identified in the RD was also removed and disposed of off site (ERRG, 2011).

Radiological remediation was performed in two phases. Phase I, completed in 2014, included radiological remediation and surveys of the northern portion of Parcel D-1, including Gun Mole Pier, South Pier, Buildings 274 and 383, former building sites 313/313A/322, and a portion of the storm drain and sanitary sewer system. Phase I included removal of 18,320 cubic yards of soil from 12,957 linear feet of sanitary sewer and storm drain lines (Shaw Environmental & Infrastructure, Inc., 2014a). Phase II included

radiological remediation and surveys of the remainder of Parcel D-1 (i.e., the southern portion of Parcel D-1) (Gilbane Federal, 2018a).

Durable covers, consisting of a combination of repaired and newly constructed asphalt pavement covers, existing building foundations, and riprap stabilization, have been constructed over the Phase I portion of Parcel D-1 (APTIM, 2018a). The existing asphalt pavement was repaired, where possible, using a combination of crack treatment, patching, and thin asphalt overlays to restore the integrity of the cover. A new asphalt pavement cover, consisting of 4 inches of aggregate base course overlain by 2 inches of asphaltic concrete, was installed over areas of the site where existing asphalt pavement was nonexistent or unrepairable. Existing concrete building foundations were restored by sealing cracks and patching openings to prevent access to the underlying soil. Degraded sections of the existing seawall were stabilized by installing riprap-filled gabion baskets in the void spaces adjacent to the seawall prior to constructing the asphalt pavement cover over the areas. A durable cover consisting of 1 foot of riprap overlying a layer of filter fabric was constructed over several small areas of eroded soil near the ends of the piers.

During Phase II, durable covers are planned to be constructed over the remaining portion of Parcel D-1 in the same manner as during Phase I described above, in accordance with the Parcel D-1 Remedial Action Work Plan (RAWP) (CB&I Federal Services LLC, 2014 and 2016).

3.3.4.2. LTM and Maintenance Activities

Durable Cover Maintenance and IC Compliance

Construction of the Parcel D-1 durable covers is currently in progress. As a result, a RACR has not been published at this time. However, an O&M Plan was developed for Parcel D-1 that describes the long-term maintenance requirements for the durable covers (APTIM, 2018a). The inspection, maintenance, and monitoring program has not been formally implemented for the Parcel D-1 durable covers because the cover construction is incomplete.

Groundwater Monitoring

Groundwater monitoring is conducted throughout HPNS under the BGMP (CE2-Kleinfelder JV, 2011b and 2012c; Trevet, Inc., 2017a). The BGMP includes quarterly monitoring of groundwater elevations to evaluate the direction and gradient of groundwater flow and sampling and analysis of COCs at varying frequencies. Periodic monitoring reports are published that describe the monitoring results and compare the results to the RGs to verify the RAOs for groundwater are being met.

For Parcel D-1, the COCs identified in groundwater are arsenic and VOCs. The list of specific VOCs is presented in the ROD (Navy, 2009c). In 2012, the VOC monitoring program at Parcel D-1 was discontinued at most monitoring wells because concentrations were less than the RGs and were stable or decreasing (CE2-Kleinfelder JV, 2012b). After 2012, the monitoring program continued to include the analysis of metals, as well as the analysis of VOCs at one monitoring well at Parcel D-1. In May 2017, no COCs exceeded their respective RGs at Parcel D-1 (Trevet, Inc., 2018).

The current monitoring program includes semiannual collection of groundwater samples, for analysis of metals, from three monitoring wells (IR17MW13A, IR22MW16A, and IR55MW02A) near the San Francisco Bay margin. These wells are monitored to ensure that COCs in groundwater do not migrate to San Francisco Bay at concentrations that adversely impact ecological receptors. Additionally, a groundwater sample is collected for analysis of VOCs from one monitoring well (IR71MW20A) to monitor VOC concentrations in the IR-71 East plume.

No COCs have been reported at concentrations exceeding their respective RGs or TLs in groundwater since 2004 (Trevet, Inc., 2018). The RAOs have been met for Parcel D-1. Current monitoring of these wells will continue in accordance with the RAMP (ChaduxTt, 2011d) and subsequent modifications made under the BGMP.

3.3.5. Parcel D-2

3.3.5.1. RA Activities and Implementation of ICs

The ROD for Parcel D-2 was finalized in August 2010 (Navy, 2010a). The ROD concluded that no further action was necessary for Parcel D-2. Radiological remediation was performed in 2009 as part of a basewide TCRA (Navy, 2006). In total, 1,988 linear feet of trench and 1,434 cubic yards of soil were excavated; approximately 45 cubic yards of soil was disposed of off site as LLRW (TtEC, 2011c). One radiologically impacted building (Building 813) was screened and remediated. All radiological work is currently being reviewed to determine if current site conditions are compliant with the RAOs.

3.3.5.2. LTM and Maintenance Activities

No LTM and maintenance activities are required at Parcel D-2. Parcel D-2 was transferred out of federal ownership to the OCII in late 2015.

3.3.6. Parcel E

3.3.6.1. RA Activities and Implementation of ICs

The RD for Parcel E was started in 2014 and included several pre-design investigations, the last of which was completed in 2015. The Navy published the Final RD Package for Parcel E, which describes the basis of design for the final remedy, in April 2018 (Construction Engineering Services, LLC [CES], 2018a). The remedy components for each contaminated medium are described below.

- **Soil, Soil Gas, and Shoreline Sediment:** The selected remedy for soil, soil gas, and shoreline sediment consists of (1) removal and disposal of contaminated soil in selected areas (referred to as Tier 1, Tier 2, and TPH locations[2]) that contain nonradioactive chemicals (including metals, SVOCs, PCBs, and TPH[3]) at concentrations exceeding risk-based levels, as well as separation and disposal of materials and soil with radiological contamination found in these areas; (2) closure of remaining portions of the steam and fuel line system; (3) construction of a durable cover consisting of 2 feet of soil over future open space areas; (4) construction of a durable cover consisting of new or restored asphalt or concrete over areas that will be part of the future Mixed-Use District; (5) implementation of SVE at Building 406 to treat VOC contamination in soil and soil gas; (6) soil gas monitoring at VOC plumes, the IR-12 debris removal area, and in future mixed-use redevelopment areas where VOCs are present in soil; (7) removal and disposal of contaminated shoreline sediment and installation of shoreline protection materials to prevent exposure to remaining contaminants in shoreline sediment; and (8) ICs to restrict specific land uses and activities.
- **Groundwater:** The selected remedy for groundwater consists of (1) treatment of VOCs in groundwater through injection of a biological amendment, (2) construction of a below-ground barrier in IR-02 to limit migration of groundwater contaminants into San Francisco Bay, (3) MNA, and (4) ICs to restrict specific land uses and activities.
- **NAPL at IR-03:** The selected remedy for NAPL at IR-03 consists of (1) removal or treatment of the NAPL source at IR-03, (2) construction of a below-ground barrier to limit migration of NAPL and contaminated groundwater into San Francisco Bay, (3) treatment of VOC and TPH contamination in groundwater through injection of a biological amendment, (4) MNA, and (5) ICs to restrict specific land uses and activities.
- **Radiologically Impacted Media:** The selected remedy for radiologically impacted media outside of IR-02 and IR-03 consists of (1) decontamination or dismantling and offsite disposal of radiologically impacted structures; (2) excavation and offsite disposal of radiologically impacted storm drain and sanitary sewer lines and soil from adjacent impacted areas; and (3) survey and obtain unrestricted release of buildings, former building sites, and radiologically impacted areas. The selected remedy for radiologically impacted media at IR-02 and IR-03 consists of (1) a radiological scan of the entire area to a depth of at least 1 foot; (2) separation and disposal of materials and soil with radiological contamination found during the surveys; (3) construction of a 2-foot-thick soil cover to prevent exposure to remaining contaminants (the soil cover at IR-02 and IR-03 would also include a demarcation layer to mark the boundary between the existing surface and the soil cover); (4) ICs (specific to radionuclides) to restrict specific land uses and activities; and (5) monitoring of groundwater to demonstrate, consistent with the findings of previous radiological investigations, that radionuclides are not present in groundwater at activity levels that are both statistically significant and pose an unacceptable risk to human health and the environment.

[2] Tier 1 locations contain COCs at concentrations greater than 10 times the RGs. Tier 2 locations contain COCs at concentrations greater than 5 times the RGs. TPH locations contain TPH (commingled with CERCLA-regulated chemicals) at concentrations exceeding the petroleum source criterion (3,500 milligrams per kilogram).

[3] These chemical groups comprise the Tier 1, Tier 2, and TPH locations proposed for removal. Dioxins and furans are not included in this list because these chemicals are not found at concentrations greater than 5 times the RGs.

Figure 8 identifies the locations of the major remedy components at Parcel E. The RA at Parcel E will be implemented in phases. At the time this report was prepared, the RAWPs were being prepared for the first two phases of the RA, and RA fieldwork is planned to begin in late 2018. The following paragraphs briefly describe the planned activities during the first three phases of the RA.

Phase 1 RA for Parcel E

The Phase 1 RA for Parcel E will consist of the following activities:

- Remove and dispose of contaminated soil in Tier 1, Tier 2, and TPH locations (except for locations within the proposed shoreline protection)
- Perform supplemental soil gas monitoring at the debris removal area within IR-12 and in areas planned for mixed use where concerns continue about residual VOCs in soil
- Investigate and close remaining portions of the steam and fuel line system to address potential sources of contamination
- Treat VOC contamination in groundwater at inland plumes using injected biological nutrients (or potentially a mixture of biological nutrients and ZVI) to accelerate the breakdown of VOCs to less toxic compounds

The Phase 1 RA also includes excavation of VOCs in vadose zone soil at two locations (IR-04 and south of Building 406) that are adjacent to planned excavations at Tier 1, Tier 2, and TPH locations. The Phase 1 RA also includes plans for installing an SVE system to address VOCs in the vadose zone under Building 406. However, contingency excavation may be implemented under Building 406 if the structure is demolished as part of the redevelopment process and the contingency excavation can be coordinated with the planned excavation south of Building 406. The Phase 1 RAWP for Parcel E was started in 2017, and the Draft RAWP was submitted in June 2018 (APTIM, 2018c).

Phase 2 RA for Parcel E

The Phase 2 RA for Parcel E, which focuses on IR-03, will consist of the following activities:

- Treat mobile NAPL at IR-03 via in-situ solidification/stabilization
- Construct a slurry wall surrounding nonmobile NAPL and related groundwater contamination at IR-03
- Remove and dispose of contaminated material (that contains NAPL and soil with elevated concentrations of TPH) on the bay-side of the slurry wall at IR-03
- Construct shoreline protection features at IR-03

The Phase 2 RAWP for Parcel E was started in 2017, and the draft RAWP is expected to be published in September 2018.

Phase 3 RA for Parcel E

The Phase 3 RA for Parcel E will consist of the following activities:

- Remove and dispose of contaminated soil in Tier 1, Tier 2, and TPH locations within (or adjacent to) the proposed shoreline protection
- Construct a slurry wall along the shoreline at IR-02 Northwest
- Construct shoreline protection features at the rest of Parcel E (outside of IR-03)

The Phase 3 RAWP for Parcel E was started in 2018 but was not completed at the time the fourth five-year review was published. The remaining RA phases will include final radiological remediation and surveys and construction of durable covers in the upland areas of Parcel E.

Future RA Work

Future RA activities will include the following activities:

- Perform radiological surveys and remediation in structures, former building sites, and buried storm drain and sewer lines (located outside of IR-02 and IR-03) that were not completed during previous TCRA
- Perform radiological surveys and remediation throughout IR-02 and IR-03 that include (1) scanning the entire area for radioactivity to a depth of at least 1 foot; (2) separating and disposing of materials and soil with radiological contamination found during the surveys; and (3) constructing a 2-foot-thick soil cover that includes a demarcation layer to mark the boundary between the existing surface and the soil cover
- Construct durable covers (consisting of either asphalt or soil) throughout Parcel E to prevent exposure to remaining contaminants in soil (the soil cover at IR-03 and the northwest portion of IR-02 would also include a protective liner to minimize water seeping into contaminated soil)

ICs, including restricted and prohibited activities, are currently being developed for Parcel E to prevent exposure to areas where potential unacceptable risk is posed by COCs in soil, soil gas, and groundwater and by radionuclides in soil. The LUC RD for Parcel E addresses the ICs and land use restrictions required by the ROD (CES, 2018b). The IC performance objectives will be met by site access controls until Parcel E is transferred out of Navy ownership.

3.3.6.2. LTM and Maintenance Activities

The LTM and maintenance program will be detailed in the post-construction O&M Plan for Parcel E and will be implemented following completion of all RA construction activities. Groundwater monitoring is the only monitoring activity currently performed in Parcel E, as described below.

Groundwater at Parcel E is currently monitored in support of the selected remedy as specified in the ROD (Navy, 2013d), with monitoring recommendations provided in the Final FS Report (ERRG, 2012b). The Navy is currently developing a RAMP for Parcel E, which will define the LTM requirements and, when finalized, be incorporated into the BGMP.

For Parcel E, the COCs were identified as metals, VOCs, and TPH (Navy, 2013d). The ROD also lists some metals, PCBs, and pesticides as COPECs. Additionally, groundwater samples are analyzed for radionuclides at Parcel E to demonstrate that they are not present in groundwater at activity levels that are both statistically significant and pose an unacceptable risk to human health and the environment.

Groundwater monitoring is currently conducted throughout HPNS under the BGMP (CE2-Kleinfelder JV, 2011b and 2012c; Trevet, Inc., 2017a). The BGMP includes periodic monitoring of groundwater elevations to evaluate the direction and gradient of groundwater flow and sampling and analysis of COCs at varying frequencies. Periodic monitoring reports are published that describe the monitoring results.

At Parcel E, the BGMP includes collection of groundwater samples from 27 wells for analysis of COCs, including metals, VOCs, SVOCs, pesticides, PCBs, TPH, MNA parameters (including dissolved gasses, total organic carbon, anions, and alkalinity), silica, and radionuclides (including cesium-137, radium-226, and strontium-90). Currently, groundwater elevation measurements are collected at 68 wells at Parcel E-2 wells on a regular basis using data-logging pressure transducers (Trevet, Inc., 2017a). Metals (copper, nickel, and zinc), naphthalene, TCE, VC, and total TPH historically exceed their respective RGs in monitoring wells at Parcel E.

Annual monitoring will continue at Parcel E until the RAMP is finalized, at which point the LTM requirements will be incorporated into the BGMP.

3.3.7. Parcel E-2

3.3.7.1. RA Activities and Implementation of ICs

The RD for Parcel E-2 was started in 2012 and included two pre-design investigations, the last of which was completed in 2013. The Navy published the Final RD Package, which describes the basis of design for the final remedy, in August 2014 (ERRG, 2014f). The remedy components for each contaminated medium are described below.

- **Soil and Shoreline Sediment:** The selected remedy for soil and shoreline sediment consists of (1) removal and disposal of contaminated soil and sediment in selected areas that contain nonradioactive chemicals (including metals, SVOCs, PCBs, and TPH) at concentrations exceeding risk-based levels, as well as separation and disposal of materials and soil with radiological contamination found in these areas; (2) radiological surveys followed by separation and disposal of radiologically contaminated materials and soil; (3) construction of a durable cover consisting of a 2-foot soil cover and a protective liner (comprising a geomembrane with an overlying geocomposite drainage layer) over upland areas; (4) construction of a durable cover consisting of a 4-foot soil cover over wetland areas; (5) construction of a durable cover consisting of riprap revetment along shoreline areas; and (6) ICs to restrict specific land uses and activities.
- **Landfill Gas:** The selected remedy for landfill gas consists of (1) removal and treatment of landfill gas to prevent it from moving beyond the Parcel E-2 boundary, (2) monitoring of landfill gas concentrations to track the effectiveness of the landfill gas treatment system, and (3) ICs to restrict specific land uses and activities.
- **Groundwater:** The selected remedy for groundwater consists of (1) construction of below-ground barriers to limit migration of groundwater contaminants from the landfill to San Francisco Bay, (2) MNA, and (3) ICs to restrict specific land uses and activities.

Figure 9 identifies the locations of major remedy components at Parcel E-2. The RA at Parcel E-2 is being implemented in phases. At the time this report was prepared, the first phase of the RA had been completed, the second phase of the RA was being implemented, and the RAWP for the third (and final) phase of the RA was being prepared. The following paragraphs briefly describe the three phases of the RA.

Phase 1 RA for Parcel E-2

The Phase 1 RA for Parcel E-2 consisted of the following activities:

- Remove and dispose of contaminated soil and sediment in hotspot areas
- Install a slurry wall along the Parcel E-2 shoreline (referred to as the “nearshore slurry wall”)

The Phase 1 RA for Parcel E-2 was initiated in 2014 and was completed in 2017 (Gilbane Federal, 2018d). Approximately 39,004 bank cubic yards of contaminated soil was excavated, screened, and removed from the hotspot areas. In addition, approximately 5,324 bank cubic yards of soil and debris was excavated prior to installation of the nearshore slurry wall, and another 3,499 bank cubic yards of material was trenched during installation of the slurry wall. In total, 49 10-cubic-yard roll-off bins of LLRW were generated during the project, and 99 radioactive commodities were recovered and removed. Approximately 1,237 linear feet of nearshore slurry wall was installed to prevent groundwater located bayward of the landfill waste from contacting surface water in San Francisco Bay.

Phase 2 RA for Parcel E-2

The Phase 2 RA for Parcel E-2 consists of the following activities:

- Excavate soil, shoreline sediment, and solid waste and consolidate it on site
- Perform radiological surveys throughout Parcel E-2 and separate and dispose of materials and soil with radiological contamination found during the surveys
- Install foundation layer for soil cover over all of Parcel E-2
- Install shoreline revetment
- Install slurry wall along the western boundary of Parcel E-2 (referred to as the "upland slurry wall")

The Phase 2 RA for Parcel E-2 was initiated in 2016 and is scheduled for completion in 2018.

Phase 3 RA for Parcel E-2

The Phase 3 RA for Parcel E-2 will consist of the following activities:

- Install a soil cover over all of Parcel E-2, with a protective liner
- Install landfill gas extraction and treatment system
- Construct surface water controls, including new tidal and freshwater wetlands
- Install cover vegetation

The Phase 3 RAWP for Parcel E-2 was started in 2017, and the Draft RAWP was submitted in February 2017 (KEMRON Environmental Services, Inc., 2018).

3.3.7.2. LTM and Maintenance Activities

The LTM and maintenance program will be detailed in the post-construction O&M Plan for Parcel E-2 and will be implemented following completion of all RA construction activities. Monitoring activities are currently conducted on an interim basis for several components of the remedy and include monitoring of methane gas, inspection and maintenance of the interim landfill cap, and monitoring of stormwater discharge. Additionally, groundwater monitoring is performed as part of the BGMP.

Methane Gas Monitoring

Landfill gas is monitored on a monthly basis under the Interim Landfill Gas Monitoring and Control Plan (MCP) (ITSI and Tetra Tech EM Inc. [TtEMI], 2004). The purpose of landfill gas monitoring is to verify the gas collection and control system is preventing landfill gas from migrating beyond the Parcel E-2 boundary and is effectively reducing emissions of methane and nonmethane organic compounds (NMOCs) in accordance with the RAOs. Monitoring results between 2013 and 2018 indicated that all methane and NMOC concentrations were less than their corresponding action levels, except for a methane exceedance

at one monitoring location during March 2015 (CKY, Inc., 2014a, 2014b, 2014c, 2014e, 2014f, 2015a, 2015b, 2015c, 2015d, 2015e, 2015f, 2015g, 2015j, 2016a, 2016b, 2016c, 2016d, 2016e, 2016f, 2016g, 2016i, 2016j, 2016k, 2016l, 2017a, 2017b, 2017c, 2017d, 2017e, 2017e, 2017f, 2017h, 2017i, 2018a, and 2018b). In response to the March 2015 exceedance, active gas extraction was initiated and follow-up monitoring was performed in accordance with the MCP.

Landfill Cap Inspection and Maintenance

Inspection and maintenance of the interim landfill cap is conducted in accordance with a site-specific O&M Plan (TtEMI, 2003b). The plan describes the procedures necessary to ensure the integrity of the interim landfill cap. The plan also includes emergency response procedures, which are to be followed in the event of a flood, major storm event, earthquake, or fire (TtEMI, 2003). O&M procedures associated with the closed landfill include (1) irrigating the landfill cap to maintain the vegetative cover and (2) mowing the vegetative cover on and adjacent to the cap to reduce potential fire hazards and prevent the growth of large shrubs and trees whose root structure could penetrate the cap. General site inspections are performed quarterly to assess the condition of vegetation growth on the cap, verify that no erosion or settlement of the soil cover has occurred, assess the presence of burrowing animals in the soil cover, and ensure that all components of the cap are functioning properly. Vegetative cover inspections are performed semiannually to ensure that vegetation growing on the interim cap is sufficient to prevent soil erosion without damaging the underlying geosynthetic membrane, and to assess the need for mowing vegetation on and adjacent to the cap. Maintenance activities performed during this five-year review period include mowing the vegetative cover twice per year and routinely filling animal burrows. Results of the O&M inspections (CKY, Inc., 2014d, 2015i, 2016h, and 2017g) confirm that the interim landfill cap is being properly maintained in accordance with the O&M Plan.

Stormwater Discharge Monitoring

Compared with the flat-lying terrain at most other HPNS areas, Parcel E-2 has more vertical relief—ranging in elevation from about 30 feet above msl to sea level at the shoreline. Consequently, there is an increased potential for erosion and sediment transport by flowing stormwater. During implementation of the Phase 1 and Phase 2 RA activities completed at Parcel E-2 to date, stormwater monitoring and management has been performed in accordance with the RAWPs (ITSI Gilbane Company, 2014a; CB&I Federal Services LLC, 2016b). Following completion of the RA, stormwater monitoring at Parcel E-2 will be performed in accordance with the RAMP (ERRG, 2014f).

Groundwater Monitoring

The RAOs for groundwater at Parcel E-2 were established based on COCs and COECs, potential receptors and exposure scenarios, and human health and ecological risk (Navy, 2012). In Parcel E-2, the COCs in groundwater are metals (including hexavalent chromium), VOCs, SVOCs, pesticides, PCBs, and TPH. Due to potential hazards from some analytes to aquatic life in San Francisco Bay, un-ionized ammonia, cyanide, sulfide, copper, lead, zinc, total PCBs, and total TPH have been added to the sampling program as COPECs

and are monitored to verify the protectiveness of the remedy (Navy, 2012). The ROD states that groundwater does not appear to have been impacted by radionuclides at activity levels that warrant RA. However, since Parcel E-2 required an RA for other COCs, groundwater monitoring includes analysis of radionuclides to verify the conclusions of the radiological addendum (Navy, 2012).

Groundwater monitoring is conducted throughout HPNS under the BGMP (CE2-Kleinfelder JV, 2011b and 2012c; Trevet, Inc., 2017a). The BGMP includes collection of groundwater samples from 17 wells for analysis of metals, VOCs, SVOCs, pesticides, PCBs, TPH, ammonia, cyanide, and radionuclides (including cesium-137, radium-226, and strontium-90). Of the 17 wells, 16 wells are sampled semiannually and 1 well is sampled biennially. Metals, VOCs, and total TPH consistently exceed their RGs in monitoring wells in Parcel E-2.

Currently, groundwater elevation measurements are collected on a regular basis at 24 wells at Parcel E-2 using data-logging pressure transducers (Trevet, 2017a). The BGMP includes periodic monitoring of groundwater elevations to evaluate the direction and gradient of groundwater flow and sampling for various COCs at varying frequencies. Periodic monitoring reports are published that describe the monitoring results and compare the results to the RGs to verify the RAOs for groundwater are being met.

Current monitoring of these wells will continue in accordance with the RAMP (Navy, 2012) and subsequent modifications made under the BGMP.

3.3.8. Parcel F

A ROD for Parcel F has not yet been published. Post-ROD RA and LTM and maintenance activities will be discussed and evaluated in future five-year review reports.

3.3.9. Parcel G

3.3.9.1. RA Activities and Implementation of ICs

The Navy published the Final RD Package for Parcel G, which describes the basis of design for the final remedy, in October 2010 (ChaduxTt, 2010c). The Final RD package was revised in January 2011 to include an updated LUC RD (ChaduxTt, 2011b). The remedy components for each contaminated medium are described below.

- **Soil and Soil Gas:** The selected remedy for soil and soil gas consists of (1) excavation of soil hot spots and removal of soil stockpiles where COC concentrations exceed RGs; (2) construction of a durable cover consisting of a minimum 2-inch-thick existing asphaltic concrete pavement restored by installation of an asphalt seal coat or asphaltic concrete overlay (in areas with repairable existing pavement); (3) construction of a durable cover consisting of 2 inches of asphaltic concrete placed over new or existing aggregate base course (in areas with heavily degraded existing pavement); (4) restoration of cracks and penetrations in building foundations; (5) soil gas surveys to evaluate vapor intrusion risks and assess the need for additional remedial activities or ARICs; and (6) ICs to restrict specific land uses and activities.

- **Groundwater:** The selected remedy for groundwater consists of (1) treatment of VOCs in groundwater at IR-09, IR-33, and IR-71 through ISB or ZVI; (2) minimizing the migration of metals in groundwater into San Francisco Bay, (3) MNA for remaining VOCs and metals in groundwater, and (4) ICs to restrict specific land uses and activities.
- **Radiologically Impacted Media:** The selected remedy for radiologically impacted media consists of (1) decontamination or dismantling and offsite disposal of radiologically impacted structures; (2) excavation and offsite disposal of radiologically impacted storm drain and sanitary sewer lines and soil from adjacent impacted areas; and (3) surveys to obtain unrestricted release of buildings, former building sites, and radiologically impacted areas.

Figure 10 identifies the locations of major remedy components at Parcel G. Completion of the RA activities in Parcel G occurred in phases. Several of the soil stockpiles at Parcel G were removed as part of initial removal actions or RA activities that were conducted in the vicinity of the stockpiles. An RA to remove soil hot spots and the remaining stockpiles was conducted between August 2010 and May 2011 (ERRG, 2011). A soil gas study was completed in 2013 (SES, 2013); results from the study were used to evaluate potential risk to human health via vapor intrusion and to assess the need for ARICs for VOC vapors. Construction of the durable covers was performed between January 2013 and July 2013 (ARCADIS U.S., Inc. [ARCADIS], 2014a).

The pre-ROD groundwater treatability study included an assessment of the risks posed to human health and the environment from metals and VOCs in five separate groundwater plumes within Parcels D-1 and G (Alliance, 2010). Three of these plumes (known as the IR-09 North, IR-09 South, and IR-33 plumes) are present entirely within Parcel G, and two of the plumes (known as the IR-71 West and IR71 East plumes) are present in both Parcels D-1 and G. The treatability study concluded that two plumes required treatment with ZVI to address VOCs in groundwater, including TCE at the IR-09 North plume and chloroform at the IR-71 West plume. The risk assessment completed during the treatability study demonstrated that the other plumes (including the IR-33 plume) did not require treatment to address metals or VOCs in groundwater. To treat the two VOC plumes, approximately 148,000 pounds of ZVI was injected into 97 groundwater injection points in IR-09 and IR-71 between October and December 2008, prior to the publication of the ROD. A post-injection groundwater and soil vapor assessment was conducted between December 2008 and April 2009 to verify the effectiveness of the ZVI treatment (Alliance, 2010). A pickling vault located at IR-09 was removed in 2010 to address elevated concentrations of chromium VI in groundwater, and approximately 31,000 pounds of ZVI was placed in the excavation following the removal (TtEC, 2010). Based on the treatability study risk assessment results, concentrations of metals in groundwater do not pose a potential risk to future construction workers at Parcel G and do not exceed criteria for protection of ecological receptors in San Francisco Bay (Alliance, 2010). Post-ROD groundwater monitoring for VOCs and metals is currently ongoing under the BGMP.

In total, approximately 66 loose cubic yards of soil was excavated from two hotspot areas in Parcel G to address lead and PAH contamination. The excavated soil was disposed of off site, and the excavations were backfilled with clean imported soil (ERRG, 2011). Two soil stockpiles identified in the RD, totaling 20 cubic yards, were also removed and disposed of off site (ERRG, 2011).

An asphalt cover was constructed over all exterior (non-building) portions of Parcel G. The asphalt cover consists of a combination of restored areas of the existing asphalt pavement (in areas where the existing asphalt pavement was repairable) and newly installed asphalt pavement (in areas where the existing asphalt pavement was heavily degraded). The existing asphalt was restored, when possible, by either applying an asphalt seal coat or installing a 2-inch asphaltic concrete overlay. New asphalt pavement, consisting of 2 inches of asphaltic concrete overlying an aggregate base course, was installed over the portions of Parcel G where the historical pavement layer was not present at or near the ground surface. Drainage features such as swales, diversion berms, catch basins, and storm drain pipes were incorporated into the asphalt cover to convey stormwater off site (ARCADIS, 2014a).

Concrete building foundations and concrete pads were restored by filling cracks and penetrations with non-shrink grout to prevent access to the underlying soil (ARCADIS, 2014a).

Radiological remediation at Parcel G began in 2007 (under a basewide TCRA [Navy, 2006]), and continued as part of the RA. In total, 50,688 cubic yards of soil was removed from 23,166 linear feet of sanitary sewer and storm drain lines; approximately 2,828 cubic yards of soil was disposed of off site as LLRW. Nine radiologically impacted buildings (351, 351A, 364, 365, 366, 401, 408, 411, and 439) and one former building site (317/364/365) were screened and remediated (TtEC, 2011b). All radiological work is currently being reviewed to determine if current site conditions are compliant with the RAOs.

Land use restrictions were designed to limit exposure of future landowners or users of the property to hazardous substances and to maintain the integrity of the remedy. The LUC objectives will be met by controlling access to the property. The activity and land use restrictions described in the LUC RD Report (ChaduxTt, 2011b) will be incorporated into the Quitclaim Deed and Covenant to Restrict Use of Property and will take effect upon transfer to the OCII and issuance of those documents.

3.3.9.2. LTM and Maintenance Activities

Long-term maintenance requirements are described in the O&M Plan for Parcel G (ARCADIS, 2014b) and a letter amendment to the O&M Plan (Navy, 2015b). The O&M Plan includes inspection items that are similar to those described for Parcels B-1 and B-2 (see Section 3.3.2.2).

Durable Cover Maintenance and IC Compliance

Quarterly inspections were conducted in October 2013, February 2014, July 2014, and November 2014 during the first year of the post-RA O&M period (ARCADIS, 2015). The Navy did not conduct formal inspections of Parcel G in 2015 (i.e., the second year of long-term monitoring and maintenance); however,

the Navy did perform informal inspections and maintenance to ensure the integrity of the remedy components. An annual inspection was conducted in June 2016 during the third year of O&M (ARCADIS, 2016) and an annual inspection was conducted in October 2017 during the fourth year of O&M (IEJV, 2018a). In 2017, O&M activities were realigned to match those described for IR-07/18 in Section 3.3.1.2.

Throughout the first 4 years of LTM and maintenance, inspections generally concluded that the remedies remain intact and in good condition and they are functioning as intended. Minor issues encountered included several small areas of damage to the asphalt cover due to weed growth through the cover, ponded water accumulating in high-traffic areas, and isolated areas of cover settlement due to contractor activities. The damaged asphalt cover was repaired in each area by removing weeds (if present), preparing the subgrade, and installing asphalt or concrete patches to restore the cover. A drainage pipe was installed in the area where the asphalt cover was damaged by excessive ponding to prevent future damage due to ponding. All items were addressed in a timely manner and in accordance with the O&M Plan (ARCADIS, 2014b).

In 2014, 2015, and 2017, the Navy conducted inspections to verify compliance with the ICs applicable to Parcel G. The inspection reports certify that the ICs related to land use and activity restrictions are being implemented in accordance with the LUC RD (ChaduxTt, 2011b).

Groundwater Monitoring

For Parcel G, the COCs in groundwater are metals and VOCs. The list of specific metals and VOCs is presented in the ROD (Navy, 2009b). Groundwater monitoring is conducted throughout HPNS under the BGMP (CE2-Kleinfelder JV, 2011b and 2012b; Trevet, Inc., 2017a). The BGMP includes periodic monitoring of groundwater elevations to evaluate the direction and gradient of groundwater flow and sampling and analysis of COCs at varying frequencies. Periodic monitoring reports are published that describe the monitoring results and compare the results to the RGs to verify that the RAOs for groundwater are being met.

At Parcel G, the BGMP includes collection of groundwater samples from four wells for analysis of VOCs (with three wells sampled semiannually and one well sampled biennially). Carbon tetrachloride, chloroform, and PCE have historically exceeded their respective RGs in Parcel G groundwater (Trevet, Inc., 2018). In 2012, monitoring of chromium VI was discontinued from the BGMP because the concentrations were an order of magnitude less than the TL and were stable or decreasing (CE2-Kleinfelder JV, 2012b).

The Navy conducted an investigation in August 2017 to evaluate whether PFAS are present in groundwater at IR-09 within Parcel G as a result of historical uses (Trevet, Inc., 2018). Monitoring wells IR09MW61A, IR09MW62A, and IR09MW31A1 were analyzed for PFAS compounds, including PFOA, PFOS, combined PFOA and PFOS, PFBS, and an additional 11 PFAS compounds by EPA Method 537 Modified. PFOA was detected in two monitoring wells (IR09MW61A and IR09P040A) at concentrations less than the FSC

of 70 ng/L. PFOS was detected in all three monitoring wells at concentrations less than the FSC of 70 ng/L. Combined PFOA and PFOS were detected in two monitoring wells (IR09MW62A and IR09P040A) at concentrations less than the FSC of 70 ng/L. PFBS was detected in two monitoring wells (IR09P040A and IR09MW61A) at concentrations significantly less than the FSC of 380 ng/L during the PFAS groundwater investigation. Concentrations of PFOA, PFOS, combined PFOA and PFOS, and PFBS were less than their respective FSCs during the PFAS groundwater investigation. Based on available data, groundwater at IR-09 has not been affected by PFAS.

Between 2013 and 2016, the BGMP at Parcel G included quarterly measurements of groundwater elevation at 20 wells. Since 2017, groundwater elevation measurements have been collected on a regular basis at 20 wells at Parcel G using data-logging pressure transducers (Trevet, 2017a).

Current monitoring of the Parcel G wells will continue in accordance with the RAMP (ChaduxTt, 2011b) and subsequent modifications made under the BGMP.

3.3.10. Parcels UC-1 and UC-2

3.3.10.1. RA Activities and Implementation of ICs

The Navy published the Final RD Package for Parcels UC-1 and UC-2, which describes the basis of design for the final remedy, in December 2010 (ChaduxTt, 2010e). The remedy components for each contaminated medium are described below.

- **Soil and Soil Gas:** The selected remedy for soil, sediment, and soil gas consists of (1) construction of a durable cover consisting of a 2-foot soil cover over vegetated slopes in Parcel UC-2; (2) construction of a durable cover consisting of new or repaired asphaltic concrete for roadways in Parcels UC-1 and UC-2; (3) conducting soil gas surveys to evaluate potential vapor intrusion risks and assess the extents of the ARICs for VOC vapors; and (4) ICs to restrict specific land uses and activities.
- **Groundwater:** The selected remedy for groundwater consists of (1) MNA for VOCs in groundwater in Parcel UC-2 and (2) ICs to restrict specific land uses and activities.
- **Radiologically Impacted Media:** The selected remedy for radiologically impacted media consists of (1) decontamination or dismantling and offsite disposal of radiologically impacted structures; (2) excavation and offsite disposal of radiologically impacted storm drain and sanitary sewer lines and soil from adjacent impacted areas; and (3) survey and obtain unrestricted release of buildings, former building sites, and radiologically impacted areas.

Figures 11 and 12 identify the locations of major remedy components at Parcels UC-1 and UC-2. The RAs for Parcels UC-1 and UC-2 were implemented concurrently. Construction of the remedies in Parcels UC-1 and UC-2 began in May 2012 and were completed in September 2012 (ERRG, 2013c). The RA included removal of the top 2 feet of soil from the sloped areas above Fisher and Spear Avenues and replacement with clean imported soil to serve as a durable cover. The soil cover was stabilized with hand-planted native species. The RA also included repair and replacement of damaged portions of the roadways, sidewalks, and gutters

along Fisher and Spear Avenues to establish a contiguous durable cover over hardscape areas. Drainage features were also constructed to improve the conveyance of stormwater off site. Groundwater monitoring wells at Parcel UC-2 were incorporated into the cover construction, and drainage features were included in the construction to convey storm water off site. Soil gas studies were completed in 2013 and 2014 (SES, 2013; ERRG, 2014g); results from the studies were used to evaluate potential risks to human health via vapor intrusion and to assess the need for ARICs for VOC vapors.

Radiological removals began in 2004 (under a basewide TCRA), and continued and were completed as part of the RA. In total, 20,680 cubic yards of soil was removed from 6,407 linear feet of sanitary sewer and storm drain lines; approximately 876 cubic yards of soil was disposed of off site as LLRW (TtEC, 2011a). One radiologically impacted building (819) at Parcel UC-1 was screened and remediated (TtEC, 2011a). All radiological work is currently being reviewed to determine if current site conditions are compliant with the RAOs.

3.3.10.2. LTM and Maintenance Activities

Durable Cover Maintenance and IC Compliance

Long-term maintenance requirements are detailed in the O&M Plan for Parcels UC-1 and UC-2 (ERRG, 2013d). The O&M Plan includes inspection items that are similar to those described for Parcels B-1 and B-2 (see Section 3.3.2.2).

The Navy conducted quarterly inspections and maintenance events for remedies in Parcels UC-1 and UC-2 in January, April, July, and October 2013 (ERRG, 2014a). The inspection frequency was reduced to semiannually following the first year of LTM and maintenance. Inspections and maintenance were performed semiannually in April and October 2014 during the second year of LTM and maintenance (ERRG, 2015d). Only a single semiannual inspection and maintenance event was performed in April 2015, because the property was transferred to OCII before the scheduled second semiannual event (ERRG, 2015d). The OCII performed inspection and maintenance events in Parcels UC-1 and UC-2 in 2016 (Geosyntec Consultants, 2016a and 2016b) in accordance with the Risk Management Plan for Parcels UC-1 and UC-2 (Geosyntec Consultants, 2015), but the Navy has no record of subsequent inspection and maintenance events. Inspections and maintenance have likely been suspended due to redevelopment construction activities. The Navy anticipates that it will receive documentation on restoration of the covers following the completion of current construction activities.

Throughout the first 3 years of LTM and maintenance, inspections generally concluded that the remedies remain intact and in good condition and they are functioning as intended. Minor issues encountered included minor damage to the asphalt cover due to heavy truck traffic, contractor activities, and weed growth, and minor areas of poor vegetation growth due to drought. Repairs made during the quarterly inspections during the first 3 years of long-term monitoring included minor maintenance items such as revegetation of poor growth areas, weed removal in sidewalk seams, and minor asphalt repairs

(ERRG 2014a, 2015d, and 2015k; Geosyntec Consultants, 2016a and 2016b). Each of these items was addressed in a timely manner and in accordance with the O&M Plan (ERRG, 2013d).

In 2013, 2014, and 2015, the Navy conducted inspections to verify continued compliance with the ICs applicable to Parcels UC-1 and UC-2. The inspection reports certify that the ICs related to land use and activity restrictions are being implemented in accordance with the LUC RD (ChaduxTt, 2010e). Parcels UC-1 and UC-2 were transferred out of federal ownership to OCII in late 2015. OCII has assumed responsibility for maintaining the durable cover remedies, performing the LUC inspections, and submitting annual O&M reports to the FFA signatories. During preparation of this five-year review, the durable covers in Parcels UC-1 and UC-2 were observed to be severely damaged due to redevelopment construction activities, as discussed in Section 5.3. The Navy understands that the covers will be restored and maintained following the completion of current construction activities.

Groundwater Monitoring

No groundwater monitoring wells are at Parcel UC-1; consequently, no groundwater monitoring is conducted at Parcel UC-1 under the BGMP. For Parcel UC-2, the COCs in groundwater are chloroform and carbon tetrachloride (Navy, 2009d). This property has been transferred to the City and County of San Francisco; however, the Navy continues to monitor groundwater under its BGMP (CE2-Kleinfelder JV, 2011b and 2012c; Trevet, Inc., 2017a). The BGMP includes quarterly monitoring of groundwater elevations to evaluate the direction and gradient of groundwater flow and sampling and analysis for COCs at varying frequencies. Periodic monitoring reports are published that describe the monitoring results and compare the results to the RGs to verify the RAOs for groundwater are being met.

The ROD for Parcel UC-2 identified natural attenuation as the remedy for VOCs in groundwater (Navy, 2009d). Groundwater samples are collected from one monitoring well (IR06MW56F) at Parcel UC-2 for analysis of VOCs (carbon tetrachloride and chloroform), metals, and MNA parameters. A soil vapor investigation conducted in 2010 did not identify any risk to human health from inhalation via vapor intrusion in the area of the identified groundwater plume. Historically, no COCs exceeded RGs in groundwater.

3.3.11. Parcel UC-3

3.3.11.1. RA Activities and Implementation of ICs

The Navy published the Final RD for Parcel UC-3, which describes the basis of design for the components of the final remedy, in early 2016 (Amec Foster Wheeler Environment & Infrastructure, Inc. [Amec Foster Wheeler], 2016a). The remedy components for each contaminated medium are described below.

- **Soil and Soil Gas:** The selected remedy for soil and soil gas consists of (1) excavation and offsite disposal of soil contaminated by metals, SVOCs, and TPH from selected areas along the railroad right-of-way (IR-52); (2) construction of a durable cover consisting of asphalt and concrete surfaces corresponding to Redevelopment Block MU-3 on the eastern portion of Parcel UC-3; (3) steam line sampling and either removal or clean and closure in place (IR-45) within Parcel UC-3; (4) soil gas survey at the IR-56 plume area and at soil areas impacted by selected SVOCs and TPH to evaluate the effectiveness of excavation remedies; (5) parcel-wide soil gas survey to determine the reduction or retention of the designated ARIC; and (6) ICs to restrict specific land uses and activities.
- **Groundwater:** The selected remedy for groundwater consists of treatment of groundwater VOCs by injection of an organic compound, MNA, and ICs.
- **Radiologically Impacted Media:** The remedy for radiologically impacted media consists of excavation and offsite disposal of radiologically impacted sewer and storm drain lines.

Figure 13 identifies the locations of major remedy components at Parcel UC-3. RA activities in Parcel UC-3 are substantially complete. The Navy implemented soil, groundwater, and soil gas remedies as part of an RA that was completed in October 2017. The activities completed under the RA included hotspot excavation, installation of durable cover, and a soil gas survey. These activities are documented in the RACR (Gilbane, 2017j).

In total, 783 cubic yards of contaminated soil was excavated from three hotspot areas in Parcel UC-3 to address metals (copper and lead), SVOCs, and TPH. In total, approximately 1,200 tons of soil was transported and disposed of at an offsite facility during the Parcel UC-3 RA.

Approximately 47,000 square feet of pavement was repaired, and another 47,000 square feet of new pavement was installed in Parcel UC-3. New pavement consisted of 4 inches of aggregate base course overlain by 4 inches of asphaltic concrete. Existing infiltration trenches, which capture and remove surface water from the surrounding paved areas, were integrated into the durable cover.

The active soil gas survey involved collection of soil gas samples from three soil gas monitoring probes installed as part of the RA. The results of the survey revealed that residual benzene contamination in soil near groundwater well IR74MW01A is generating soil gas that slightly exceeds the designated soil gas action level. The Navy is evaluating this hazard to determine if it is necessary to designate an ARIC in this area to address future inhalation and other exposure hazards.

The steam line closure component of the selected soil remedy was not performed as part of the RA because the portion of the steam line within Parcel UC-3 was not used for conveying oil, it was assessed during previous site investigations with no evidence of contamination, and it is outside of the area where previous investigations had identified waste oil impacts in the steam lines (Amec Foster Wheeler, 2016a).

The groundwater remedy was not implemented as part of the RA because historical and current TCE concentrations in groundwater at the IR-56 plume have not exceeded the RG since monitoring began in 1996 and have not exceeded the vapor intrusion criterion since the end of 2009 (Amec Foster Wheeler, 2016a).

Radiological removals were started in 2009 and completed in 2011, under a basewide TCRA and prior to the issuance of the ROD. In total, 18,024 cubic yards of soil was removed from 18,363 linear feet of sanitary sewer and storm drain lines; approximately 789 cubic yards of soil was disposed of off site as LLRW (TtEC, 2012b). All radiological work is currently being reviewed to determine if current site conditions are compliant with the RAOs.

3.3.11.2. LTM and Maintenance Activities

Durable Cover Maintenance and IC Compliance

Long-term maintenance requirements will be described in the forthcoming Final O&M Plan for Parcel UC-3. The O&M Plan will primarily address inspection and maintenance of the durable covers and implementation and monitoring of ICs.

Groundwater Monitoring

The Navy monitored groundwater at Parcel UC-3 under its BGMP (CE2-Kleinfelder JV, 2011b and 2012c; Trevet, Inc., 2017a). Groundwater has been monitored quarterly for TCE and chloroform at the only well (IR74MW01A) at IR-56 within Parcel UC-3. Historically, no COCs have exceeded their RGs in this monitoring well. The groundwater monitoring RAOs have been met in Parcel UC-3, so groundwater monitoring activities associated with the parcel have been ceased (Trevet, Inc., 2018).

Section 4. Progress Since Last Review

This section provides protectiveness statements and associated recommendations presented in the Third Five-Year Review. This section also discusses the progress made toward addressing those recommendations.

4.1. IR-07/18

The Third Five-Year Review Report included the following protectiveness statement for IR-07/18 (TriEco-Tt, 2013b):

> *"The remedy for the portion of Parcel B at Sites IR-07 and IR-18 is protective of human health and the environment.*
>
> *Previous soil removals and durable covers on upland areas and the revetment along the shoreline have achieved the RAO of preventing exposure to contaminants, including radionuclides, in soil and sediment. Removal of the methane source has achieved the RAO for methane. Data collected during ongoing groundwater monitoring along the bay margin do not indicate migration of COCs at levels that would pose a risk to human health or the environment. The IC performance objectives specified in the amended ROD are being met by access controls until the time of transfer to prevent potential exposure. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs* [covenants to restrict the use of the property] *at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property."*

The Third Five-Year Review Report did not present any issues or recommendations for IR-07/18 (TriEco-Tt, 2013b).

4.2. PARCELS B-1 AND B-2

The Third Five-Year Review Report included the following protectiveness statement for the remainder of Parcel B (excluding IR-07/18), which was subdivided (in 2013) into Parcels B-1 and B-2 (TriEco-Tt, 2013b):

> *"The remedy for the remainder of Parcel B is expected to be protective of human health and the environment upon completion. In the interim, remedial activities completed to date have adequately addressed all exposure pathways that could result in unacceptable risks in these areas.*

> *The excavation and off-site disposal of soil was completed in 2010. Likewise, the radiologically related portions of the remedy have been completed, and DTSC approved an unrestricted release for radionuclides in the remainder of Parcel B (that is, excluding Sites IR-07 and IR-18). Construction of the remaining components of the remedy, including covers and revetment, operation of the SVE system at IR-10, and treatment of groundwater at IR-10 are under way. During construction, potential risk posed by exposure to contaminants in soil, soil vapor, or groundwater is controlled by access restrictions. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property."*

The Third Five-Year Review Report identified an issue regarding mercury concentrations in groundwater within Parcel B-2 (at IR-26 wells IR26MW49A and IR26MW51A). Mercury concentrations continue to exceed the trigger level despite previous soil removal actions. The Third Five-Year Review Report recommended that (1) groundwater at wells IR26MW49A and IR26MW51A should continue to be monitored semiannually for mercury to evaluate the trend in mercury concentrations, and (2) the mass flux of mercury into the bay in the vicinity of wells IR26MW49A and IR26MW51A should be evaluated (TriEco-Tt, 2013b).

Since 2013, groundwater continues to be monitored for mercury at bay margin wells (including wells IR26MW49A and IR26MW51A) under the BGMP. A dissolved mercury mass discharge evaluation was conducted at IR-26 in 2015 to estimate the mass discharge of mercury to San Francisco bay via groundwater transport (TriEco-Tt, 2016). Based on the results of that evaluation, the Navy is implementing in-situ stabilization of mercury to minimize migration of mercury in groundwater to the bay, as described in Section 3.3.2. The stabilization effort is currently underway and its performance will be reported in a future RACR.

4.3. PARCEL C

The Third Five-Year Review Report included the following protectiveness statement for Parcel C (TriEco-Tt, 2013b):

> *"The remedy for Parcel C is expected to be protective of human health and the environment upon completion. In the interim, remedial activities completed to date have adequately addressed all exposure pathways that could result in unacceptable risks in these areas.*
>
> *Soil excavation, groundwater treatment using lactate injection and SVE are underway. Radiological removals are also underway. Construction of the remaining components of the remedy (durable covers) will proceed after the radiological removals and excavations have been completed. During construction, potential risk posed by exposure to contaminants in soil, soil vapor, or groundwater is controlled by access restrictions. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property."*

The Third Five-Year Review Report did not present any issues or recommendations for Parcel C (TriEco-Tt, 2013b).

4.4. PARCEL D-1

The Third Five-Year Review Report included the following protectiveness statement for Parcel D-1 (TriEco-Tt, 2013b):

> *"The remedy for Parcel D-1 is expected to be protective of human health and the environment upon completion. In the interim, remedial activities completed to date have adequately addressed all exposure pathways that could result in unacceptable risks in these areas.*
>
> *The excavation and off-site disposal of soil was partially completed in 2010. Groundwater treatment using ZVI injection was completed in 2008. Radiological removals are under way. Construction of the remaining components of the remedy (removal of two remaining areas and covers) will proceed after the radiological removals have been completed. During construction, potential risk posed by exposure to contaminants in soil, soil vapor, or groundwater is controlled by access restrictions. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property."*

The Third Five-Year Review Report did not present any issues or recommendations for Parcel D-1 (TriEco-Tt, 2013b).

4.5. PARCEL D-2

The Third Five-Year Review Report did not include a protectiveness statement for Parcel D-2, because the parcel was deemed to require no further action following completion of radiological remediation.

4.6. PARCEL G

The Third Five-Year Review Report included the following protectiveness statement for Parcel G (TriEco-Tt, 2013b):

> *"The remedy for Parcel G is expected to be protective of human health and the environment upon completion. In the interim, remedial activities completed to date have adequately addressed all exposure pathways that could result in unacceptable risks in these areas.*
>
> *The excavation and off-site disposal of soil and removal of soil stockpiles were completed in 2010. Groundwater treatment using ZVI injection was completed at IR-09 and IR-71 in 2008. The radiologically related portions of the remedy have been completed, and DTSC approved an unrestricted release for radionuclides in Parcel G. Construction of the remaining component of the remedy (covers) is substantially completed. During construction, potential risk posed by exposure to contaminants in soil, soil vapor, or groundwater is controlled by access restrictions. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property."*

The Third Five-Year Review Report did not present any issues or recommendations for Parcel G (TriEco-Tt, 2013b).

4.7. PARCEL UC-1

The Third Five-Year Review Report included the following protectiveness statement for Parcel UC-1 (TriEco-Tt, 2013b):

> *"The remedy for Parcel UC-1 is expected to be protective of human health and the environment upon completion. In the interim, remedial activities completed to date have adequately addressed all exposure pathways that could result in unacceptable risks in these areas.*
>
> *Previous soil removals and durable covers have achieved the RAO of preventing exposure to contaminants in soil. The radiologically related portions of the remedy have been completed, and DTSC approved an unrestricted release for radionuclides in Parcel UC-1. Plans for a soil vapor survey at Parcel UC-1 are in progress. The IC performance objectives specified in the ROD are being met by access controls until the time of transfer to prevent potential exposure. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property."*

The Third Five-Year Review Report did not present any issues or recommendations for Parcel UC-1 (TriEco-Tt, 2013b).

4.8. PARCEL UC-2

The Third Five-Year Review Report included the following protectiveness statement for Parcel UC-2 (TriEco-Tt, 2013b):

> *"The remedy for Parcel UC-2 is expected to be protective of human health and the environment upon completion. In the interim, remedial activities completed to date have adequately addressed all exposure pathways that could result in unacceptable risks in these areas.*
>
> *Previous soil removals and durable covers have achieved the RAO of preventing exposure to contaminants in soil. The radiologically related portions of the remedy have been completed, and DTSC approved an unrestricted release for radionuclides in Parcel UC-2. Concentrations of VOCs in groundwater are less than remediation goals or are decreasing. During monitoring of natural attenuation, potential risk posed by exposure to contaminants in soil, soil vapor, or groundwater is controlled by access restrictions. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property."*

The Third Five-Year Review Report did not present any issues or recommendations for Parcel UC-2 (TriEco-Tt, 2013b).

Section 5. Five-Year Review Process

This section describes activities conducted in support of this Fourth Five-Year Review Report for HPNS.

5.1. COMMUNITY NOTIFICATION, INVOLVEMENT, AND SITE INTERVIEWS

Members of the BRAC Cleanup Team (BCT) were notified of the initiation of the five-year review process at a meeting held on March 8, 2018. The members of the BCT were also interviewed to solicit their feedback for this report and they were requested to review and comment on the draft and draft final versions of this report.

Members of the San Francisco community were notified about the initiation of five-year review process through an email sent on April 1, 2018; at a community meeting held on April 11, 2018; and through public notices published in local newspapers (*San Francisco Chronicle* and *San Francisco Bay View*) in June 2018. The public notices informed the community members that the Fourth Five-Year Review Report would be made available for public review and comment.

BCT members (which include EPA, DTSC, and the Water Board) and San Francisco Department of Public Health representatives were interviewed on February 22, 2018, as part of the five-year review process. Appendix B contains records of the interviews. The most common issues and concerns raised during the interviews are summarized below.

- Concerns related to the adequacy of historical radiological remediation based on the discovery of widespread falsification of radiological data by a Navy contractor. The radiological issues have resulted in (1) distrust of the Navy's cleanup program by the regulatory agencies and the community; (2) delays in the achievement of cleanup, transfer, and redevelopment of the affected parcels; and (3) increased workloads for regulatory agency representatives, resulting in delays in document reviews.
- Community expectations that the regulatory agencies more actively oversee future Navy work and be involved with developing the plans to address the radiological remediation issues to ensure that work is performed appropriately.
- The need for the Navy to increase its community involvement effort and ensure the transparent exchange of information with the public.
- The need for increased communication by the Navy at BCT meetings in advance of planning and executing work to avoid general confusion and time spent by the regulatory agencies reviewing documents, commenting on documents, and understanding the scopes and intent of the work.

- Concerns about Navy document quality and responsiveness to comments on documents leading to lengthy regulatory agency reviews and extensive comments.
- Dust generation and control during cleanup work activities.

Additionally, local community members were invited to participate in a survey on February 26, 2018, regarding the status of cleanup activities conducted over the past 5 years. Appendix B contains records of the survey responses. The most common issues and concerns raised in the surveys are summarized below.

- General lack of public trust in the adequacy of the cleanup work and how information on the radiological issues has been communicated.
- Concerns over losses in property value caused by the discovery of the radiological cleanup issues, the effect of delays in redevelopment on the community's growth and value, and whether it is safe to live in Parcel A.
- The need for the Navy to act quickly to address the radiological cleanup issues and communicate progress with the community more frequently, transparently, and effectively.
- Dust generation during cleanup work activities.

5.2. DOCUMENT AND DATA REVIEW

As part of this five-year review, documents and data related to remedy implementation were reviewed for each parcel. The reviews primarily focused on (1) documents and data that provide information on the technical and regulatory considerations that led to remedy selection and implementation, (2) documents that demonstrate remedy completion, and (3) documents and parcel-specific data that demonstrate the remedies continue to be protective of human health and the environment.

The types of documents reviewed include those focused on remedy implementation, maintenance, and monitoring, such as RDs, LUC RDs, RAMPs, RAWPs, RACRs, O&M Plans, post-construction O&M reports, soil vapor investigation reports, SVE progress reports, groundwater treatment progress reports, and BGMP reports, including semiannual groundwater monitoring reports.

The types of data reviewed to assess remedy performance include:

- Soil confirmation sampling data collected following hotspot excavation remedies
- Soil gas data collected during soil gas investigations
- Qualitative remedy performance data presented in O&M inspection reports
- SVE data collected as part of SVE remedy monitoring
- Groundwater treatment data collected to evaluate performance of in-situ groundwater treatment remedies
- Groundwater data for metals and VOCs collected as part of MNA and LTM remedies

The Navy has completed an extensive review of the radiological remediation documents and data as part of its evaluation of the potential contractor manipulation and/or falsification of data and has identified the areas where resurveying for radionuclides is required to address all issues discovered during the Navy's evaluation. Any available information on the status of the review and discoveries made by the Navy were considered during the development of this five-year review.

5.3. SITE INSPECTIONS

The Navy conducted site inspections for this review on January 29, 2018. The purpose of the site inspections was to review and document current site conditions to assist in evaluating the protectiveness of the remedial systems. Site access and general site conditions were also evaluated during the inspection. Appendix C contains the site inspection checklists and associated photographic logs that document the observations made during the inspections.

The inspection focused on the completed cover remedies at IR-07/18 and Parcels B-1, B-2, C, G, and UC-3. At the time of the inspections, the completed cover remedies in Parcels UC-1 and UC-2, which have already been transferred to the City and County of San Francisco, were in disrepair due to redevelopment construction activities that are being performed in accordance with an approved Risk Management Plan (Geosyntec Consultants, 2015). The roadways in Parcels UC-1 and UC-2 were damaged as a result of heavy truck traffic associated with construction within the new Hunters Point Artist Parcel, and they will be repaired upon the completion of current construction activities. As a result, these covers could not be inspected. Observations made during the site inspections indicated that the remedies at all sites were operating properly and successfully.

The soil cover at IR-07/18 was observed to be in good condition with no evidence of settlement, erosion, bulges, or cracks. All slopes appeared stable, and the cover vegetation was well established. Minor holes (typically 2 to 5 inches in diameter) that did not appear to extend far below surface were observed. The holes would not endanger the effectiveness of the soil cover, which is at least 3 feet thick within the radiological ARIC and at least 2 feet thick in other areas. The shoreline revetment was observed to be in good condition, with some sand refilling the bayward areas of the revetment toe. The small asphalt cover at the northeastern corner of IR-07 was observed to be in good condition.

The soil cover in Parcel B-1 was observed to be in good condition with no evidence of settlement, erosion, bulges, or cracks. All slopes appeared stable, and the cover vegetation was well established. The asphalt cover and building foundations across Parcels B-1 and B-2 were observed to be in good condition, with only minor damage caused by weed growth at seams in the asphalt cover. Swales were intact and free of major debris. The shoreline revetment was observed to be in good condition.

The asphalt cover and building foundations across Parcels C were observed to be in good condition, with only minor damage caused by weed growth at seams in the asphalt cover. Swales were intact and free of major debris. The shoreline armoring area near the entrance to Dry Dock 2 was observed to be in good condition.

The asphalt cover and building foundations across Parcel G were observed to be in good condition, with only minor damage caused by weed growth at seams in the asphalt cover. Swales were intact and free of major debris.

The newly installed asphalt cover in Parcel UC-3 was observed to be in good condition, with only minor damage caused by frequent traffic on the roadway surface. The O&M program for Parcel UC-3 has not begun yet, but the first inspection and repair event is expected to occur within the next few months. Any damaged areas will be addressed at that time. The infiltration trenches in the roadway shoulder were intact and free of major debris.

Monitoring well surface completions observed during the site inspections were found to be in good condition. Monitoring wells are regularly inspected during the semiannual groundwater sampling events and were generally observed to be in good condition.

Section 6. Technical Assessment

Three questions are examined in the technical assessment to evaluate whether the completed remedies at HPNS are protective of human health and the environment:

- Question A: Is the remedy functioning as intended by the decision documents?
- Question B: Are the exposure assumptions, toxicity data, cleanup levels, and RAOs used at the time of the remedy still valid?
- Question C: Has any other information come to light that could call into question the protectiveness of the remedy?

The following sections address each of these questions, based on the information and data summaries presented in previous sections. The discussion presented in the following sections provides a framework for the protectiveness statements that are provided in Section 8. The technical assessments and protectiveness statements relate to remedies that have been implemented and demonstrated to be complete at the time of this five-year review.

6.1. QUESTION A

Is the remedy functioning as intended by the decision documents?

Each type of remedy implemented to date was evaluated to determine whether it is functioning as designed. The factors listed below were considered when making the determination about each remedy:

<u>RA performance (if applicable):</u>

- Whether the RA continues to operate and function as designed
- Whether cleanup levels are being achieved or are on a path to be achieved in a reasonable time frame
- Whether containment is effective, if applicable
- Whether opportunities exist to improve the performance and/or reduce costs of monitoring, sampling, and treatment systems

System O&M (if applicable):

- Whether operating procedures, as implemented, are working in a manner that will continue to maintain the effectiveness of the remedy
- Whether frequent equipment breakdowns or changes indicate a potential issue affecting protectiveness
- Whether large variances in O&M costs could indicate a potential remedy problem

Implementation of ICs and other measures (if applicable):

- Whether ICs are in place and are proving to be effective in preventing exposure
- Whether access controls (e.g., fencing and warning signs) are in place and are proving to be effective in preventing exposure
- Whether other actions (e.g., removals) necessary to ensure that immediate threats have been addressed are complete

The responses to Question A are discussed below for each remedy component, most of which have been implemented at multiple parcels. Only remedy components that have been implemented and demonstrated to be complete are evaluated in this technical assessment.

6.1.1. Excavation and Offsite Disposal of Soil Hot Spots

Are the hotspot excavation remedies implemented in Parcels B-1, B-2, C, D-1, E-2, G, and UC-3 functioning as intended by the decision documents? YES

RA Performance: Published documents verify that the hotspot excavations, as required by the RODs, were implemented properly and are reducing site-wide risk as intended in Parcels B-1, B-2, C, D-1, E-2, G, and UC-3. The hotspot excavations included the collection of confirmation samples to demonstrate adequate removal of soil. All hot spots were backfilled with clean imported soil meeting specified backfill acceptance criteria. Permanent removal of soil that poses an unacceptable exposure risk, in combination with the durable cover remedies described in Section 6.1.2, effectively achieves the RAO of preventing exposure to organic and inorganic chemicals in soil at concentrations greater than RGs. No opportunities for optimization or early indicators of potential problems were identified for the hotspot excavations during this review.

System O&M: Not applicable.

Implementation of ICs and other measures: Section 6.1.2 discusses implementation of the ICs to addresses exposure to remaining contaminants in soil and sediment.

6.1.2. Durable Covers

Are the durable cover remedies implemented in IR-07/18 and Parcels B-1, B-2, C, G, UC-1, UC-2, and UC-3 functioning as intended by the decision documents? YES

RA Performance: Published documents, site inspections, and communication with personnel knowledgeable about the sites indicate that the durable covers, as required by the RODs, were implemented properly and are functioning as intended in IR-07/18 and Parcels B-1, B-2, C, G, UC-1, UC-2, and UC-3. Durable covers on upland areas and along the shoreline have been shown to effectively contain and prevent exposure to remaining organic and inorganic chemicals in soil and sediment. The proper function of the durable covers effectively achieves the RAO of preventing exposure to organic and inorganic chemicals in soil at concentrations greater than the RGs. In Parcels UC-1 and UC-2, where durable covers have been compromised by redevelopment work, construction activities are being implemented and monitored in accordance with an approved Risk Management Plan that complies with applicable ICs. No opportunities for optimization or early indicators of potential problems were identified for the durable covers during this review.

System O&M: The durable covers in IR-07/18 and Parcels B-1, B-2, C, G, UC-1, and UC-2 are monitored and maintained in accordance with their respective O&M Plans. The durable covers in Parcel UC-3 were constructed recently and an O&M Plan is currently in development. Regularly scheduled inspections performed by qualified professionals have verified that all durable covers within the post-construction O&M phase are in good condition, and that O&M of the covers has been effective. Minor issues encountered, such as asphalt cover damaged by weed growth or heavy traffic, animal burrows in soil covers, areas of poor vegetation growth on soil covers, and breaches of the perimeter fence, have not compromised the integrity of the remedy. O&M costs are generally consistent from year to year and are not anticipated to change significantly as long as the current configurations of the durable cover remedies are maintained. In Parcels UC-1 and UC-2, where durable covers have been compromised by redevelopment work, construction activities are being implemented and monitored in accordance with an approved Risk Management Plan that complies with applicable ICs and restoration of the durable covers will comply with the applicable O&M Plan.

Implementation of ICs and Other Measures: The IC performance objectives that relate to preventing potential exposure to contaminants in soil and sediment are being met by access controls. Overall access to HPNS is restricted by manned, restricted-access checkpoints. Access to most sites and parcels is additionally controlled by fencing and signs at the site. Access controls will not be required in the future following the completion of redevelopment activities. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs following transfer of the property.

The Navy and the OCII perform annual inspections to verify compliance with the ICs designated by each site's or parcel's LUC RD. The inspection reports certify that the ICs related to land use and activity restrictions are being implemented in accordance with the LUC RD.

6.1.3. SVE

Are the SVE remedies implemented in Parcels B-1 and C functioning as intended by the decision documents? YES. The source of the VOC mass in the vadose zone is being reduced by SVE. However, mass removal efficiency is low due to mass diffusion limitations in the heterogeneous soil at HPNS.

RA Performance: SVE remedies are currently being implemented in Parcel B-1 (IR-10) and five of eight planned treatment areas (1, 3, 6, 7, and 8) in Parcel C. Treatment in Areas 4 and 5 is expected to begin in 2018. The goal of implementing SVE in Parcels B-1 and C is to reduce the source of the VOC mass in soil. The SVE technology was prescribed for use in Parcels B-1 and C as long as operations are efficient (i.e., mass removal is cost effective).

The SVE systems installed and activated to date in Parcels B-1 and C were constructed and operated in accordance with the RODs, RDs, and system-specific operation and optimization plans.

System O&M: SVE system operation in Parcels B-1 and C is ongoing. Operations are monitored and optimized, as required, to maximize removal efficiency. Optimization measures include system modifications to improve operational performance, pulsed and cycled operation of extraction wells, targeted operation of SVE wells in the areas of highest contaminant concentrations, optimization of vacuum pressures to control radii of influence and minimize water entrainment from the SVE wells, and passive air venting to address stagnation points. The mass removal achieved to date is summarized below.

- Approximately 18.5 pounds of VOCs (predominantly TCE) has been removed from IR-10 in Parcel B-1.
- Approximately 2.5 pounds of VOCs (predominantly TCE) has been removed to date from Area 1 in Parcel C.
- Approximately 1.4 pounds of VOCs (predominantly PCE and TCE) has been removed to date from Area 3 in Parcel C.
- Approximately 4 pounds of VOCs (predominantly TCE) has been removed to date from Areas 6 and 7 in Parcel C.
- Approximately 21 pounds of VOCs (predominantly PCE and TCE) has been removed to date from Area 8 in Parcel C.

Despite proper system operation and optimization, SVE treatment has achieved a limited reduction in the contaminant source to date in all active treatment areas within Parcels B-1 and C. SVE operations have revealed the systems are operating in diffusion-limited conditions, which reduces the efficiency of mass removal and results in long rebound times. SVE operations in Parcels B-1 and C are characterized by rapid declines in soil gas concentrations upon initiation of SVE system operations, followed by long rebound/equilibration periods where soil gas ultimately approaches initial concentrations, indicating that transport of the VOC mass from soil to soil gas is limited by a slow rate of diffusion. Soil at HPNS is primarily

artificial fill composed of low-permeability heterogeneous silts and clays with gravel and debris. The slow transport rate of VOC mass from low-permeability soil has limited the VOC mass removed to date.

This review has determined that SVE, although being implemented in accordance with the RODs and RDs and meeting the ROD objective of removing VOCs, is not operating efficiently to reduce the mass of source contamination in soil. Optimization of the existing SVE systems will not significantly improve source mass reduction.

Implementation of ICs and Other Measures: The IC performance objectives specified in the RODs will be met by land use and activity restrictions to prevent potential exposure to soil gas. Construction of enclosed structures will be restricted and may require implementation of engineering controls and monitoring. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs following transfer of the property.

6.1.4. In-Situ Groundwater Treatment

Are the in-situ groundwater remedies implemented in Parcels B-1 and C functioning as intended by the decision documents? YES

RA Performance: In-situ groundwater treatment remedies have been implemented in Parcel B-1 (IR-10) and Parcel C (RU-C1, RU-C2, RU-C4, and RU-C5). Published documents indicate that the in-situ groundwater treatment remedies, as required by the RODs, were implemented properly. Additional treatment is planned for one or more of the RUs in Parcel C in the near future. No opportunities for optimization or early indicators of potential problems were identified for the in-situ groundwater treatment remedies during this review.

System O&M: Performance monitoring of the groundwater treatment remedies is currently being performed under the BGMP and will continue to occur until the RAOs are met at each plume. Monitoring and reporting costs are generally consistent from year to year and are not anticipated to change significantly.

Implementation of ICs and Other Measures: The IC performance objectives specified in the RODs are being met by land use and activity restrictions to prevent potential exposure to groundwater. Well installation and groundwater use are restricted. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs following transfer of the property.

The Navy performs annual inspections to verify compliance with the ICs designated by each parcel's LUC RD. The inspection reports certify that the ICs related to land use and activity restrictions are being implemented in accordance with the LUC RDs.

6.1.5. MNA and LTM of Groundwater

Are the MNA and LTM remedies in IR-07/18 and Parcels B-1, B-2, C, D-1, G, UC-2, and UC-3 functioning as intended by the decision documents? YES

RA Performance: MNA of VOC and/or LTM of metals in groundwater are currently being implemented at IR-07/18 and Parcels B-1, B-2, C, D-1, G, and UC-2. MNA for VOCs in groundwater at Parcel UC-3 was specified in the RD, but pre-RA monitoring data demonstrated that groundwater treatment and MNA were unnecessary at Parcel UC-3.

Published documents indicate that the MNA and LTM remedies are being implemented appropriately and in accordance with the RODs and RAMPs. The MNA and LTM remedies functioned, or are functioning, as intended. Data collected during ongoing groundwater monitoring are providing information on the attenuation rates of COCs in groundwater and allowing for data comparisons to RGs and well-specific TLs.

MNA and LTM are implemented under the BGMP. The program is reviewed and optimized regularly. No opportunities for further optimization or early indicators of potential problems were identified for the MNA and LTM remedies during this review.

System O&M: MNA and LTM remedies are currently performed under the BGMP and will continue to occur until the groundwater RGs are met. Monitoring and reporting costs are generally consistent from year to year and are not anticipated to change significantly.

Implementation of ICs and Other Measures: The IC performance objectives specified in the RODs are being met by land use and activity restrictions to prevent potential exposure to groundwater. Well installation and groundwater use are restricted. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs following transfer of the property.

The Navy performs annual inspections to verify compliance with the ICs designated by each parcel's LUC RD. The inspection reports certify that the ICs related to land use and activity restrictions are being implemented in accordance with the LUC RDs.

6.1.6. Radiological Surveys and Remediation

Are the radiological surveys and remediation remedies implemented in IR-07/18 and Parcels B-1, B-2, C, D-1, D-2, E, G, UC-1, UC-2, and UC-3 functioning as intended by the decision documents? YES (for IR-07/18 and Parcel D-1); NO (for Parcels B-1, B-2, C, D-2, E, G, UC-1, UC-2, and UC-3).

RA Performance: Published documents report the completion of radiological surveys and remediation in IR-07/18 and Parcels B-1, B-2, C, D-1, D-2, E, G, UC-1, UC-2, and UC-3. In January 2018, the Navy determined that a significant portion of the radiological survey and remediation work completed to date

was compromised by potential manipulation and/or falsification of data by one of its radiological remediation contractors. Compromised data were identified in reports associated with Parcels B-1, B-2, C, D-2, E, G, UC-1, UC-2, and UC-3. The Navy is currently in the process of planning corrective actions to ensure the radiological remedies specified in the RODs are implemented as intended.

The radiological remedies that have been successfully completed and are functioning as intended are described below.

- Radiological surveys removals were completed in 2010 at IR-07/18. A MARSSIM Class 1 survey has been completed for the entire surface of IR-07/18, and the top 1 foot of soil was remediated to levels specified in the Amended ROD to ensure a radiologically clean surface before the cover remedy was applied. The constructed cover over the portion of IR-07/18 (within the radiological ARIC) prevents exposure to radionuclides in accordance with the RAOs. CDPH completed further surface scans at IR-07/18. CDPH concluded that there was no evidence or indication of radiological health and safety concerns based on surface gamma radiation in the surveyed areas of IR-07/18 (CDPH, 2013).
- The Phase 1 radiological TCRA has been completed at Parcel D-1, and the RACR for the Phase 2 radiological TCRA is currently being developed. The TCRAs included radiological surveys and remediation for radiologically impacted buildings, structures, and former building sites. Additionally, radiologically impacted storm drain and sanitary sewer lines were removed and the trenches were surveyed and remediated.

System O&M: The durable covers within the radiological ARIC in IR-07/18 are monitored and maintained in accordance with the O&M Plan (ERRG, 2012d). Regularly scheduled inspections performed by qualified professionals have verified that all durable covers within the post-construction O&M phase are in good condition, and that O&M of the covers has been effective. Minor issues encountered, such as animal burrows in soil covers, areas of poor vegetation growth on soil covers, and breaches of the perimeter fence, have not compromised the integrity of the remedy. O&M costs are generally consistent from year to year and are not anticipated to change significantly as long as the current configurations of the durable cover remedies are maintained within the radiological ARIC.

O&M is not applicable to the completed radiological remedies in Parcel D-1, because this parcel has been radiologically released.

Implementation of ICs and Other Measures: The IC performance objectives that relate to preventing potential exposure to radionuclides within the radiological ARIC in IR-07/18 are being met by access restrictions. The site is currently, and will remain, enclosed by a perimeter fence with locked gates until transfer to the OCII. The durable covers are inspected and maintained in accordance with the O&M Plan (ERRG, 2012d) and prevent contact with underlying soil. The activity and land use restrictions described in the LUC RD Report (ChaduxTt, 2010a) will be incorporated into the Quitclaim Deed and Covenant to Restrict Use of Property and will take effect upon transfer to the OCII and issuance of those documents.

Future implementation of land use and activity restrictions will effectively prevent exposure to COCs following transfer of the property.

ICs for radionuclides are applicable to a portion of Parcel D-1, as this area was not released by the Phase 1 and Phase 2 TCRAs. The Navy is planning to revise the existing LUC RD for Parcel D-1 to define those ICs and their area of applicability.

The Navy performs annual inspections to verify compliance with the ICs designated by each parcel's LUC RD. The inspection reports certify that the ICs related to land use and activity restrictions are being implemented in accordance with the LUC RDs.

6.2. QUESTION B

Are the exposure assumptions, toxicity data, cleanup levels, and RAOs used at the time of remedy selection still valid?

EPA's guidance document for five-year reviews identifies several areas to be considered in evaluating whether the assumptions made at the time of remedy selection remain valid (EPA, 2001). Areas of consideration include:

Standards and To Be Considered (TBC) Criteria:

- Whether standards identified as ARARs, newly promulgated standards, and/or changes in TBC criteria could call into question the protectiveness of the remedy

Toxicity and Other Contaminant Characteristics:

- Whether toxicity factors for COCs at the site have changed in a way that could affect the protectiveness of the remedy

Risk Assessment Methods:

- Whether risk assessment methodologies or guidance have changed in a way that could affect the protectiveness of the remedy

Exposure Pathways:

- Whether current or reasonably anticipated future land use on or near the site has changed or may change in the near future (including redevelopment or changed resource use)
- Whether human health or ecological routes of exposure or receptors have been newly identified or changed in a way that could affect the protectiveness of the remedy
- Whether there are newly identified contaminants or contaminant sources leading to a potential/actual pathway not previously addressed by the remedy

- Whether there are unanticipated toxic byproducts or daughter products of the remedy not previously addressed by the decision documents
- Whether physical site conditions or the understanding of these conditions have changed in a way that could affect the protectiveness of the remedy

Expected Progress Toward Meeting RAOs:

- Whether the remedy is progressing as expected toward meeting the RAOs
- Whether new site conditions (e.g., discovery of new contaminants) impact the RAOs and remedy protectiveness

Five-year review guidance (EPA, 2001) indicates that the question of interest in developing the five-year review is not whether changes have occurred but rather whether changes call into question the protectiveness of the cleanup action. The following sections evaluate each of the above considerations.

6.2.1. Changes in Standards and TBC Criteria

The Navy evaluated the ARARs established in the RODs for Parcels B (i.e., IR-07/18 and Parcels B-1 and B-2), C, D-1, D-2, E, E-2, G, UC-1, UC-2, and UC-3. No changes to chemical-specific, location-specific, or action-specific ARARs established in the RODs were identified that would bear on the protectiveness of the remedies.

6.2.2. Changes in Toxicity and Other Contaminant Characteristics

Soil and Groundwater: The Navy evaluated changes in soil and groundwater toxicity criteria and other contaminant characteristics since the third five-year review to determine if they would affect the protectiveness of the remedies. To perform this evaluation, the Navy focused its evaluation on the COCs that are the primary risk drivers in soil and groundwater at HPNS. The primary risk drivers in soil are arsenic, benzo(a)pyrene, and Aroclor-1260, and the primary risk drivers in groundwater are TCE, PCE, and VC.

The RGs established in the ROD for the primary risk drivers in soil and groundwater at Parcels B, C, D-1, G, UC-1, UC-2, and UC-3 were selected based on a comparison of the COC-specific risk-based concentration (RBC), the laboratory practical quantitation limit (PQL) based on standard EPA analytical methods, and the Hunters Point ambient level (HPAL) for naturally occurring chemicals. The RBCs were calculated based on a target excess cancer risk level of 1×10^{-6} and target noncancer HI of 1, consistent with the exposure pathways and assumptions used in the parcel-specific HHRAs to assess risks. Table 15 provides the soil RGs identified in the RODs for the primary COCs, and Table 16 provides the groundwater RGs for the primary COCs.

Changes to toxicity criteria have occurred since the signing of the RODs. These changes are observable as differences between the ROD RBCs and current risk-based values developed by EPA and CalEPA DTSC. Current risk-based values were obtained from EPA's Regional Screening Level (RSL) Tables (EPA, 2018)

and DTSC's HHRA Note Number 3 (DTSC, 2018). The toxicity values used to calculate RSLs are selected using a hierarchy of toxicological sources, with the Integrated Risk Information System as its primary source. For most chemicals, DTSC endorses the values listed in the EPA RSL tables. However, some values listed in the EPA RSL tables differ significantly from values calculated using CalEPA toxicity criteria and risk assessment procedures. DTSC-modified screening levels (DTSC-SLs) are used in conjunction with the EPA RSLs to evaluate chemical concentrations in environmental media at California sites and facilities. Note that the DTSC-SLs are derived at a target risk level of 1×10^{-6} and a target hazard quotient (HQ) of 1 as are the EPA RSLs. Table 15 shows a comparison of current risk-based values for soil to the RGs listed in the RODs.

For groundwater, risk-based values were based on the groundwater to indoor air exposure pathway (i.e., vapor intrusion). Table 16 shows a comparison of ROD RGs and current EPA Vapor Intrusion Screening Levels (VISLs). The VISLs are based on default residential or nonresidential (i.e., commercial) exposure scenarios, a target cancer risk level of one per million (1×10^{-6}), and a target noncancer HQ of 1.0.

For some of the COCs in soil and groundwater, the RG was based on the laboratory PQL because the RBC was below the PQL at the time of the ROD. However, as analytical techniques improve over time, laboratories are able to achieve lower PQLs for some of the COCs. As part of the toxicity evaluation, current analytical limits of quantitation (LOQs) were compared to PQLs listed in the ROD. In present-day terminology, the PQL is referred to as an LOQ in accordance with the DoD Quality Systems Manual for Environmental Laboratories and the Navy's Tier II SAP format guidelines. Furthermore, for analytes where the LOQ is higher than an RBC using the best available technology, another laboratory-specific limit, the detection limit, can be used to evaluate risk and is the preferred laboratory limit for use in risk assessments.

As shown in Tables 15 and 16, the comparison of ROD cleanup levels to current risk-based screening levels and laboratory-specific limits indicate that some levels are higher, some lower, and some levels were nearly the same. Although some changes to the toxicity criteria and to laboratory-specific limits have occurred, these changes do not affect the protectiveness of the remedies because RBC for the primary risk drivers remain within the risk management range. Additionally, protectiveness will be maintained as long as ICs preventing exposure remain in place and ongoing monitoring continues until COC concentrations in soil and groundwater are at such levels to allow for unrestricted use and exposure at the time when the future property owner proposes to terminate those ICs.

Emerging chemicals (PFAS compounds) were added to the analytical suites for groundwater sampling activities in IR-10 (Parcel B-1) and IR-09 (in Parcel G) in August 2017. Concentrations of PFOA, PFOS, combined PFOA and PFOS, and PFBS were less than their respective FSCs during the PFAS groundwater investigation. Based on available data, groundwater at IR-10 and in Parcel G has not been affected with PFAS. As a result, concerns regarding emerging groundwater chemicals do not call into question the protectiveness of the remedies.

No new contaminants or contaminant sources in soil and groundwater originating from the sites have been identified or detected during monitoring performed since the third five-year review. No unanticipated toxic byproducts have been generated as a result of remedy implementation. The toxicity data used at the time of the remedy selection are still valid.

Soil Gas: The Navy is implementing ICs to manage risk associated with soil gas within the ARICs defined for Parcels B-1, B-2, C, D-1, E, G, UC-1, UC-2, and UC-3. In Parcels B-1 and C, the Navy is also implementing active treatment (by SVE and ISB) to reduce the source contamination contributing to elevated COC concentrations in soil gas. There have been changes to soil gas toxicity criteria since the third five-year review. Those changes may affect the Navy's methodology for developing preliminary soil gas action levels (SGALs) used in post-ROD soil gas investigations to refine the ARICs defined in the RODs. The regulatory agencies are currently reviewing and reevaluating their methods for assessing vapor intrusion risk, as discussed further in Section 6.2.3. As a result, the Navy plans to reevaluate its approach to calculating SGALs and will incorporate current toxicity criteria into the process, as required. Updated SGALs will be used to appropriately size the soil vapor ARICs for each parcel prior to property transfer. Until that time, the Navy will rely on the more conservative ARICs originally presented in the RODs to maintain current remedy protectiveness.

6.2.3. Changes in Risk Assessment Methods

Since the RODs were signed and since the third five-year review was completed, EPA issued supplemental guidance updating standard default exposure parameters for use on Superfund sites (EPA, 2014). Standard default updates include the following:

Definition (units)	Previous Value	2014 Value
Resident Skin Surface Area for Soil – Child (cm^2)	2,800	2,690
Resident Skin Surface Area for Soil – Adult (cm^2)	5,700	6,032
Worker Skin Surface Area for Soil – Adult (cm^2)	3,300	3,470
Resident Soil Adherence Factor – Child (mg/cm^2)	0.2	0.2
Resident Soil Adherence Factor – Adult (mg/cm^2)	0.07	0.07
Worker Soil Adherence Factor – Adult (mg/cm^2)	0.2	0.12
Adult Body Weight – Adult (kg)	70	80
Resident Exposure Duration (year)	30	26
Resident Exposure Duration – adult (year)	24	20

Notes:
cm^2 = square centimeters
kg = kilograms
mg/cm^2 = milligrams per square centimeters

Use of these updated default exposure parameters in place of the original values used in the risk assessments for each of the parcels primarily results in increasing the RBCs for the adult receptors. The increase is not significantly different from the values estimated in the original risk assessments. As such, EPA changes to default exposure parameters do not affect the protectiveness of the remedies.

The Navy established preliminary SGALs in 2011, prior to the third five-year review (ChaduxTt, 2011g). The SGALs are "action levels" (not RGs) based on calculated vapor intrusion risks and COCs identified during soil gas assessments conducted in each parcel. The results of comparisons of soil gas concentrations to SGALs supersede the groundwater vapor intrusion risk estimates and COCs identified in the RODs for Parcels B, C, D-1, E, G, UC-1, UC-2, and UC-3. Actions must be taken if results of soil gas surveys exceed SGALs. Those actions may include ICs (e.g., access limitations) or engineering controls (such as a vapor barrier) and would not necessarily prompt additional remediation, as might be implied by the term "remediation goal."

The method used for calculating risk-based concentrations for indoor air is similar to the EPA (2009, 2011a) and CalEPA (2005) methods used to calculate risk-based concentrations for HPNS parcels. A target indoor air cancer risk of 10^{-6} and a noncancer HI of 1 were used for calculating risk-based concentrations for indoor air. These target cancer and noncancer levels are consistent with the levels used to identify COCs in the HHRAs for HPNS. Likewise, the exposure assumptions used to calculate risk-based concentrations for indoor air are consistent with those used in the HHRAs for HPNS.

To translate the risk-based concentrations for indoor air to risk-based concentrations for soil gas, the Navy must make assumptions related to the attenuation and dilution of surface vapors through the vadose zone and building floor slab. The attenuation factors can be based on a model or on empirical data. Currently, the Navy's preliminary SGALs are calculated based on the generic attenuation factors provided in CalEPA (2005) that were derived from the 1991 Johnson and Ettinger model (JEM) (modified to include exposure time and air exchange rate in 2011) and generic attenuation factors provided by EPA (2002) that were derived from empirical data.

The generic attenuation factors presented in CalEPA (2005) were derived from the JEM and are based on the following assumptions: (1) a shallow source of vapors close to the building foundation, (2) relatively permeable (sandy) soil, (3) limited exchange between indoor and outdoor air, (4) homogeneous vapor concentrations underlying the building footprint, (5) constant source concentrations (e.g., no decrease in chemical concentrations over time through biodegradation), (6) under-pressurized buildings, (7) single-story buildings, and (8) lack of lateral vapor transport.

The generic attenuation factors provided in EPA (2002) were derived using empirical data for 40 residences. Shallow soil gas samples are defined as those collected either from directly below the foundation or from depths less than 5 feet below the foundation level. Consequently, EPA identified an attenuation factor of 0.1 as generally reasonable upper-bound value for the case where soil gas is measured directly beneath a

foundation (i.e., subslab measurements) or where soil gas is measured at less than 5 feet below the foundation level. Deep soil gas samples (i.e., samples collected from just above the water table or from depths greater than 5 feet below the foundation level) represent a more direct measurement of the source vapor concentration and are subject to less variability than is observed for shallow soil gas samples. Therefore, EPA (2002) recommends an attenuation factor of 0.01 for screening deep soil gas results for residential buildings. EPA (2002) does not specifically provide recommended attenuation factors for nonresidential buildings; however, EPA (2010) recommended an attenuation factor of 0.001 for screening deep soil gas results for industrial buildings at HPNS.

The Navy uses the preliminary SGALs as a first tier screening tool to determine which areas require additional evaluation. Based on the results of the first tier data screening, the Navy may perform a second tier evaluation to refine the SGALs. The second tier evaluation uses modeled, site-specific attenuation factors based on site-specific chemical and geotechnical data. Modeling is performed using the most up-to-date version of JEM at the time of the evaluation.

Since the establishment of the Navy's approach to calculating SGALs, the regulatory agencies (EPA and DTSC) have questioned the validity of using JEM to model active gas sampling and attenuation factors to derive site-specific SGALs. Agency concerns are based on EPA's assertion that its previously recommended attenuation factors are no longer valid (documented in notes from a meeting held between the Navy and EPA Region 9 on January 27, 2017) and recent research indicating previously unknown critical exposure effects (e.g., immune, neurotoxicity and increased fetal cardiac malformations caused by exposure to TCE), as discussed in Section 6.2.2. The EPA has proposed that the Navy cease to implement the second tier evaluations to develop SGALs and exclusively rely upon the results of the first tier evaluations to redefine or reduce ARICs for VOCs in the future. The Navy intends to consider agency concerns and reevaluate its approach to assigning SGALs. To maintain current remedy protectiveness, the Navy will rely upon the ARICs for VOCs defined in the RODs, as they were conservatively established to cover all areas that will be reused for human habitation (see Section 6.2.2).

6.2.4. Changes in Exposure Pathways

No new routes of exposure that could affect the protectiveness of the remedies have been identified. No changes to site conditions that could result in increased exposure have been identified. No significant changes to the risk assessment methodology have occurred that would affect the protectiveness of the remedy. The vapor intrusion exposure pathway was considered during the risk assessments that were used to support remedy selection.

ICs, including restrictive covenants regulating restricted land use, restricted activities, and prohibited activities, have been implemented to prevent exposure to areas where potential unacceptable risk is posed by COCs in soil and groundwater. ICs will remain in place as long as contamination remains at the site above levels that allow for unlimited use and unrestricted exposure. Physical site conditions or the understanding of these conditions has not changed in a way that could affect the protectiveness of the remedies.

Exposure assumptions developed in the HHRA considered the potential future exposures based on the expected reuses. The future redevelopment plan was updated in 2010 (SFRA 2010). To support implementation of the 2010 redevelopment plan at Parcel G, OCII prepared a feasibility assessment that analyzed the residual concentrations of COCs in soil using health-based regulatory standards to determine whether the residential land use restrictions could be reduced. The feasibility assessment concluded that current site conditions are appropriate for residential use in most of Parcel G. The feasibility assessment also concluded that the areas requiring residential land use restrictions could be reduced, provided that features of the selected remedy (e.g., durable covers and ICs with an O&M plan) remain in place (Langan, 2016). An ESD to the Final ROD was prepared to document the reduction in the areas requiring residential land use restrictions, based on the recommendations of the feasibility assessment (Navy, 2017). Otherwise, no changes to site conditions or expected reuses that could result in increased exposure have been identified. The exposure assumptions used at the time of the remedy selection are still valid.

6.2.5. Expected Progress Toward Meeting RAOs

The remedies are progressing as expected, except for the SVE remedies in Parcels B-1 and C and radiological remediation in Parcels B-1, B-2, C, D-2, E, G, UC-1, UC-2, and UC-3. Soil removal and containment remedies are functioning as intended to prevent contact with soil and sediment. Groundwater treatment remedies are in progress and being monitored to evaluate their long-term performance. MNA and long-term groundwater monitoring remedies are being implemented to gather the data necessary to track the attenuation of chemicals over time.

SVE remedies currently being implemented in Parcels B-1 and C are minimally effective at reducing the VOC source contamination due to the diffusion limitations inherent to site soil at HPNS. The inefficiency of the SVE technology reduces the long-term effectiveness of the treatment technology. Because the SVE technology is not a cost-effective means of removing VOC contamination from the vadose zone in Parcels B-1 and C in advance of implementation of ICs, use of this technology may be reconsidered. The ICs specified in the RODs, however, remain as an effective remedy for addressing risks from soil vapor intrusion in the future.

The Navy has concluded that a significant portion of the radiological survey and remediation work completed to date was compromised by potential manipulation and/or falsification of data by one of its radiological remediation contractors. Compromised data were identified in reports associated with Parcels B-1, B-2, C, D-2, E, G, UC-1, UC-2, and UC-3. The Navy is currently in the process of implementing corrective actions to ensure that the radiological remedies specified in the decision documents have been implemented as intended. The radiological rework will successfully achieve the RAOs for radionuclides specified in the RODs.

6.3. QUESTION C

Has any other information come to light that could call into question the protectiveness of the remedy?
YES.

No new ecological risks have been identified. No weather-related incidents, earthquakes, or other natural disasters have affected the protectiveness of the remedies.

The potential for an increase in the sea level elevation as a result of atmospheric warming (consistent with recent scientific research) has also been considered in the design of the shoreline protection measures at Parcels E and E-2, which contain areas where buried waste will be managed in place. The California Ocean Protection Council and the California Natural Resources Agency recently updated statewide guidance for sea-level rise to reflect recent advances in scientific projections (Griggs et al., 2017). Using the methodology of Kopp et al. (2014), the guidance estimated future sea-level rise at the Golden Gate tide gauge in San Francisco. The estimated sea-level rise in San Francisco under three future scenarios (referred to as representative concentration pathways [RCPs]) is summarized below.

- RCP 8.5 is consistent with a future in which there are no significant global efforts to limit or reduce emissions. In 2100, the likely sea-level rise associated with this scenario ranges from 1.6 to 3.4 feet.
- RCP 4.5 is a moderate emissions reduction scenario and assumes that global greenhouse gas emissions will be curtailed. In 2100, the likely sea-level rise associated with this scenario ranges from 1.2 to 2.7 feet.
- RCP 2.6 is a stringent emissions reduction scenario and assumes that global greenhouse gas emissions will be significantly curtailed. In 2100, the likely sea-level rise associated with this scenario ranges from 1.0 to 2.4 feet.

Based on the information summarized above, a contingency of up to a 3-foot increase in sea level was considered in designing the crest elevation for Parcels E and E-2.

No other information has been identified to suggest that the remedies may not be protective of human health or the environment.

Section 7. Issues, Recommendations, and Other Findings

The tables below presents issues, recommendations, and follow-up actions for HPNS parcels where at least some remedy components have been implemented and demonstrated to be complete.

Site(s): Parcels B-1 and C	**Issue Category:** Remedy Effectiveness			
	Issue: SVE implementation in Parcels B-1 and C is reducing source mass, but with limited effectiveness due to diffusion-limited conditions in the subsurface. Although ICs will maintain future protectiveness, source removal inefficiency is extending the period within which SVE will be implemented.			
	Recommendation: It is recommended that use of the SVE technology be evaluated for each treatment area due to inefficiency caused by diffusion-limited conditions. Site-specific studies (e.g., remedy optimization analyses) should be performed to estimate the magnitude and extent of source mass at each treatment area in Parcels B-1 and C to determine if other measures could be implemented to enhance SVE performance in the future. Any changes implemented to the approach for reducing source contamination in SVE areas should be discussed in the next five-year review report.			
Affect Current Protectiveness	**Affect Future Protectiveness**	**Party Responsible**	**Oversight Party**	**Milestone Date**
No	No	Navy	EPA/DTSC/Water Board	12/31/2019

Site(s): Parcels B-1, B-2, D-1, and G	**Issue Category:** Remedy Protectiveness			
	Issue: The regulatory agencies do not agree with the Navy's risk assessment methodology used to reduce the ARICs for VOCs.			
	Recommendation: In the near-term, the Navy should rely upon the original ARICs for VOCs defined in the RODs to maintain the current protectiveness of the remedies. The regulatory agencies are currently reviewing and reevaluating their methods for assessing vapor intrusion risk. Once consensus is achieved, the Navy should reevaluate its approach for calculating SGALs. The new SGALs would be developed based on the most current standards, toxicity criteria, and risk assessment methods. The new SGALs would be used to redefine the ARICs for soil gas at each parcel prior to property transfer. Any changes to soil gas risk assessment methodology should be discussed in the next five-year review report.			
Affect Current Protectiveness	**Affect Future Protectiveness**	**Party Responsible**	**Oversight Party**	**Milestone Date**
No	Yes	Navy	EPA/DTSC/Water Board	12/31/2018

Site(s): Parcels B-1, B-2, C, D-2, E, G, UC-1, UC-2, and UC-3	**Issue Category:** Remedy Protectiveness			
	Issue: The Navy has determined that a significant portion of the radiological survey and remediation work completed to date was compromised by potential manipulation and/or falsification of data by one of its radiological remediation contractors. It is currently not known if the RAOs for radionuclides have been achieved in Parcels B-1, B-2, C, D-2, G, E, UC-1, UC-2, and UC-3.			
	Recommendation: The Navy is currently in the process of implementing corrective actions to ensure that the radiological remedies specified in the decision documents have been implemented as intended. The radiological rework will successfully achieve the RAOs for radionuclides specified in the RODs. It is recommended that the Navy continue to perform its investigations to definitively determine that the radiological RAOs have been met at each of the affected parcels. It is anticipated that the radiological rework will span 5 years and be completed prior to the next five-year review. The results of the radiological rework should be discussed in the next five-year review.			
Affect Current Protectiveness	**Affect Future Protectiveness**	**Party Responsible**	**Oversight Party**	**Milestone Date**
No	To Be Determined	Navy	EPA/DTSC/Water Board	11/1/2023

Section 8. Protectiveness Statement

This section provides the protectiveness statements for each site or parcel where at least some remedy components have been implemented and demonstrated to be complete.

8.1. IR-07/18

The remedy for IR-07/18 is protective of human health and the environment. Previous soil removals and placement of durable covers on upland areas and along the shoreline have achieved the RAO of preventing exposure to contaminants, including radionuclides, in soil and sediment. Removal of the methane source has achieved the RAO for methane. Data collected during ongoing groundwater monitoring along the bay margin do not indicate migration of COCs at concentrations that would pose a risk to the environment (i.e., San Francisco Bay). The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property.

8.2. PARCEL B-1

The remedies completed to date for Parcel B-1 are protective of human health and the environment, noting that the radiological removal actions are being retested. Previous soil removals and placement of durable covers on upland areas and along the shoreline have achieved the RAO of preventing exposure to contaminants in soil and sediment. Data collected during ongoing groundwater monitoring are used to monitor COCs. Performance monitoring of groundwater treatment at IR-10 is currently underway and expected to be protective of San Francisco Bay in the future. Operation of the SVE system at IR-10 is ongoing, and ICs will be relied upon in the future to protect human health. Radiological surveys and removal actions completed in Parcel B-1 were compromised, and corrective actions are required to determine if the RAOs have been achieved. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property.

8.3. PARCEL B-2

The remedies completed to date for Parcel B-2 are protective of human health and the environment, noting that the radiological removal actions are being retested. Previous soil removals and placement of durable covers on upland areas and along the shoreline have achieved the RAO of preventing exposure to contaminants in soil and sediment. Data collected during ongoing groundwater monitoring are used to

monitor COCs. Performance monitoring of groundwater following in-situ stabilization of mercury in soil at IR-26 is currently underway, and it is anticipated that this action will be protective of the environment. Radiological surveys and removal actions completed in Parcel B-2 were compromised, and corrective actions are required to determine if the RAOs have been achieved. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property.

8.4. PARCEL C

The remedies completed to date for Parcel C are protective of human health and the environment, noting that the radiological removal actions are being retested. Previous soil removals and placement of durable covers have achieved the RAO of preventing exposure to contaminants in soil. Data collected during ongoing groundwater monitoring are used to monitor COCs that could pose a risk to human health or the environment. Additional groundwater treatment and performance monitoring of groundwater treatment at RU-C1, RU-C2, RU-C4, and RU-C5 is currently underway and expected to be protective in the future. Operation of the SVE system at Areas 1, 3, 6, 7, and 8, is ongoing and ICs will be relied upon in the future to protect human health. Treatment in Areas 4 and 5 is expected to begin in 2018. Radiological surveys and removal actions completed in Parcel C were potentially compromised, and corrective actions are required to determine if the RAOs have been achieved. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property.

8.5. PARCEL D-1

The remedy for Parcel D-1 is expected to be protective of human health and the environment upon completion. In the interim, remedial activities completed to date have adequately addressed all exposure pathways that could result in unacceptable risks in these areas.

Previous soil removals and partial placement of durable covers have partially achieved the RAO of preventing exposure to contaminants in soil and sediment. Data collected during ongoing groundwater monitoring are used to monitor COCs that could pose a risk to human health or the environment. Pre-ROD groundwater treatment using ZVI injection at IR-71 has been performed, and groundwater monitoring is currently being implemented in accordance with the RAMP. Radiological removals are complete and the parcel has been free released, with the exception of areas requiring restrictions for radionuclides. The restrictions for radionuclides will be defined in a forthcoming addendum to the LUC RD for Parcel D-1. Construction of the remaining components of the remedy will be completed in 2018. During construction, potential risk posed by exposure to contaminants in soil, soil vapor, or groundwater is controlled by access restrictions. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to

COCs and prevent activities that could damage the integrity of the remedy following transfer of the property.

8.6. PARCEL D-2

The ROD concluded that no further action was necessary for Parcel D-2. At that time, radiological removals had been completed in 2009. In total, 1,988 linear feet of trench and 1,434 cubic yards of soil were excavated; approximately 45 cubic yards of soil was disposed of off site as LLRW. One radiologically impacted building (813) was screened and remediated. Radiological surveys and removal actions completed in Parcel D-2 were potentially compromised, and corrective actions are required to determine if the RAOs have been achieved.

8.7. PARCEL G

The remedies completed to date for Parcel G are protective of human health and the environment, noting that the radiological removal actions are being retested. Previous soil removals and placement of durable covers on upland areas have achieved the RAO of preventing exposure to contaminants in soil. Data collected during ongoing groundwater monitoring are used to monitor COCs that could pose a risk to human health or the environment. Pre-ROD groundwater treatment using ZVI injection at IR-09 and IR-71 has been performed, and groundwater monitoring is currently being conducted in accordance with the RAMP. Radiological surveys and removal actions completed in Parcel G were potentially compromised, and corrective actions are required to determine if the RAOs have been achieved. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property.

8.8. PARCEL UC-1

The remedies completed to date for Parcel UC-1 are protective of human health and the environment, noting that the radiological removal actions are being retested. Previous soil removals and placement of durable covers on upland areas have achieved the RAO of preventing exposure to contaminants in soil. Radiological surveys and removal actions completed in Parcel UC-1 were potentially compromised, and corrective actions are required to determine if the RAOs have been achieved. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer are effectively preventing exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property.

8.9. PARCEL UC-2

The remedies completed to date for Parcel UC-2 are protective of human health and the environment, noting that the radiological removal actions are being retested. Previous soil removals and placement of durable covers on upland areas have achieved the RAO of preventing exposure to contaminants in soil. Data

collected during ongoing groundwater monitoring were used to monitor COCs that could pose a risk to human health or the environment and have demonstrated that the RAO for preventing exposure to contaminants in groundwater has been achieved. Radiological surveys and removal actions completed in Parcel UC-2 were potentially compromised, and corrective actions are required to determine if the RAOs have been achieved. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property.

8.10. PARCEL UC-3

The remedies completed to date for Parcel UC-3 are protective of human health and the environment, noting that the radiological removal actions are being retested. Previous soil removals and placement of durable covers on upland areas have achieved the RAO of preventing exposure to contaminants in soil. Data collected during ongoing groundwater monitoring were used to monitor COCs that could pose a risk to human health or the environment and have demonstrated that the RAO for preventing exposure to contaminants in groundwater has been achieved. Radiological surveys and removal actions completed in Parcel UC-3 were potentially compromised, and corrective actions are required to determine if the RAOs have been achieved. The effective implementation of IC performance objectives through land use and activity restrictions incorporated into deeds and CRUPs at the time of transfer will effectively prevent exposure to COCs and prevent activities that could damage the integrity of the remedy following transfer of the property.

Section 9. Next Review

The next five-year review will be completed in 2023, 5 years from the date of this Fourth Five-Year Review Report.

Figures

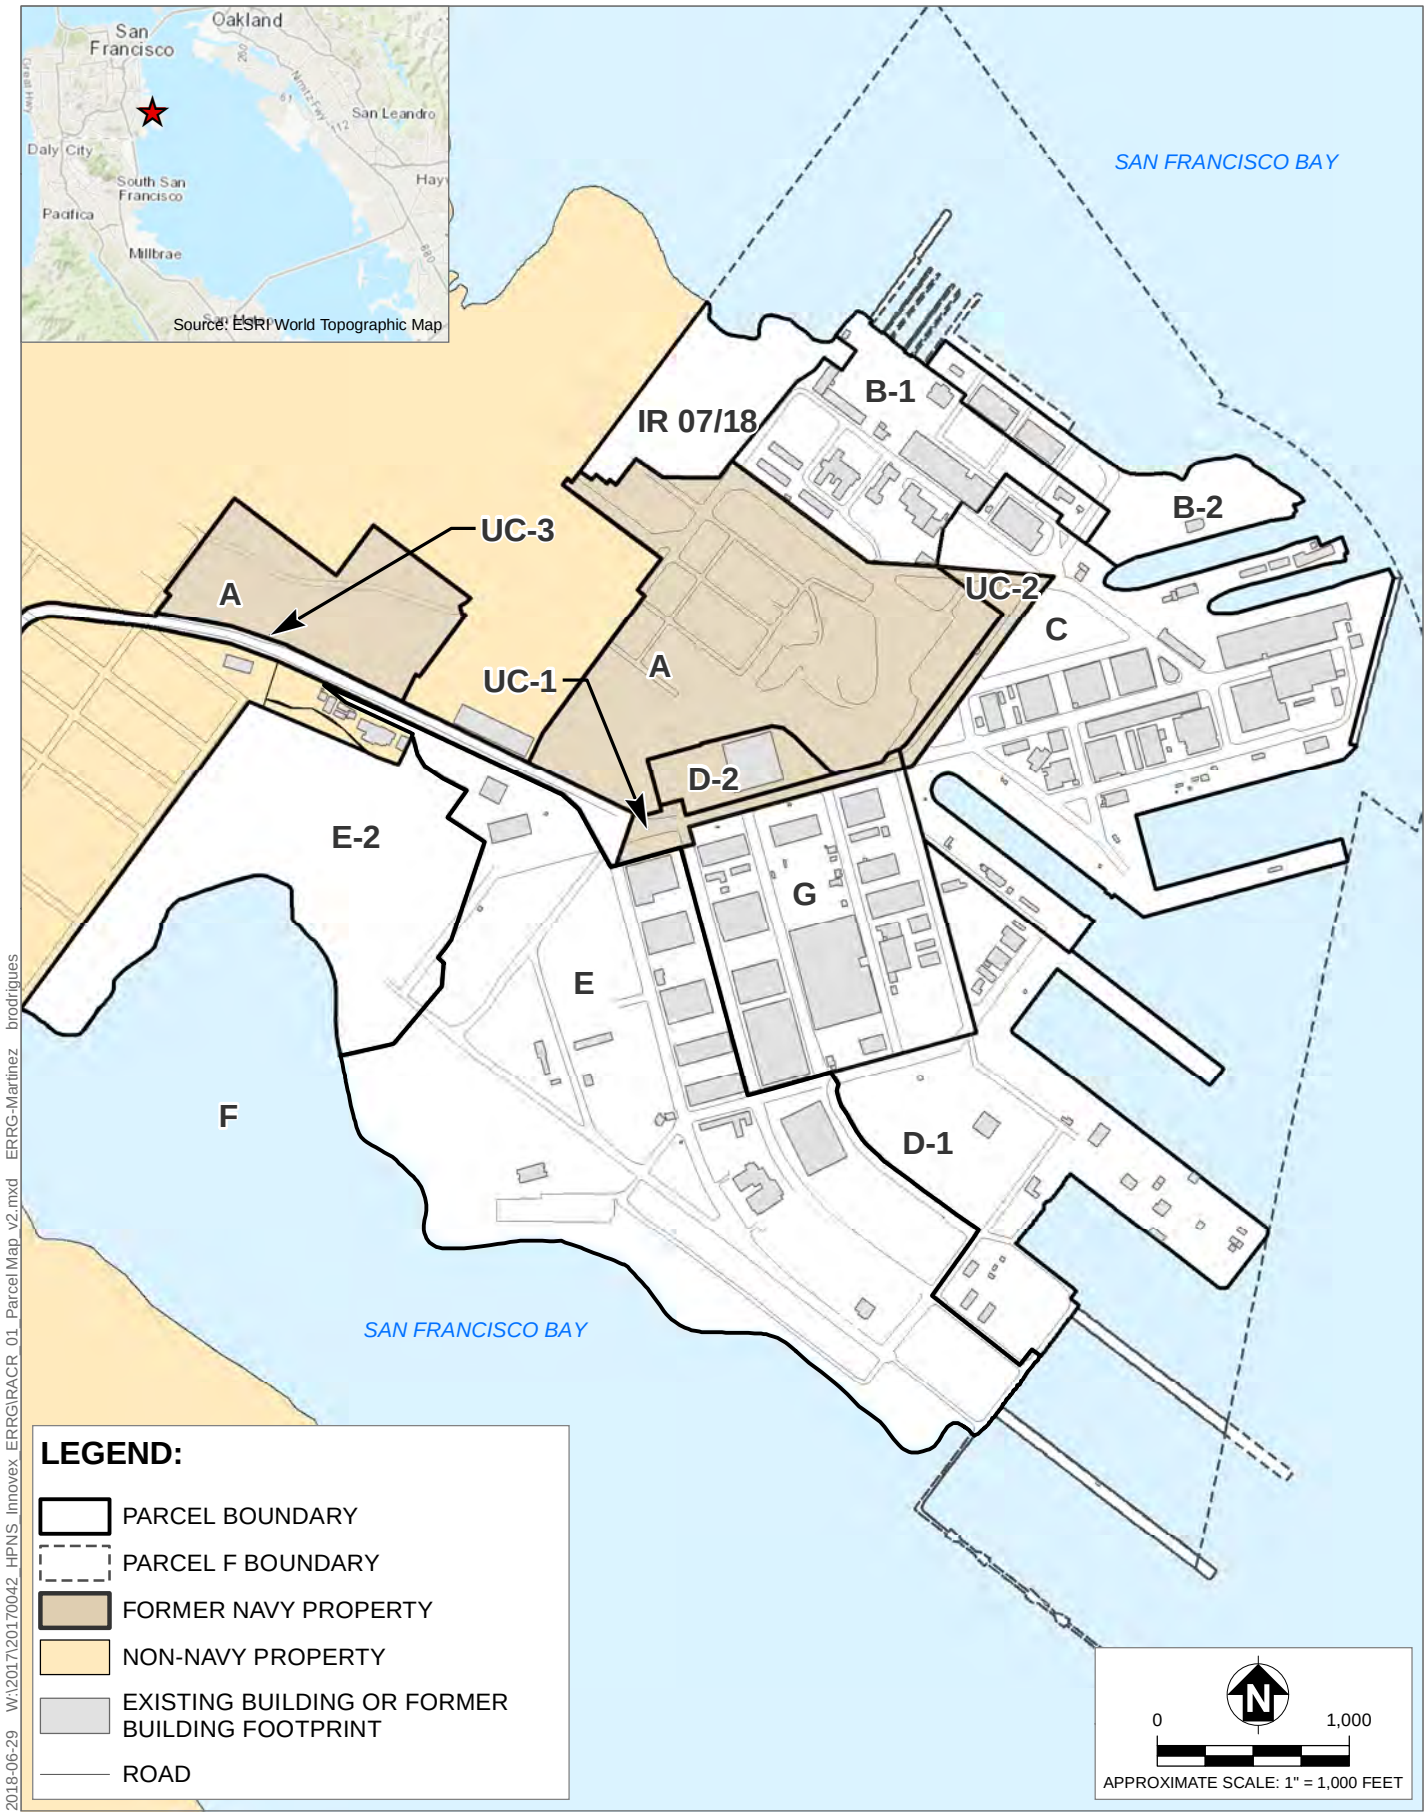

2018-06-29 W:\2017\20170042_HPNS_Innovex_ERRG\RACR_01_Parcel Map_v2.mxd ERRG-Martinez brodrigues

Figure 1. Parcel Map

Fourth Five-Year Review of Remedial Actions, Hunters Point Naval Shipyard, San Francisco, California

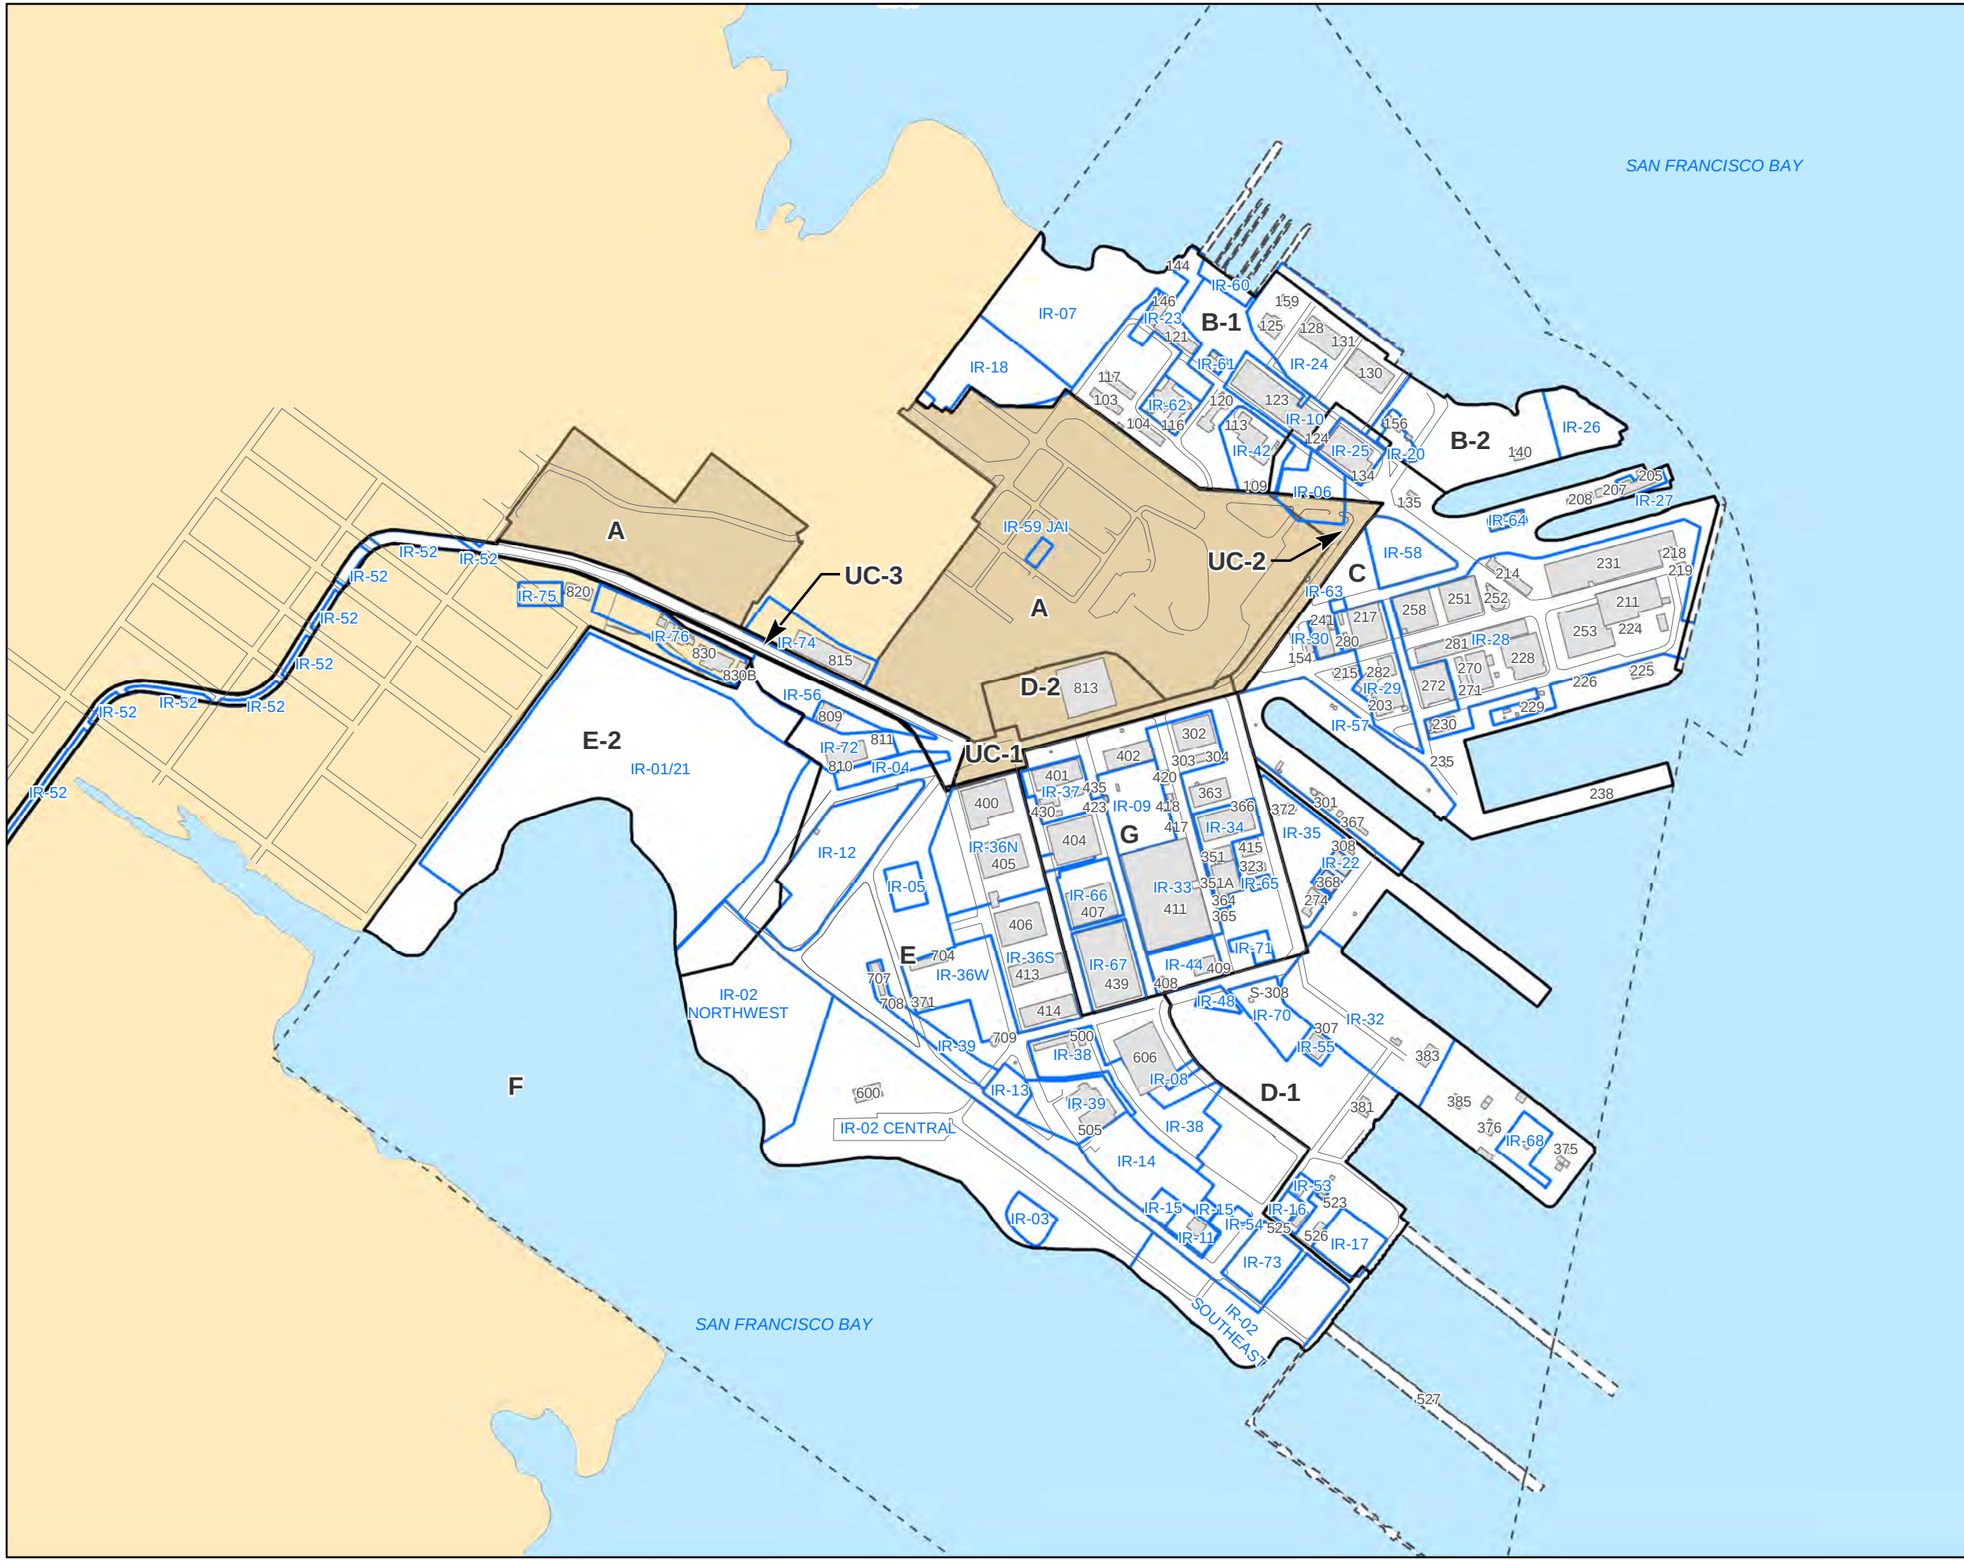

Hunters Point Naval Shipyard, San Francisco, California

Department of the Navy, BRAC PMO West, San Diego, California

FIGURE 2

INSTALLATION RESTORATION SITES

W:\2017\20170042_HPNS_Innovex_ERRG\RACR_02_IR_Sites_rev1.mxd Last updated: 6/29/2018 at 4:51:31 PM

NON-NAVY PROPERTY

EARL STREET

INNES AVENUE

IR18MW21A

IR18MW100B

IR18MW101B

IR18MW92A

IR07MW23A

IR07MW25A

IR07MW24A

IR07MW21A1

IR07MW94A

IR07MW93A

IR07MWS-4

IR07MW26A

IR07MWS-2

IR07MW20A1

SETTLEMENT MONUMENT 2

SETTLEMENT MONUMENT 1

DRAINAGE SWALE

3 FT. OF COVER

2 FT. OF COVER

SG-PT18

SG-PT19

SG-PT17

SG-PT15

SG-PT16

DONAHUE STREET

EXISTING DRAINAGE CHANNEL

BUILDING 117

SHORELINE REVETMENT

CREST OF REVETMENT

TOE OF REVETMENT

SAN FRANCISCO BAY

MLLW = −3.56 MSL

ASPHALT PARKING

ASPHALT

UNPAVED

LEGEND:

- SHORELINE REVETMENT (RIPRAP)
- ASPHALT COVER
- GROUNDWATER MONITORING WELL
- FORMER METHANE MONITORING PROBE
- SETTLEMENT MONUMENT
- DRAINAGE SWALE
- AREA REQUIRING INSTITUTIONAL CONTROLS FOR POTENTIAL RADIONUCLIDES
- IR-07 BOUNDARY
- IR-18 BOUNDARY
- EXISTING CONTOUR
- FINAL CONTOUR 3-FT. COVER
- FINAL CONTOUR 2-FT. COVER
- FINAL CONTOUR REVETMENT
- FENCE

N

0' 120'

SCALE: 1"=120'

NAVFAC	CLIENT: DEPARTMENT OF THE NAVY BRAC PMO WEST SAN DIEGO, CALIFORNIA	OVERVIEW OF REMEDY COMPONENTS FOR IR-07/18		
	LOCATION: HUNTERS POINT NAVAL SHIPYARD SAN FRANCISCO, CALIFORNIA	DRAWN BY: SC 04/18/12	CHECKED BY: JS 04/18/12	PROJECT NO. 20170042	FIG NO. 3

FILE NAME: C:\Civil 3D Projects\ERRG\Projects\20170042\Figures_B-1\O&M 5 year\Fig-3.dwg LAYOUT NAME: 3 PLOTTED: Saturday, June 30, 2018 - 1:08pm

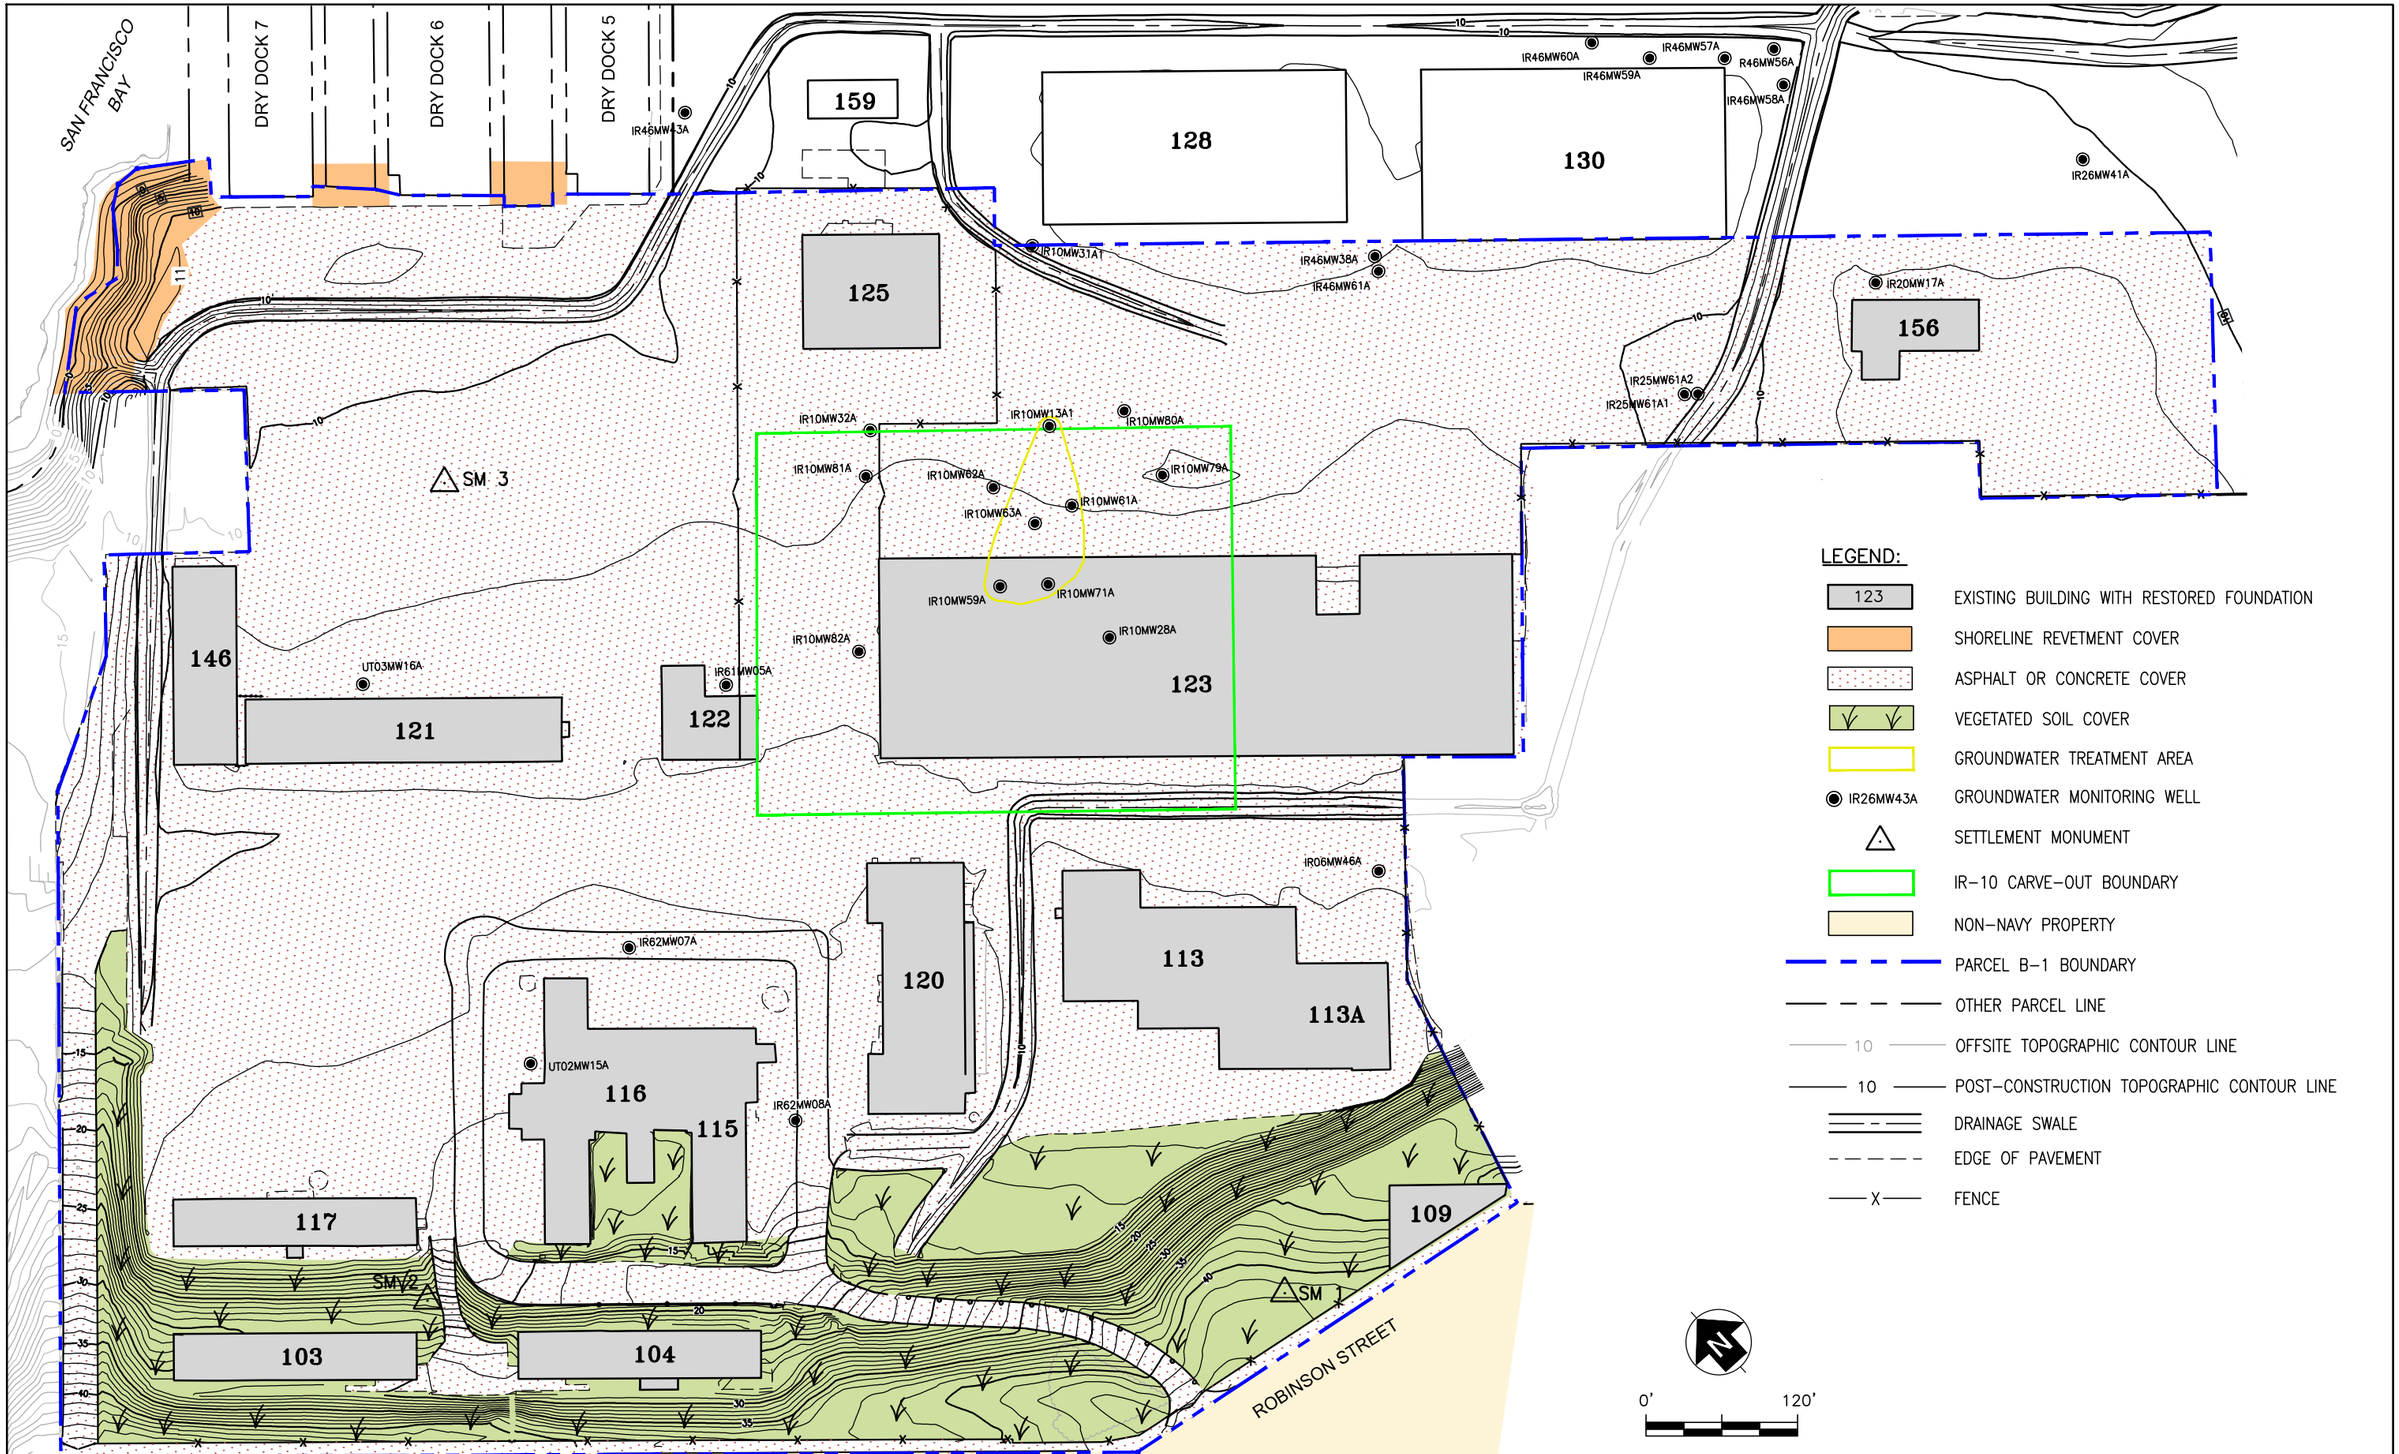

NAVFAC	CLIENT: DEPARTMENT OF THE NAVY BRAC PMO WEST SAN DIEGO, CALIFORNIA	OVERVIEW OF REMEDY COMPONENTS FOR PARCEL B-1		
	LOCATION: HUNTERS POINT NAVAL SHIPYARD SAN FRANCISCO, CALIFORNIA	DRAWN BY: SC 09/27/16	CHECKED BY: JS 09/27/16	PROJECT NO. 20170042	FIG NO. 4

FILE NAME: C:\Civil 3D Projects\ERRG\Projects\20170042\figures_B-1\O&M 5 year\Fig-4.dwg LAYOUT NAME: 4 PLOTTED: Saturday, June 30, 2018 - 1:09pm

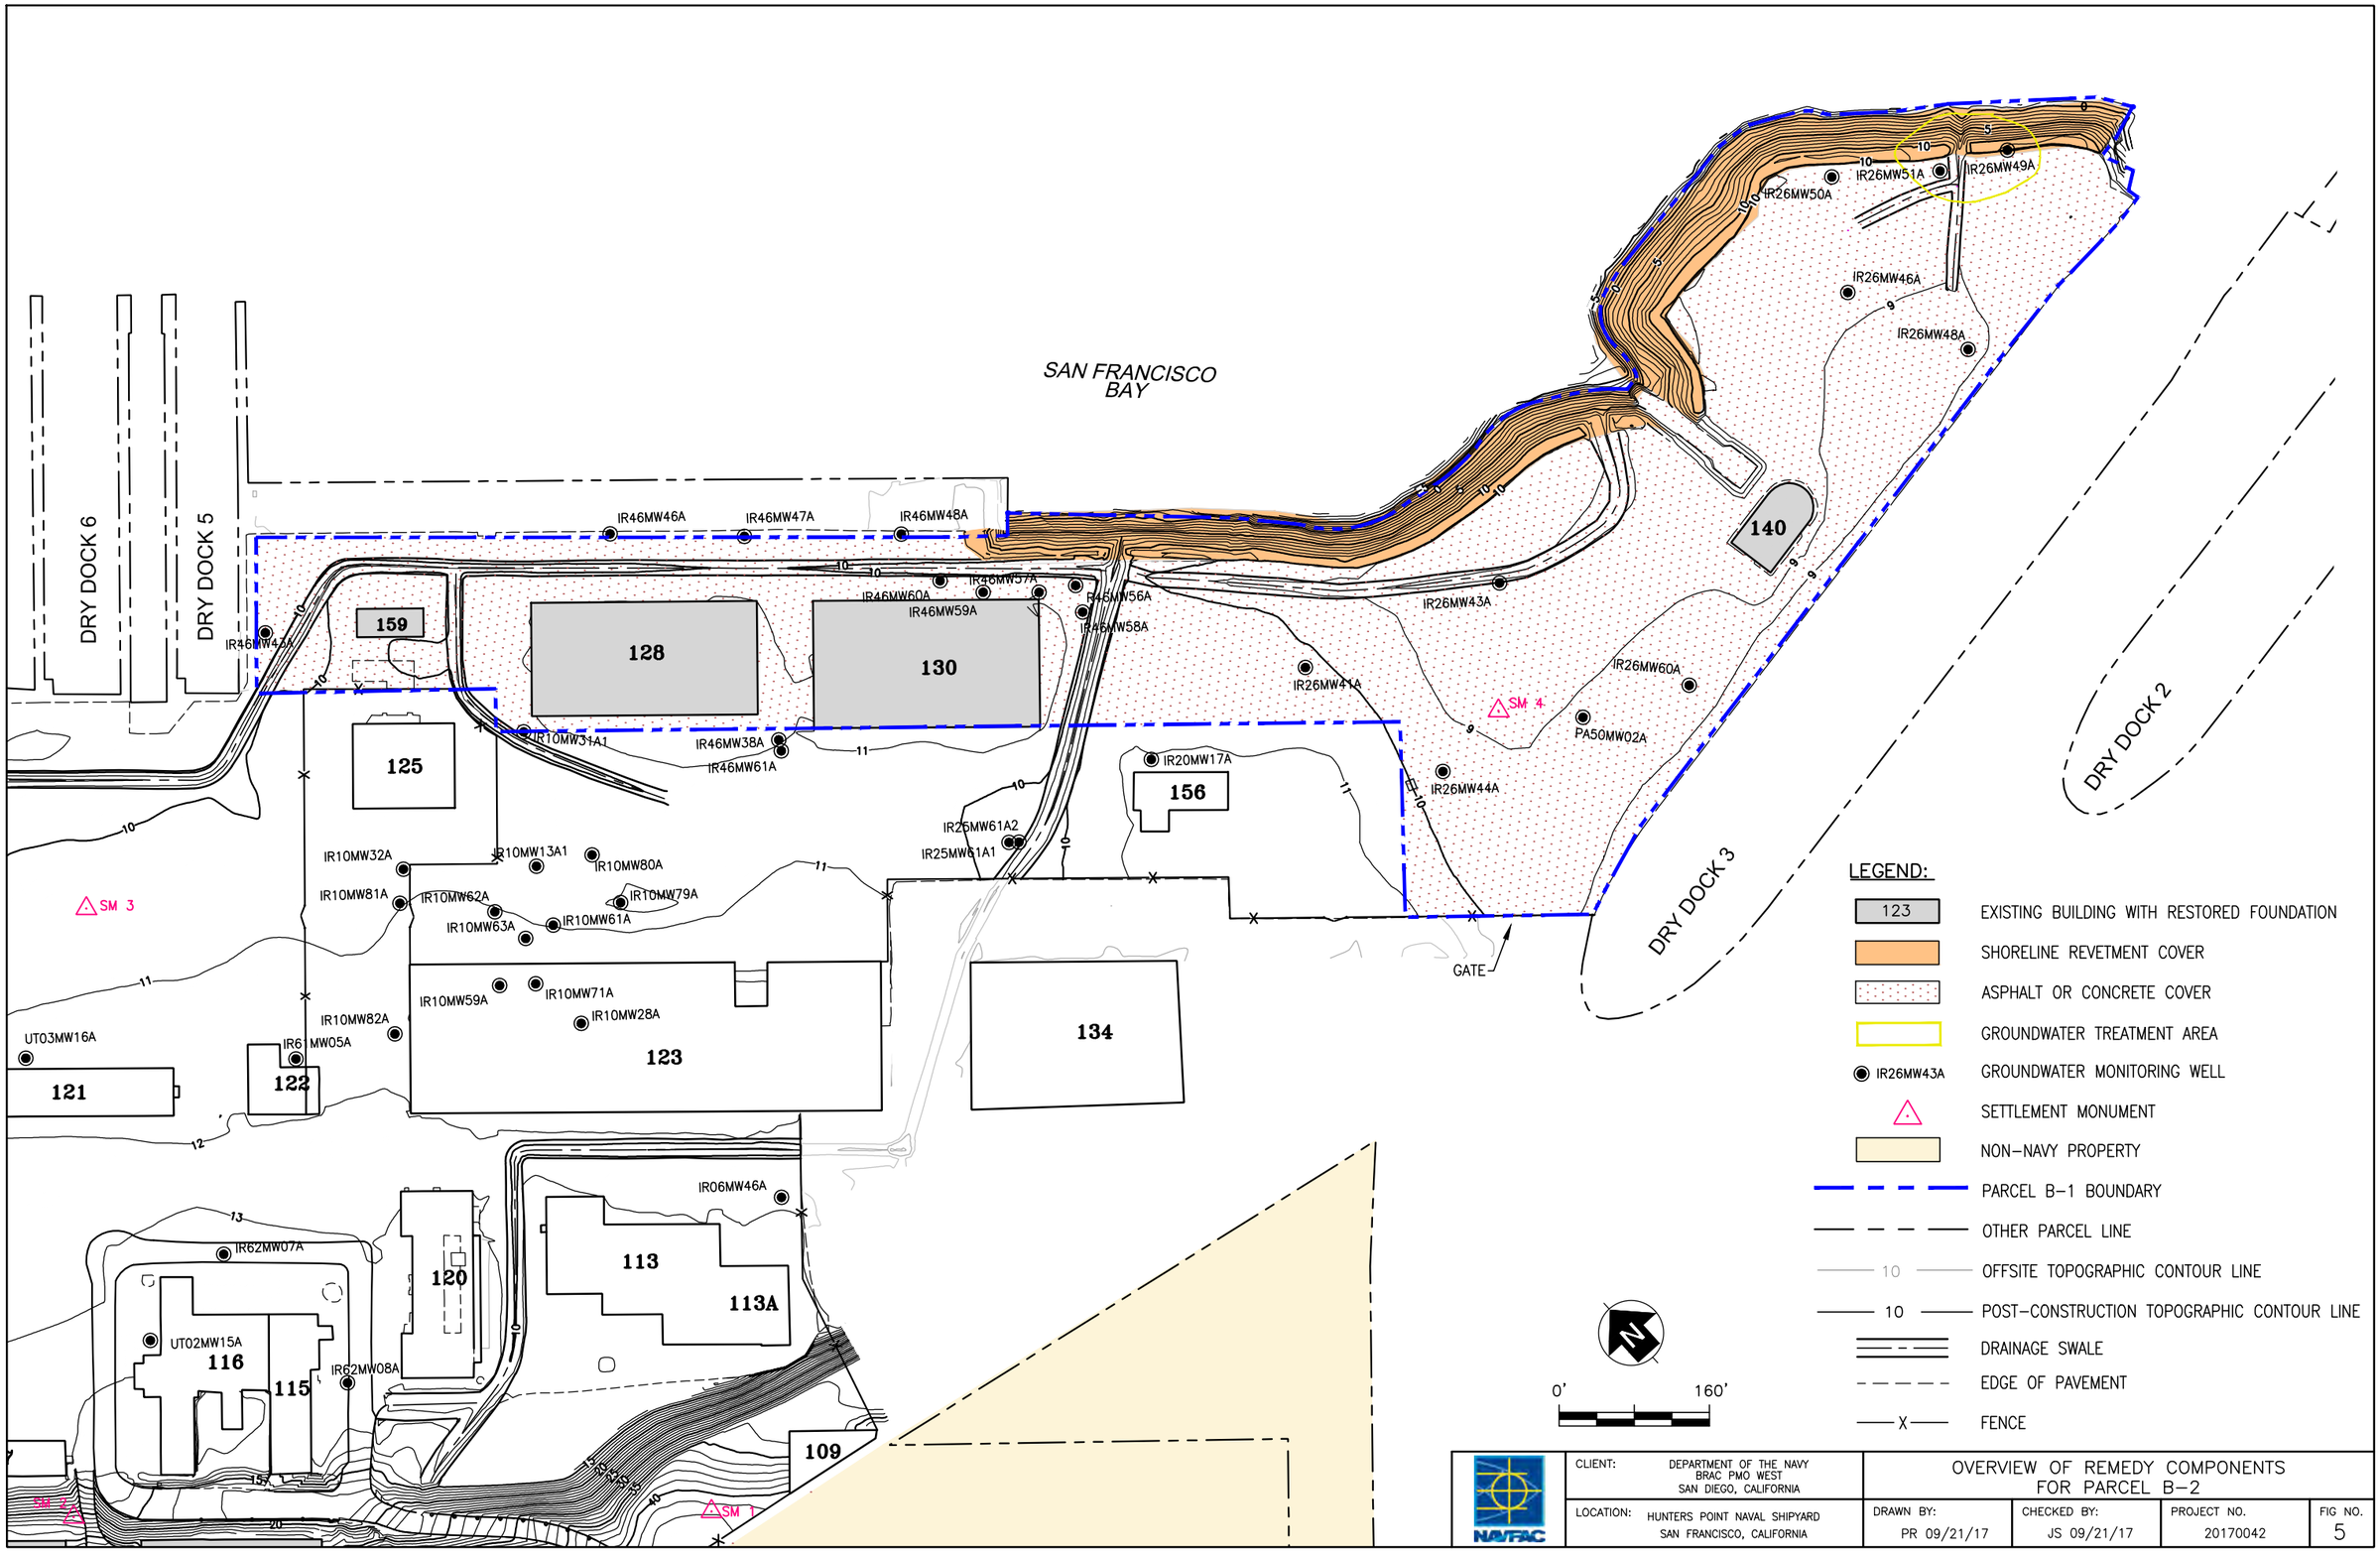
SAN FRANCISCO BAY
DRY DOCK 6
DRY DOCK 5
DRY DOCK 3
DRY DOCK 2
GATE
159
128
130
125
156
140
121
122
123
134
120
113
113A
116
115
109
IR46MW46A
IR46MW47A
IR46MW48A
IR46MW43A
IR46MW57A
IR46MW60A
IR46MW59A
IR46MW56A
IR46MW58A
IR46MW38A
IR46MW61A
IR10MW31A1
IR26MW43A
IR26MW41A
IR26MW60A
PA50MW02A
IR26MW44A
IR26MW51A
IR26MW49A
IR26MW50A
IR26MW46A
IR26MW48A
IR20MW17A
IR25MW61A2
IR25MW61A1
IR10MW32A
IR10MW13A1
IR10MW80A
IR10MW81A
IR10MW62A
IR10MW79A
IR10MW63A
IR10MW61A
IR10MW59A
IR10MW71A
IR10MW28A
IR10MW82A
IR6 MW05A
UT03MW16A
IR06MW46A
IR62MW07A
UT02MW15A
IR62MW08A
SM 1
SM 2
SM 3
SM 4
LEGEND:
123 EXISTING BUILDING WITH RESTORED FOUNDATION
SHORELINE REVETMENT COVER
ASPHALT OR CONCRETE COVER
GROUNDWATER TREATMENT AREA
IR26MW43A GROUNDWATER MONITORING WELL
SETTLEMENT MONUMENT
NON-NAVY PROPERTY
PARCEL B-1 BOUNDARY
OTHER PARCEL LINE
10 OFFSITE TOPOGRAPHIC CONTOUR LINE
10 POST-CONSTRUCTION TOPOGRAPHIC CONTOUR LINE
DRAINAGE SWALE
EDGE OF PAVEMENT
X FENCE
0'
160'
NAVFAC
CLIENT: DEPARTMENT OF THE NAVY BRAC PMO WEST SAN DIEGO, CALIFORNIA
LOCATION: HUNTERS POINT NAVAL SHIPYARD SAN FRANCISCO, CALIFORNIA
OVERVIEW OF REMEDY COMPONENTS FOR PARCEL B-2
DRAWN BY: PR 09/21/17
CHECKED BY: JS 09/21/17
PROJECT NO. 20170042
FIG NO. 5
FILE NAME: C:\Civil 3D Projects\ERRG\Projects\20170042\figures_B-1\O&M 5 year\Fig-5.dwg LAYOUT NAME: 5 PLOTTED: Saturday, June 30, 2018 - 1:11pm

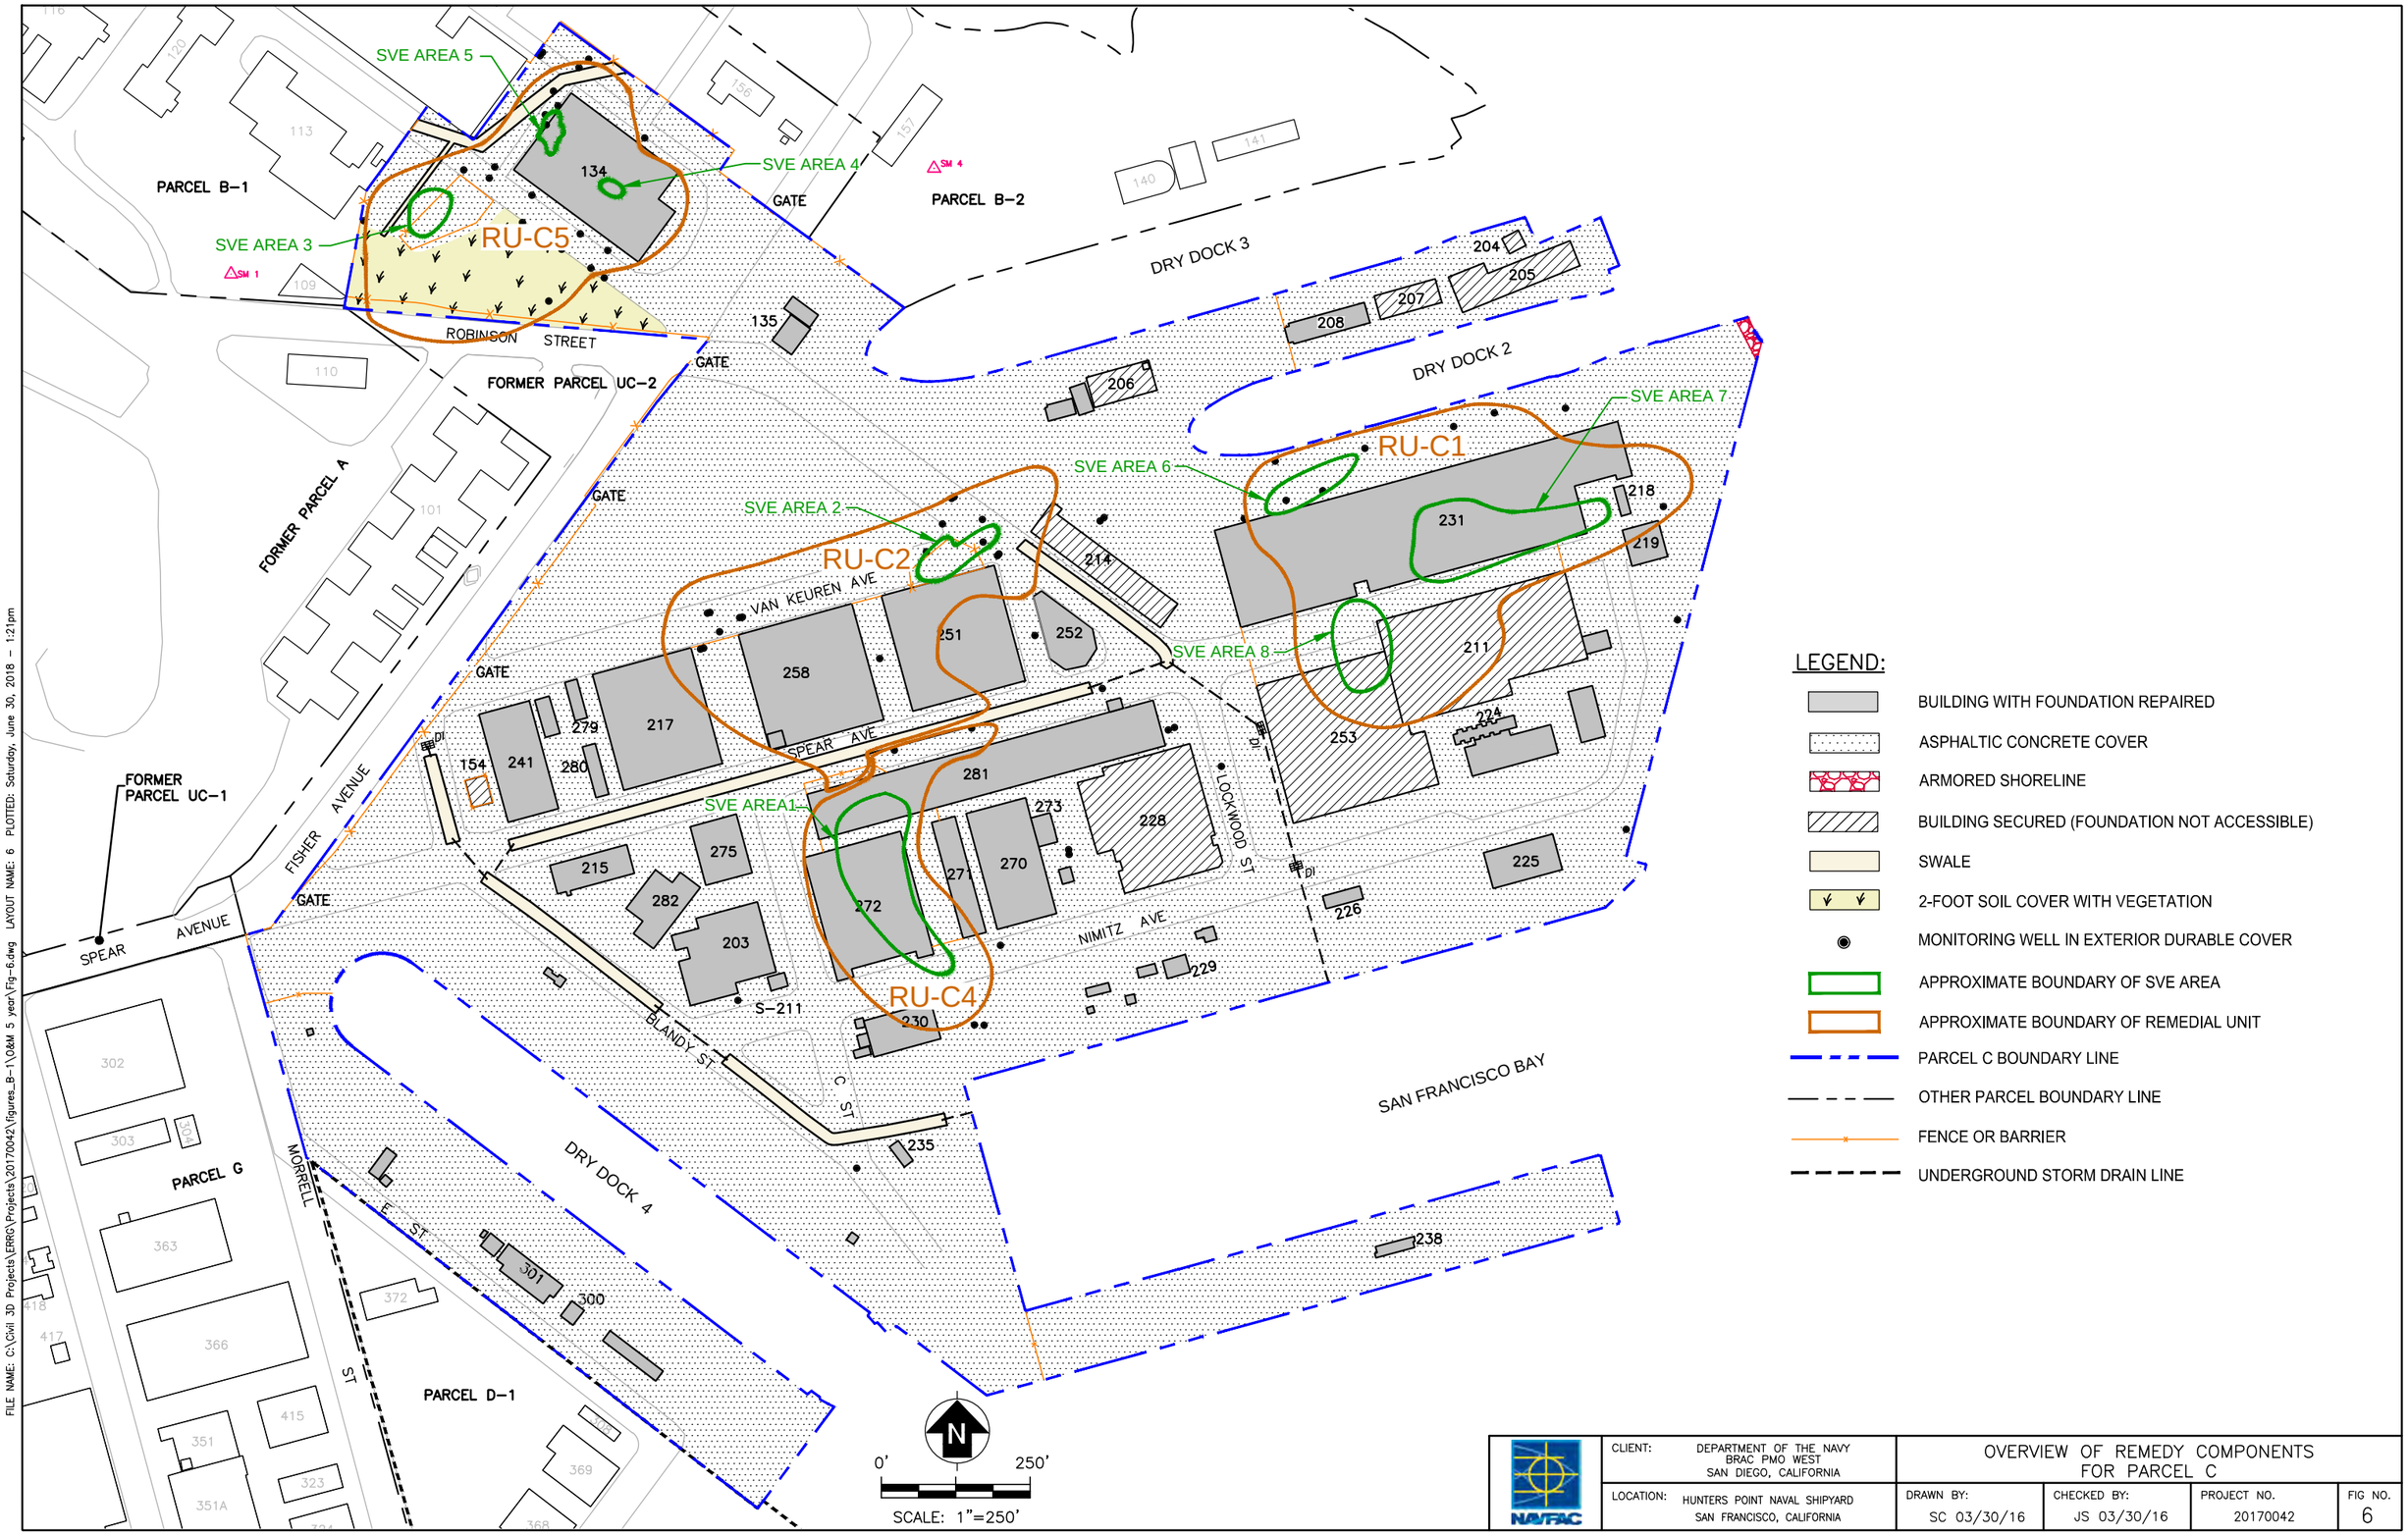

LEGEND:

- BUILDING WITH FOUNDATION REPAIRED
- ASPHALTIC CONCRETE COVER
- ARMORED SHORELINE
- BUILDING SECURED (FOUNDATION NOT ACCESSIBLE)
- SWALE
- 2-FOOT SOIL COVER WITH VEGETATION
- MONITORING WELL IN EXTERIOR DURABLE COVER
- APPROXIMATE BOUNDARY OF SVE AREA
- APPROXIMATE BOUNDARY OF REMEDIAL UNIT
- PARCEL C BOUNDARY LINE
- OTHER PARCEL BOUNDARY LINE
- FENCE OR BARRIER
- UNDERGROUND STORM DRAIN LINE

NAVFAC	CLIENT: DEPARTMENT OF THE NAVY BRAC PMO WEST SAN DIEGO, CALIFORNIA	OVERVIEW OF REMEDY COMPONENTS FOR PARCEL C		
	LOCATION: HUNTERS POINT NAVAL SHIPYARD SAN FRANCISCO, CALIFORNIA	DRAWN BY: SC 03/30/16	CHECKED BY: JS 03/30/16	PROJECT NO. 20170042	FIG NO. 6

FILE NAME: C:\Civil 3D Projects\ERRG\Projects\20170042\figures_B-1\O&M 5 year\Fig-6.dwg LAYOUT NAME: 6 PLOTTED: Saturday, June 30, 2018 - 1:21pm

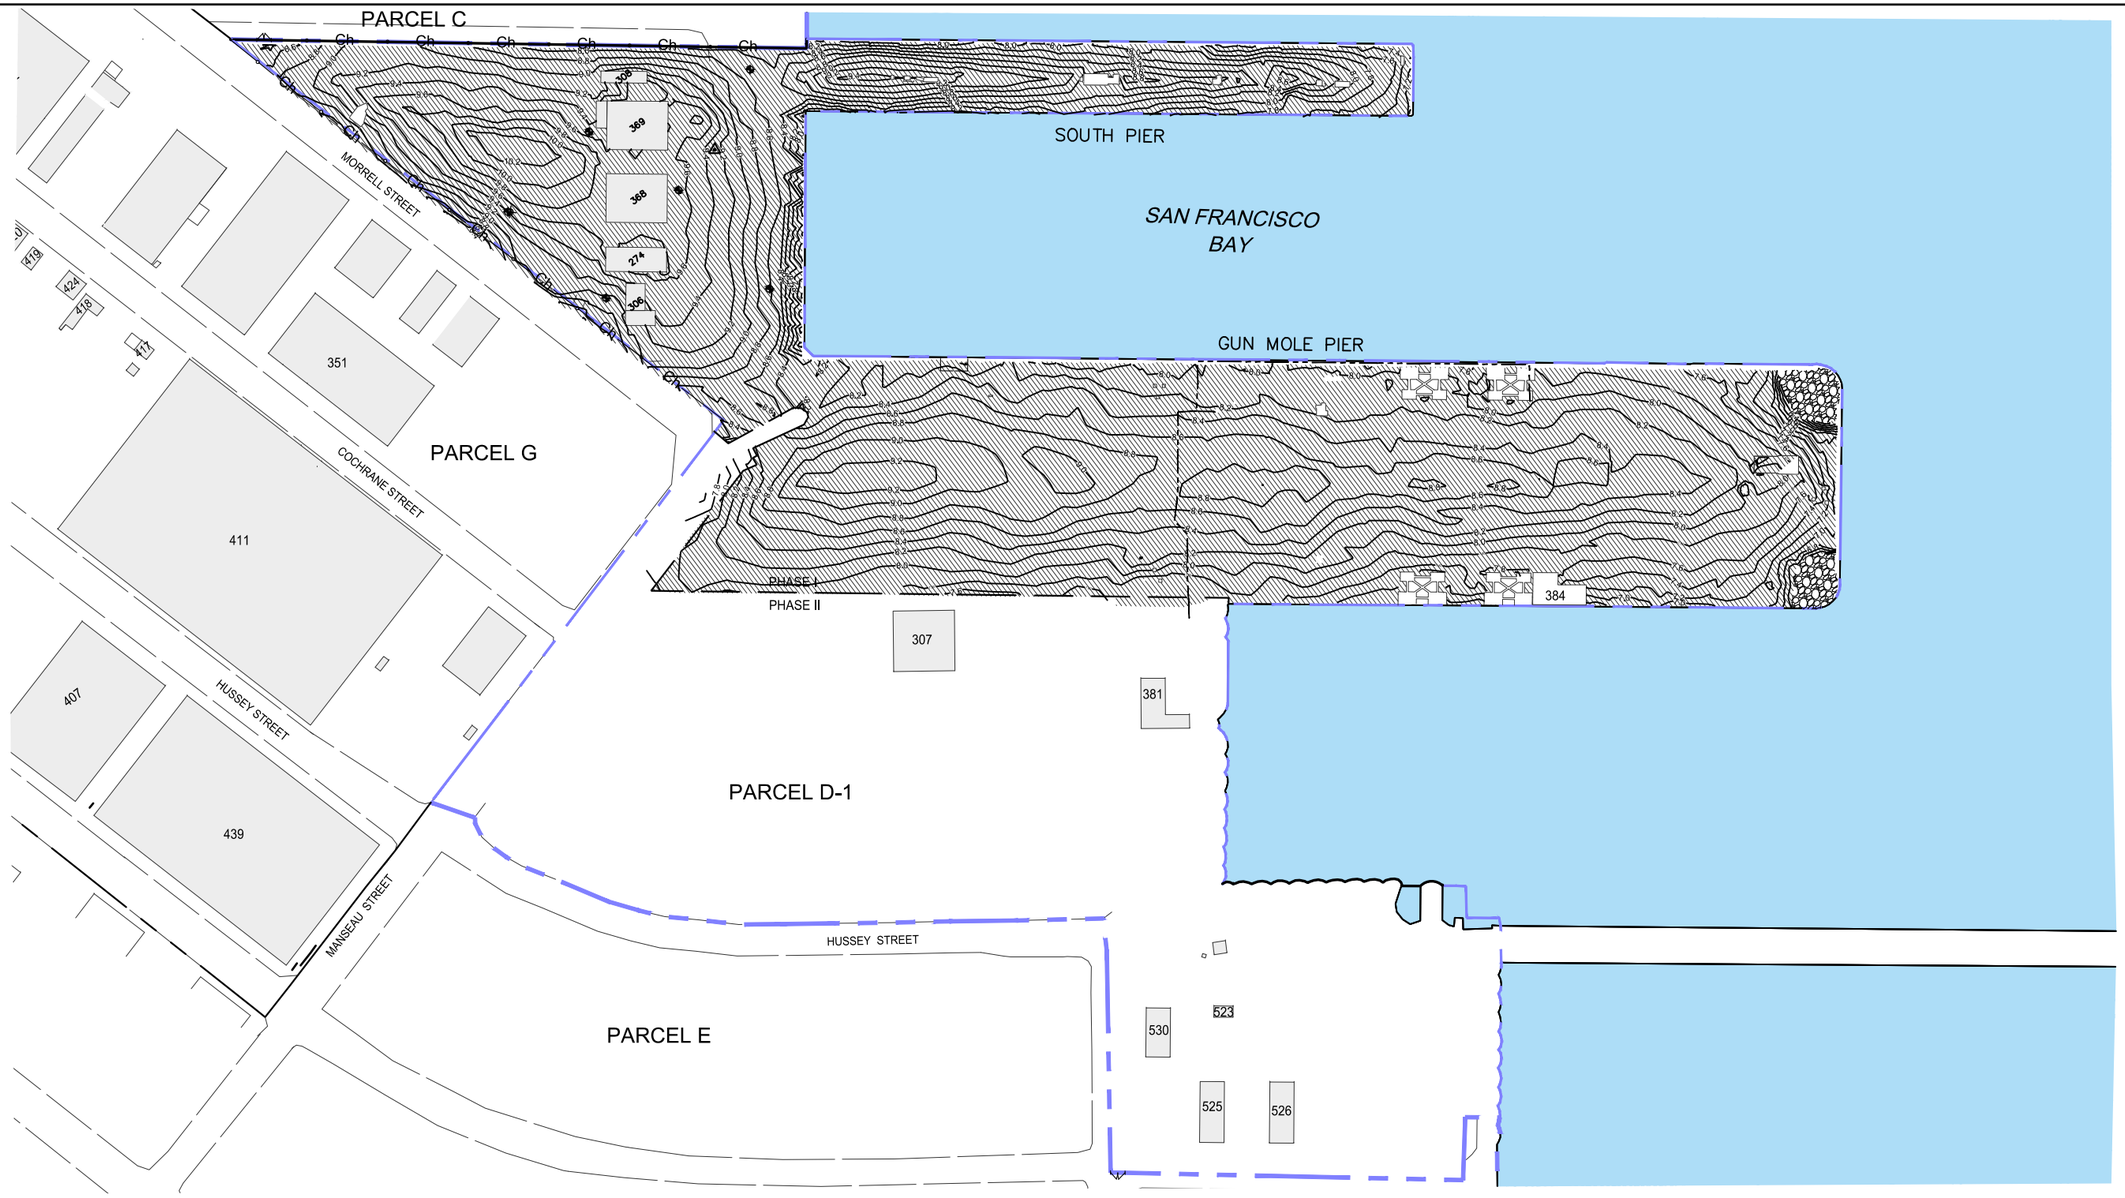

LEGEND:

- RIPRAP STABILIZATION
- ASPHALT
- EXISTING BUILDING
- ELECTRICAL CONDUIT
- EXISTING MONITORING WELL
- Ch — SITE SECURITY FENCE
- GATE
- SURVEY MONUMENT

0 250' 500'

SCALE: 1" = 250'

NAVFAC	CLIENT: DEPARTMENT OF THE NAVY BRAC PMO WEST SAN DIEGO, CALIFORNIA	OVERVIEW OF REMEDY COMPONENTS FOR PARCEL D-1		
	LOCATION: HUNTERS POINT NAVAL SHIPYARD SAN FRANCISCO, CALIFORNIA	DRAWN BY: PR 09/21/17	CHECKED BY: JS 09/21/17	PROJECT NO. 20170042	FIG NO. 7

FILE NAME: C:\Civil 3D Projects\ERRG\Projects\20170042\figures_B-1\O&M 5 year\Fig-7.dwg LAYOUT NAME: 7 PLOTTED: Saturday, June 30, 2018 - 1:23pm

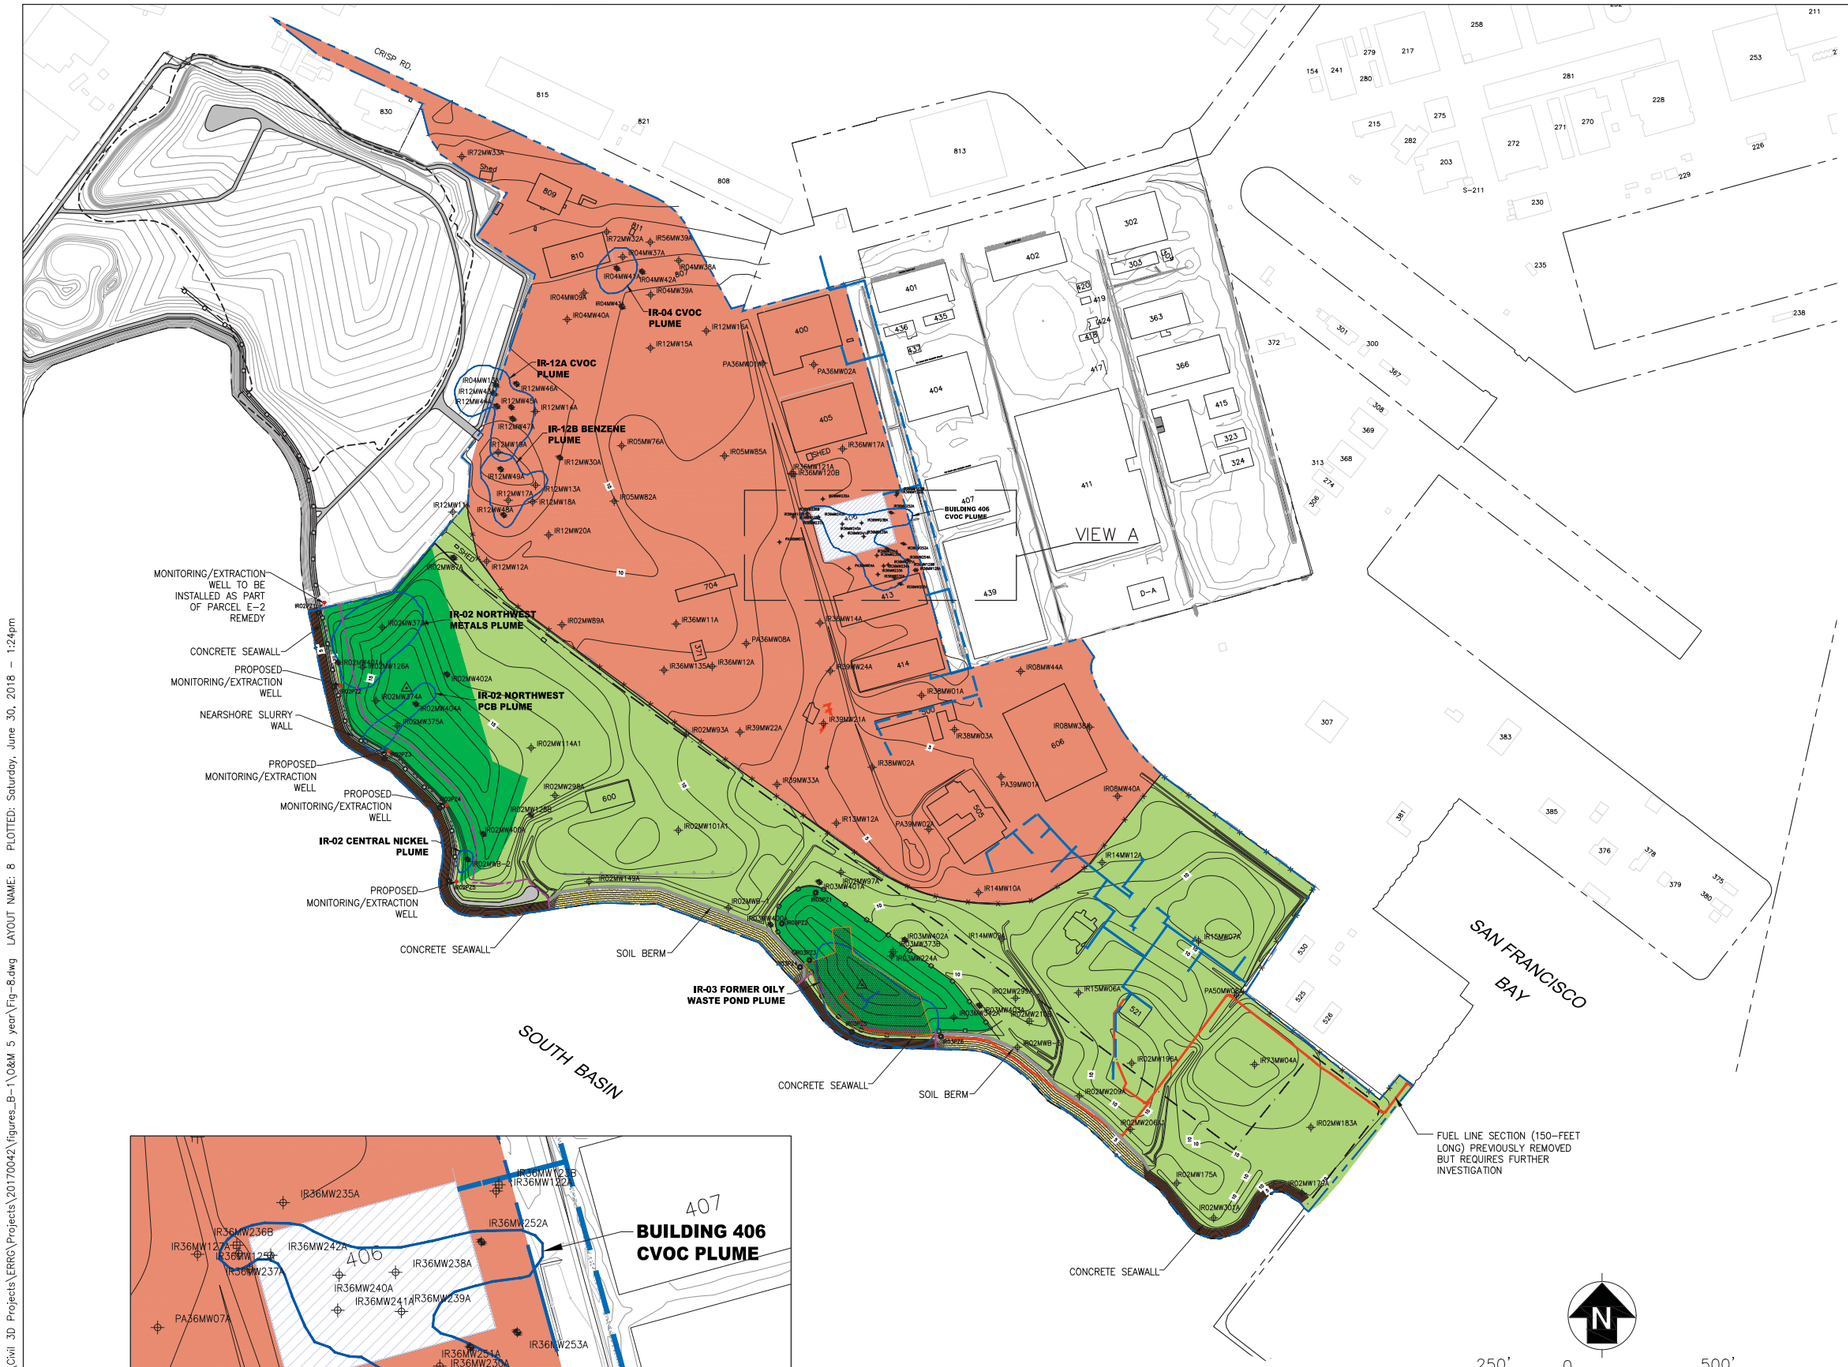

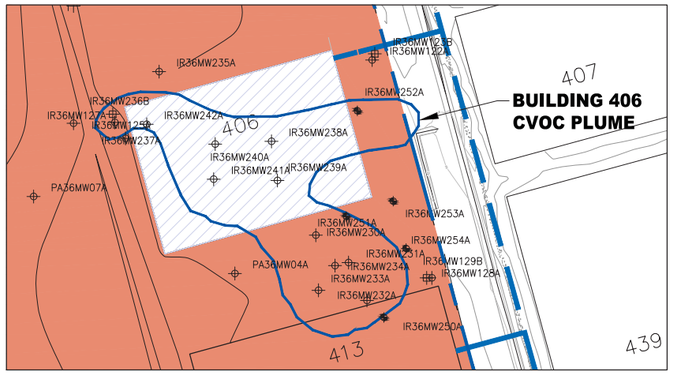

VIEW A
NOT TO SCALE

LEGEND:

- VEGETATIVE SOIL COVER WITH UNDERLYING PROTECTIVE LINER (COVER TYPE E)
- VEGETATIVE SOIL (COVER TYPE D)
- ASPHALTIC CONCRETE (COVER TYPE A)
- SVE REMEDIATION AREA
- SERVICE ROAD
- SHORELINE REVETMENT (COVER TYPE B)
- SHORELINE NATURAL SAND (COVER TYPE C)
- ISS TREATMENT AREA
- EXISTING FUEL LINES (FIELD VERIFY EXTENT)
- EXISTING STEAM LINES (FIELD VERIFY EXTENT)
- EXISTING STEAM LINES CLOSED IN PLACE (DURING PREVIOUS ACTION)
- SLURRY WALL
- INLAND EXTENT OF DEMARCATION LAYER
- INLAND EXTENT OF GEOGRID REINFORCEMENT
- SOIL BERM
- PARCEL E BOUNDARY
- PARCEL BOUNDARY OTHER
- MOBILE NAPL BOUNDARY
- DRAINAGE CHANNEL
- FINISH GRADE TOPOGRAPHIC CONTOUR LINE (5, 4)
- EXISTING A-AQUIFER GROUNDWATER MONITORING WELL (TO REMAIN)
- EXISTING B-AQUIFER GROUNDWATER MONITORING WELL (TO REMAIN)
- NEW A-AQUIFER GROUNDWATER MONITORING WELL
- NEW B-AQUIFER GROUNDWATER MONITORING WELL
- PROPOSED PIEZOMETER
- NEW SURVEY MONUMENT
- PROPOSED MONITORING/EXTRACTION WELL
- FENCE

N

250' 0 500'

SCALE: 1"=250'

NAVFAC	CLIENT: DEPARTMENT OF THE NAVY BRAC PMO WEST SAN DIEGO, CALIFORNIA	OVERVIEW OF REMEDY COMPONENTS FOR PARCEL E		
	LOCATION: HUNTERS POINT NAVAL SHIPYARD SAN FRANCISCO, CALIFORNIA	DRAWN BY: SC 10/12/16	CHECKED BY: MG 10/12/16	PROJECT NO. 20170042	FIG NO. 8

FILE NAME: C:\Civil 3D Projects\ERRG\Projects\20170042\figures_B-1\O&M 5 year\Fig-8.dwg LAYOUT NAME: 8 PLOTTED: Saturday, June 30, 2018 - 1:24pm

LEGEND:

- FINAL COVER
- WASTE CONSOLIDATION AREA
- FRESHWATER WETLAND (NO GEOSYNTHETIC CAP)
- TIDAL WETLAND
- SERVICE ROAD
- RIPRAP REVETMENT SLOPE PROTECTION
- PARCEL E-2 BOUNDARY
- PROPOSED RIGHT-OF-WAY
- LEACHATE EXTRACTION CONDUIT TRENCH
- GROUNDWATER DIVERSION DRAIN
- LIMIT OF LANDFILL WASTE
- APPROXIMATE LIMIT OF GEOSYNTHETIC CAP
- APPROXIMATE LIMIT OF EXISTING GEOSYNTHETIC CAP
- PERIMETER DRAINAGE CHANNEL
- EXISTING GROUNDWATER MONITORING WELL (TO REMAIN)
- EXISTING GAS MONITORING PROBE
- EXISTING LFG VENT
- EXISTING LFG VENT (TO BE DECOMMISSIONED)
- EXISTING LFG ROI TEST WELL
- NEW PIEZOMETER
- NEW GAS MONITORING PROBE
- NEW GROUNDWATER MONITORING WELL
- NEW LANDFILL GAS EXTRACTION WELL
- NEW LEACHATE MONITORING/EXTRACTION WELL
- NEW SURVEY MONUMENT
- DRAIN INLET
- 5 4 FINISH GRADE TOPOGRAPHIC CONTOUR LINE
- 1 0 EXISTING TOPOGRAPHIC CONTOUR LINE
- SLURRY WALL
- FENCE

NAVFAC	CLIENT: DEPARTMENT OF THE NAVY BRAC PMO WEST SAN DIEGO, CALIFORNIA	OVERVIEW OF REMEDY COMPONENTS FOR PARCEL E		
	LOCATION: HUNTERS POINT NAVAL SHIPYARD SAN FRANCISCO, CALIFORNIA	DRAWN BY: SC 10/12/16	CHECKED BY: MG 10/12/16	PROJECT NO. 20170042	FIG NO. 9

FILE NAME: C:\Civil 3D Projects\ERRG\Projects\20170042\figures_B-1\O&M 5 year\Fig-9.dwg LAYOUT NAME: 9 PLOTTED: Monday, July 02, 2018 - 11:52pm

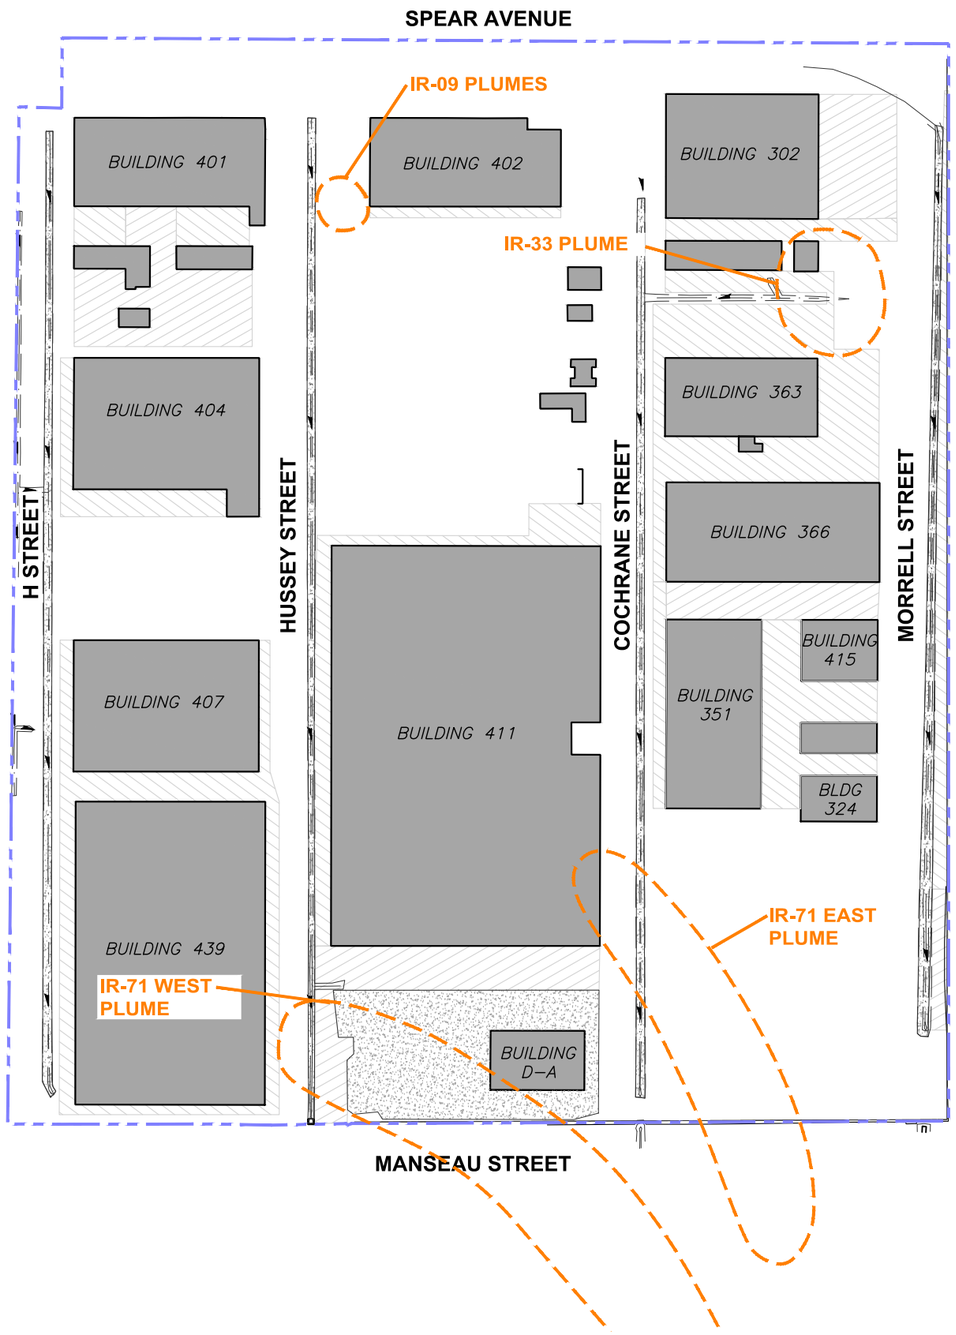

LEGEND:

- SEAL COAT APPLICATION (11%)
- 2" AC OVERLAY ON EXISTING AC (5%)
- CONCRETE PATCHING AND SHOTCRETE (6%)
- CRACK REPAIR/SEALING ON BUILDING SLAB (34%)
- NEW PAVEMENT CONSTRUCTION (44%) (REMAINDER OF SITE)
- DRAINAGE SWALE
- PARCEL BOUNDARY

N

0 200 Feet

NAVFAC	CLIENT: DEPARTMENT OF THE NAVY BRAC PMO WEST SAN DIEGO, CALIFORNIA	OVERVIEW OF REMEDY COMPONENTS FOR PARCEL G		
	LOCATION: HUNTERS POINT NAVAL SHIPYARD SAN FRANCISCO, CALIFORNIA	DRAWN BY: SC 03/30/16	CHECKED BY: JS 03/30/16	PROJECT NO. 20170042	FIG NO. 10

FILE NAME: G:\Civil 3D Projects\ERRG\Projects\20170042\figures_B-1\O&M 5 year\Fig-10.dwg LAYOUT NAME: 10 PLOTTED: Saturday, June 30, 2018 - 1:26pm

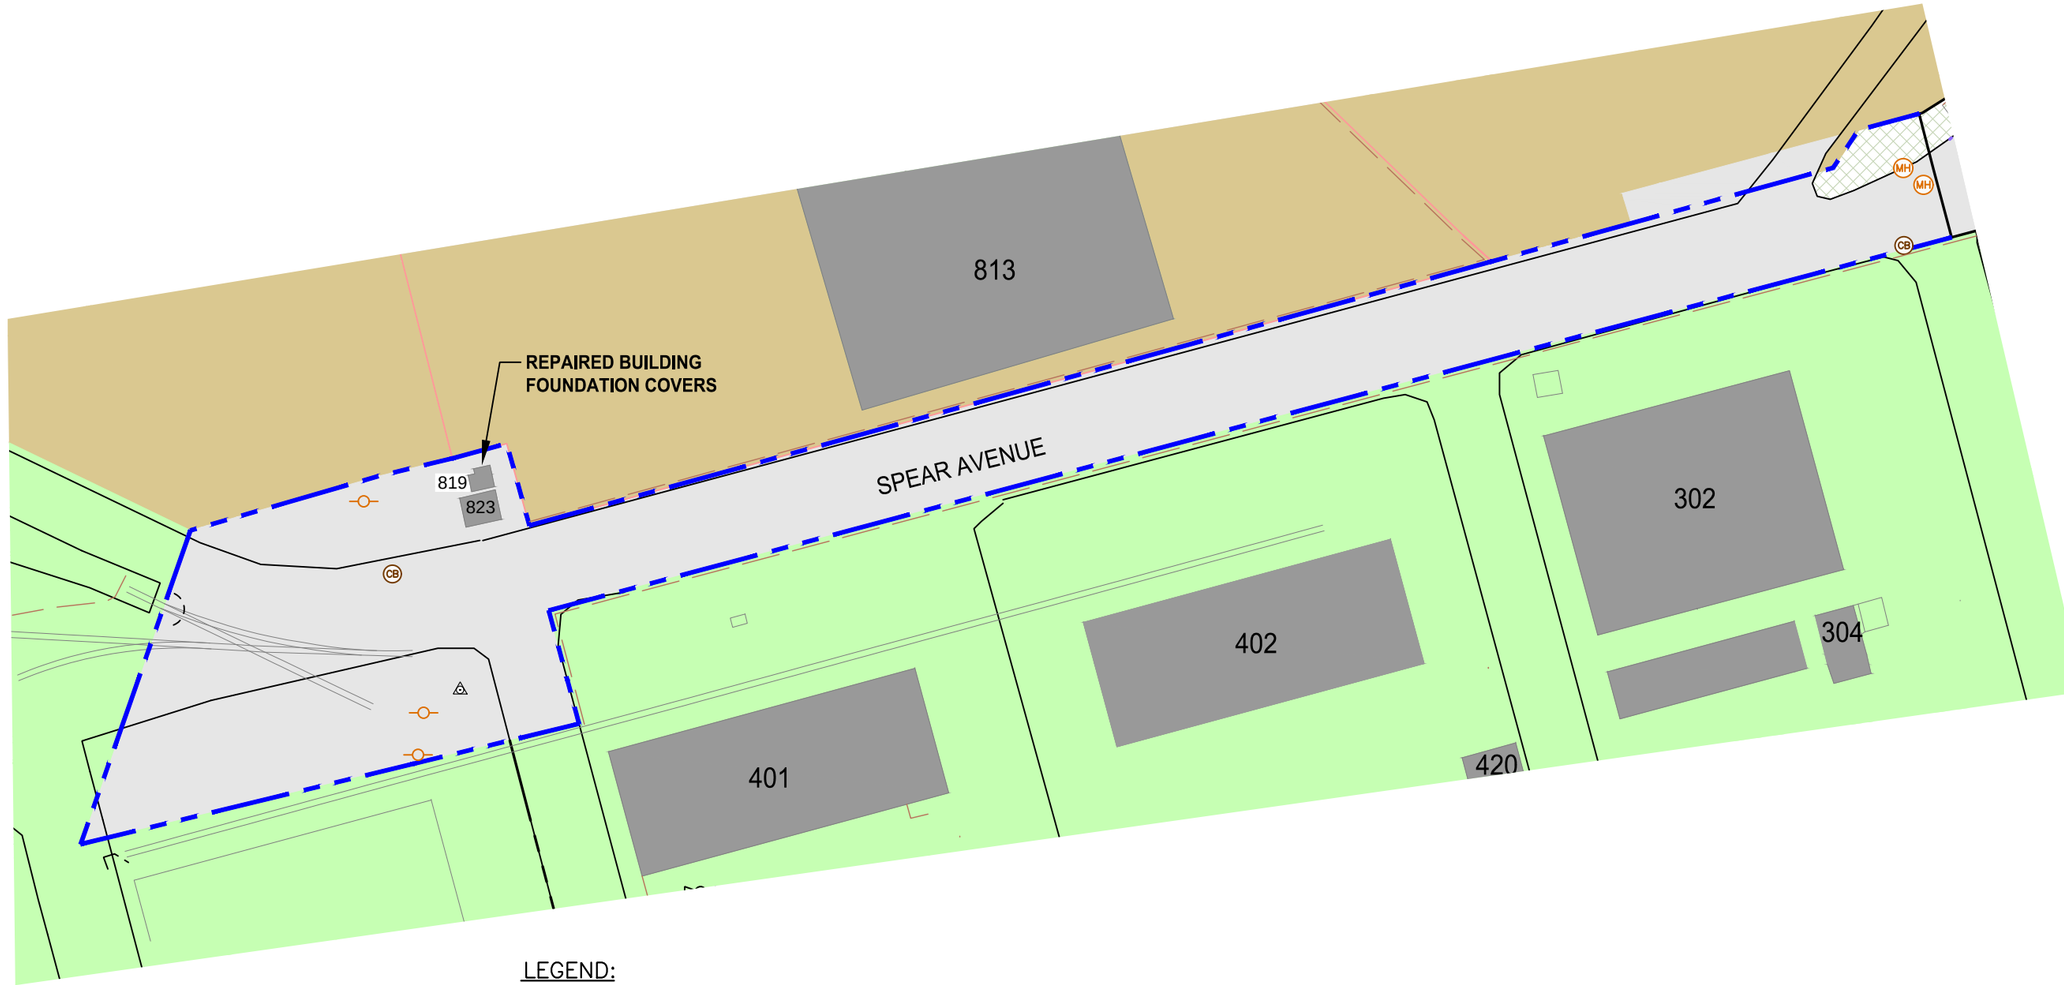

LEGEND:

- EXISTING BUILDING
- ASPHALT PAVEMENT COVER
- SOIL COVER
- ADJACENT NAVY PARCEL(S)
- ADJACENT NON–NAVY PROPERTY
- CATCH BASIN
- MANHOLE
- SETTLEMENT MONUMENT
- UTILITY POLE APPROX. LOCATION
- PARCEL BOUNDARY
- FENCE
- RAILROAD TRACK

N

0' 120'

SCALE: 1"=120'

NAVFAC	CLIENT: DEPARTMENT OF THE NAVY, BRAC PMO WEST SAN DIEGO, CALIFORNIA	OVERVIEW OF REMEDY COMPONENTS FOR PARCEL UC–1		
	LOCATION: HUNTERS POINT NAVAL SHIPYARD SAN FRANCISCO, CALIFORNIA	DRAWN BY: SC 03/14/14	CHECKED BY: JS 03/14/14	PROJECT NO. 20170042	FIG NO. 11

FILE NAME: C:\Civil 3D Projects\ERRG\Projects\20170042\figures_B-1\O&M 5 year\Fig-11.dwg LAYOUT NAME: 11 PLOTTED: Saturday, June 30, 2018 – 1:29pm

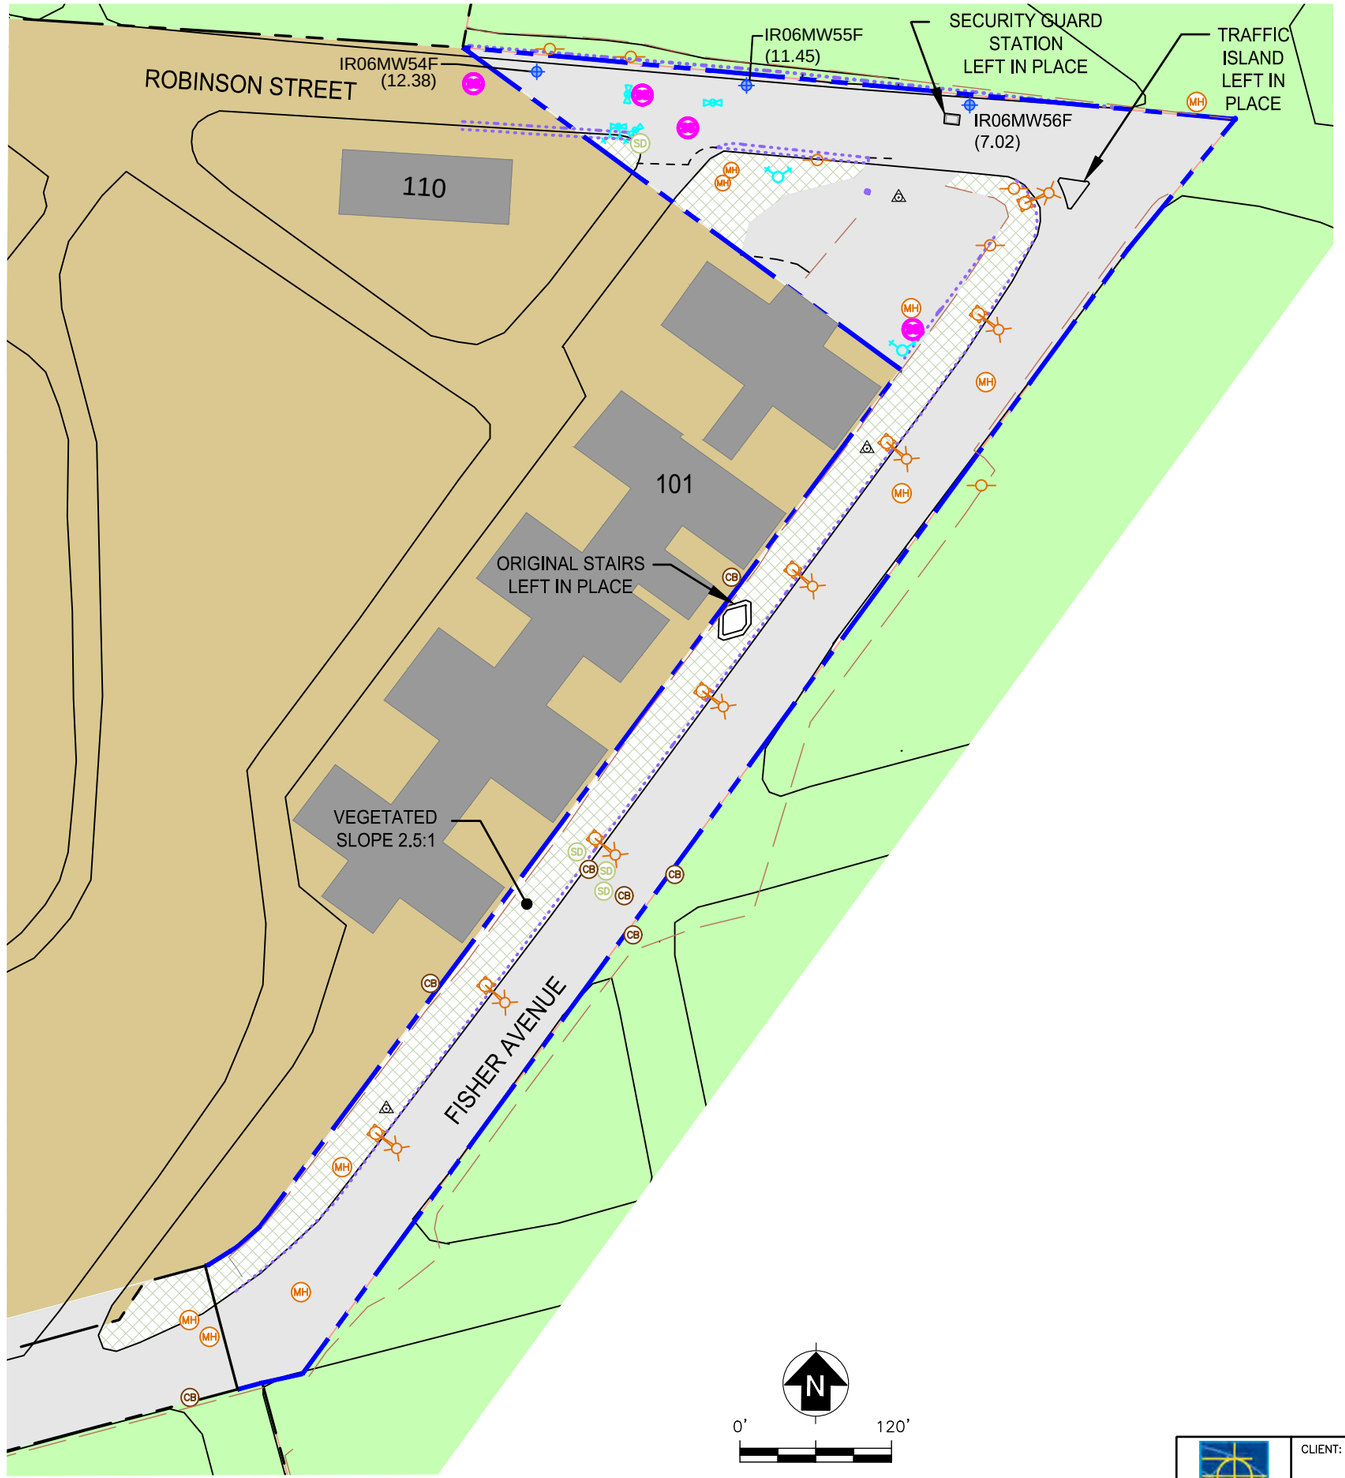

LEGEND:

IR06MW54F	MONITORING WELL AND WELL ID
(12.38)	WATER LEVEL ELEVATION (MSL)*
	EXISTING BUILDING
	ASPHALT PAVEMENT COVER
	SOIL COVER
	ADJACENT NAVY PARCEL
	ADJACENT NON–NAVY PROPERTY
	PARCEL BOUNDARY
CB	CATCH BASIN
MH	MANHOLE
	SANITARY SEWER
SD	STORM DRAIN
	SETTLEMENT MONUMENT
	FIRE HYDRANT
	WATER VALVE
	UTILITY FEATURE STREET LIGHT
	UTILITY POLE APPROX. LOCATION
	UTILITY FEATURE
	FENCE
	CONCRETE WALL

NAVFAC	CLIENT: DEPARTMENT OF THE NAVY, BRAC PMO WEST SAN DIEGO, CALIFORNIA	OVERVIEW OF REMEDY COMPONENTS FOR PARCEL UC–2		
	LOCATION: HUNTERS POINT NAVAL SHIPYARD SAN FRANCISCO, CALIFORNIA	DRAWN BY: SC 03/14/14	CHECKED BY: JS 03/14/14	PROJECT NO. 20170042	FIG NO. 12

FILE NAME: C:\Civil 3D Projects\ERRG\Projects\20170042\figures_B-1\O&M 5 year\Fig-12.dwg LAYOUT NAME: 12 PLOTTED: Saturday, June 30, 2018 - 1:30pm

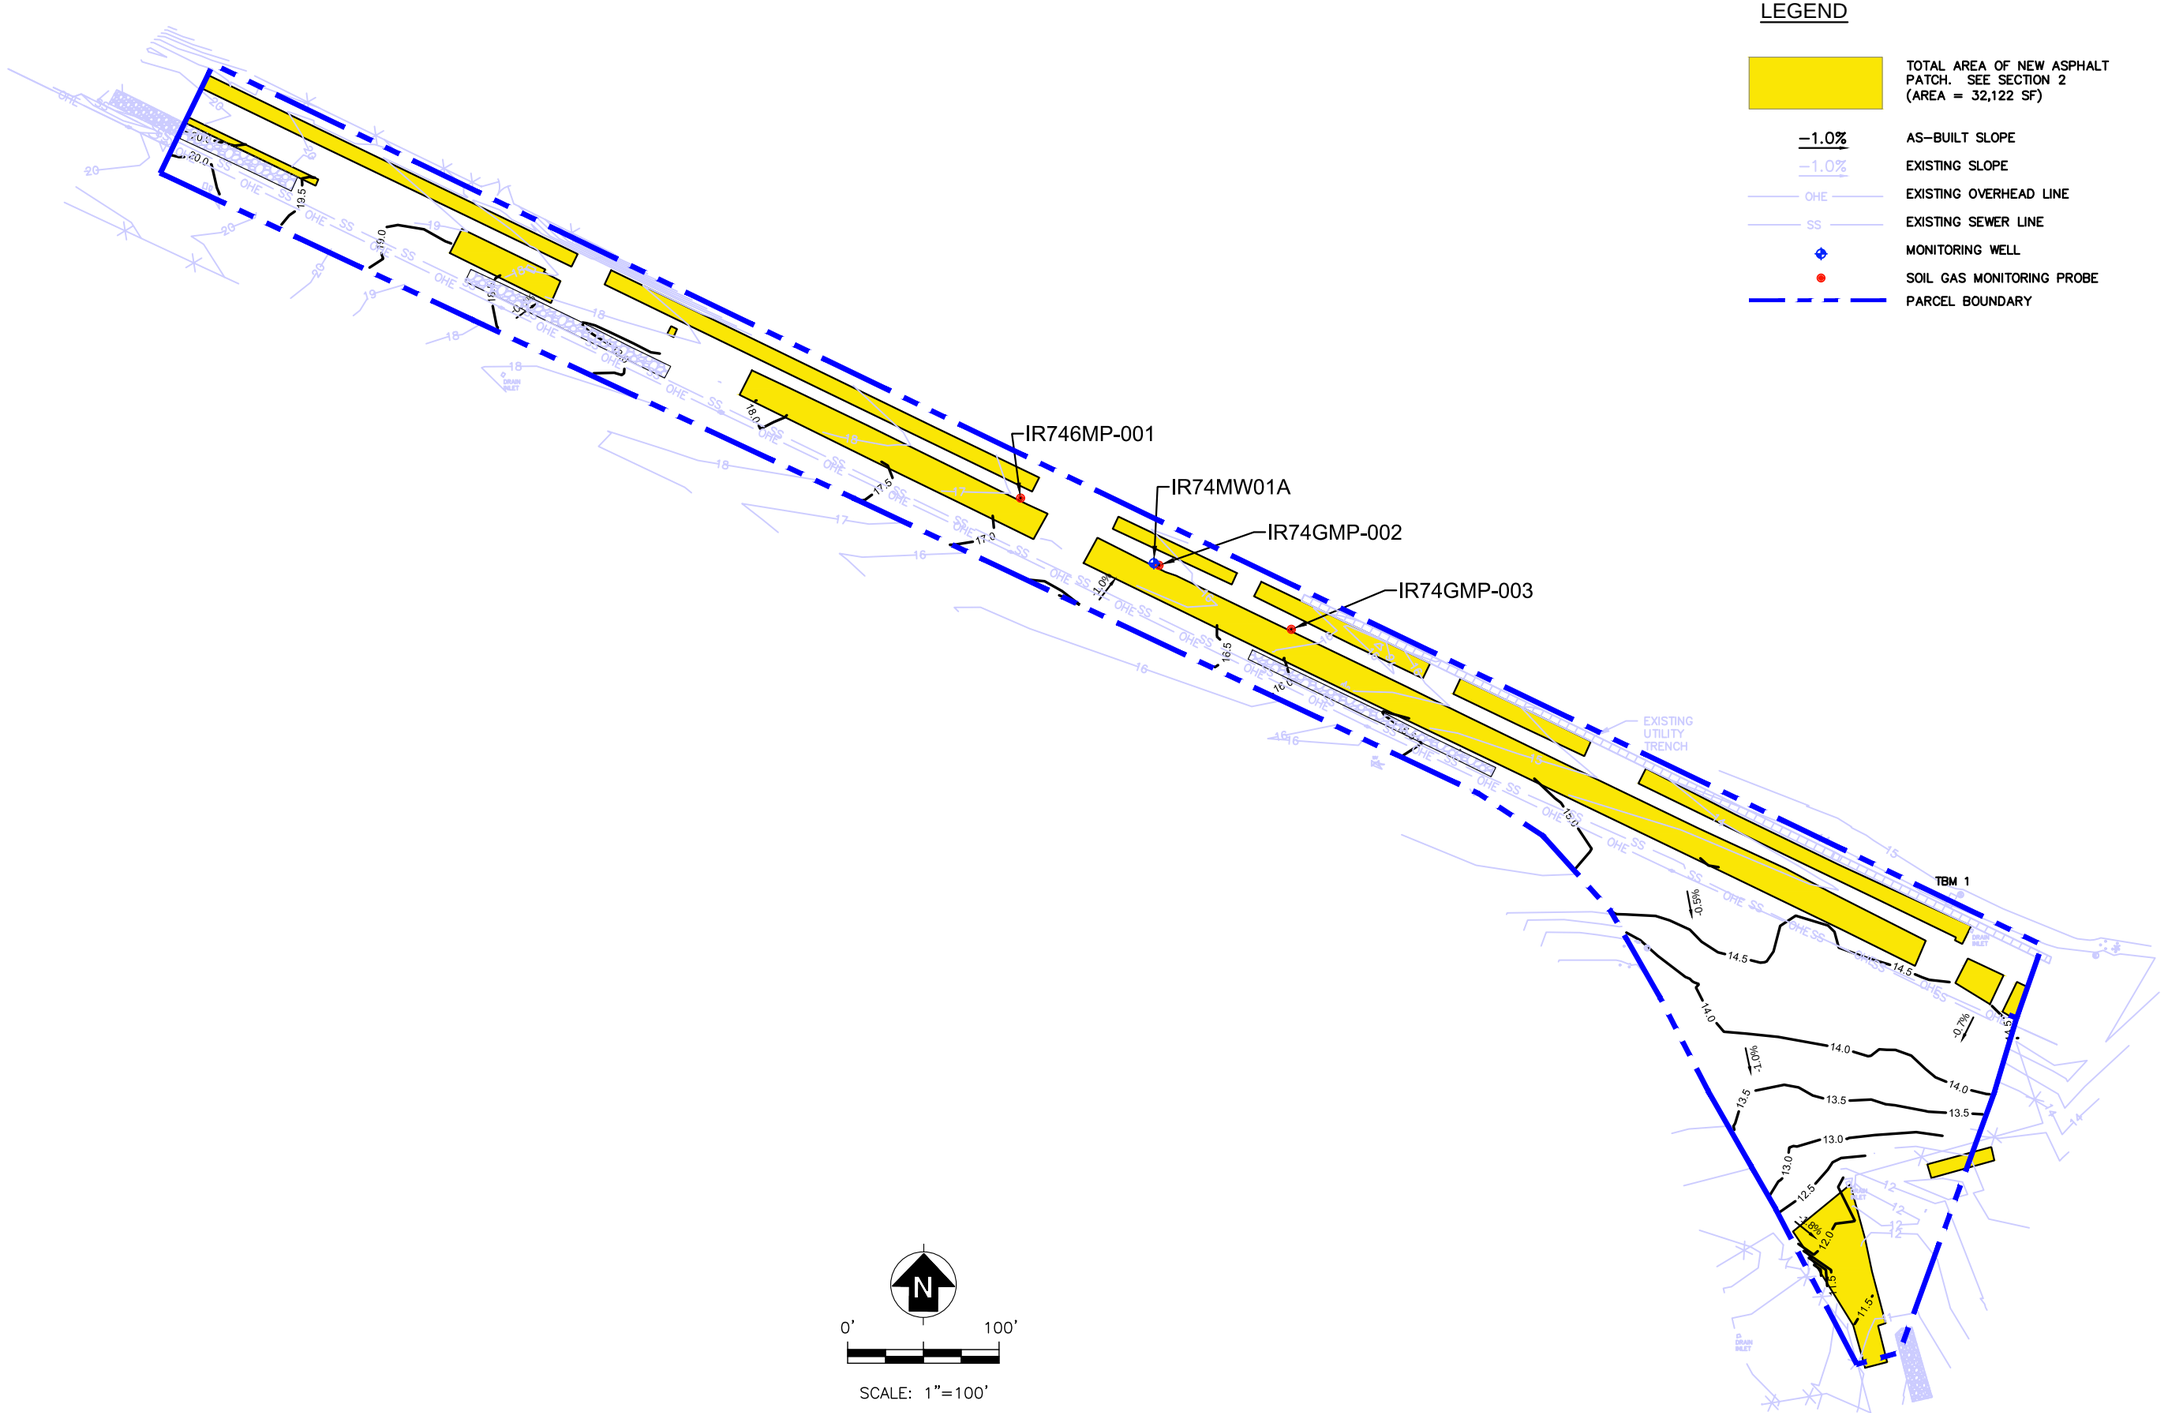

NAVFAC	CLIENT: DEPARTMENT OF THE NAVY, BRAC PMO WEST SAN DIEGO, CALIFORNIA	OVERVIEW OF REMEDY COMPONENTS FOR PARCEL UC-3		
	LOCATION: HUNTERS POINT NAVAL SHIPYARD SAN FRANCISCO, CALIFORNIA	DRAWN BY: SC 03/30/16	CHECKED BY: JS 03/30/16	PROJECT NO. 20170042	FIG NO. 13

FILE NAME: C:\Civil 3D Projects\ERRG\Projects\20170042\Figures_B-1\O&M 5 year\Fig-13.dwg LAYOUT NAME: 13 PLOTTED: Monday, July 02, 2018 - 11:43am

Tables

Table 1. Chemicals of Concern and Contaminated Media
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

	Parcel																																																
	B (including IR-07/18 and B-1 and B-2)							C						D-1					D-2	E						E-2						F		G					UC-1			UC-2				UC-3			
Chemical	Soil	Sediment	Soil Gas[1]	Groundwater, Vapor Intrusion	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil	Soil Gas[3]	Groundwater, Vapor Intrusion	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil	Soil Gas[1]	Groundwater, Vapor Intrusion	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil and Structures, Radionuclides	Soil	Sediment	Soil Gas[3]	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil, Human Health and Terrestrial Wildlife	Sediment	Soil Gas	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Sediment	Sediment, Radionuclides	Soil	Soil Gas[1]	Groundwater, Vapor Intrusion	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil	Soil Gas[2]	Soil and Structures, Radionuclides	Soil	Soil Gas[1]	Groundwater, Vapor Intrusion	Soil and Structures, Radionuclides	Soil	Soil Gas[2]	Groundwater	Soil and Structures, Radionuclides
1,1,2,2-Tetrachloroethane										X																																							
1,1,2-Trichloroethane										X																																							
1,1-Dichloroethane										X	X																		X																				
1,1-Dichloroethene																							X																										
1,2,3-Trichloropropane										X																			X																				
1,2,4-Trichlorobenzene				X							X									X																													
1,2,4-Trimethylbenzene				X						X	X									X																													
1,2-Dichlorobenzene				X						X	X																																						
1,2-Dichloroethane				X				X		X	X																		X																				
1,2-Dichloroethene (total)				X						X	X																																						
1,2-Dichloropropane				X						X	X																																						
1,3,5-Trimethylbenzene				X						X	X									X																													
1,3-Dichlorobenzene											X																																						
1,4-Dichlorobenzene				X	X			X		X	X												X						X																				
2,4-Dimethylphenol											X																																						
2,4-Dinitrotoluene											X																																						
2-Methylnaphthalene				X				X			X																																						
2-Methylphenol											X																																						
3,3'-Dichlorobenzidine								X												X																													
4-Methylphenol											X																																						
4-Nitrophenol																				X									X																				
4,4'-DDD																				X																													
4,4'-DDE																				X																													
4,4'-DDT																										X																							
Aldrin											X									X																													
alpha-BHC											X									X																													
Aluminum		X																																															
Americium-241																									X																								
Antimony	X				X			X			X									X						X	X																						
Aroclor-1016																										X			X																				
Aroclor-1242																										X			X																				
Aroclor-1248																				X						X																							
Aroclor-1254	X							X												X						X			X																				
Aroclor-1260	X							X												X						X			X																				
Arsenic	X				X			X			X			X						X			X			X			X					X								X							

Table 1. Chemicals of Concern and Contaminated Media *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

	Parcel																								
	B (including IR-07/18 and B-1 and B-2)							C						D-1					D-2	E					
Chemical	Soil	Sediment	Soil Gas[1]	Groundwater, Vapor Intrusion	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil	Soil Gas[3]	Groundwater, Vapor Intrusion	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil	Soil Gas[1]	Groundwater, Vapor Intrusion	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil and Structures, Radionuclides	Soil	Sediment	Soil Gas[3]	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides
Benzene			X	X	X			X		X	X				X	X				X					
Benzo(a)anthracene	X							X			X									X					
Benzo(a)pyrene	X							X			X			X						X					
Benzo(b)fluoranthene	X							X						X						X					
Benzo(k)fluoranthene	X							X												X					
beta-BHC	X																								
bis(2-Ethylhexyl)phthalate	X							X			X									X					
Bromodichloromethane			X	X						X	X														
Cadmium	X							X												X	X				
Carbazole											X									X					
Carbon Tetrachloride										X						X									
Cesium-137							X						X					X	X						X
Chlorobenzene				X						X	X														
Chloroethane				X	X					X	X														
Chloroform			X	X						X	X				X	X									
Chromium VI						X					X	X					X								
Chrysene								X			X									X					
cis-1,2-Dichloroethene				X						X	X												X		
cis-1,3-Dichloropropene										X															
Cobalt-60							X						X					X							X
Copper	X	X				X		X												X	X				
Dibromochloromethane										X															
Dichlorodifluoromethane				X																					
Dibenz(a,h)anthracene	X	X						X												X					
Dibenzofuran											X														
Dieldrin	X	X						X			X									X					
Dioxin																									
Dioxins/furans																				X					
Endrin																									
Ethylbenzene															X										
gamma-BHC (Lindane)								X												X					
Heptachlor																									
Heptachlor epoxide	X							X			X									X					
Heptachlor epoxide A																									
Heptachlor epoxide B																									

	Parcel																							
	E-2						F		G					UC-1			UC-2				UC-3			
Chemical	Soil, Human Health and Terrestrial Wildlife	Sediment	Soil Gas	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Sediment	Sediment, Radionuclides	Soil	Soil Gas[1]	Groundwater, Vapor Intrusion	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil	Soil Gas[2]	Soil and Structures, Radionuclides	Soil	Soil Gas[1]	Groundwater, Vapor Intrusion	Soil and Structures, Radionuclides	Soil	Soil Gas[2]	Groundwater	Soil and Structures, Radionuclides
Benzene				X						X	X				X			X				X		
Benzo(a)anthracene	X			X																	X			
Benzo(a)pyrene	X			X					X												X			
Benzo(b)fluoranthene	X			X					X												X			
Benzo(k)fluoranthene	X			X																	X			
beta-BHC				X																				
bis(2-Ethylhexyl)phthalate				X																				
Bromodichloromethane																								
Cadmium	X																							
Carbazole																								
Carbon Tetrachloride				X						X	X								X					
Cesium-137						X		X					X			X				X				X
Chlorobenzene																								
Chloroethane																								
Chloroform				X						X	X				X				X					
Chromium VI				X								X												
Chrysene				X																				
cis-1,2-Dichloroethene																								
cis-1,3-Dichloropropene																								
Cobalt-60						X		X					X			X								
Copper	X	X					X														X			
Dibromochloromethane																								
Dichlorodifluoromethane																								
Dibenz(a,h)anthracene	X			X																	X			
Dibenzofuran																								
Dieldrin	X	X		X																				
Dioxin	X																							
Dioxins/furans																								
Endrin		X																						
Ethylbenzene																								
gamma-BHC (Lindane)																								
Heptachlor				X																				
Heptachlor epoxide	X			X																				
Heptachlor epoxide A				X																				
Heptachlor epoxide B				X																				

	Parcel																																																
	B (including IR-07/18 and B-1 and B-2)							C						D-1					D-2	E						E-2						F		G					UC-1			UC-2				UC-3			
Chemical	Soil	Sediment	Soil Gas[1]	Groundwater, Vapor Intrusion	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil	Soil Gas[3]	Groundwater, Vapor Intrusion	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil	Soil Gas[1]	Groundwater, Vapor Intrusion	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil and Structures, Radionuclides	Soil	Sediment	Soil Gas[3]	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil, Human Health and Terrestrial Wildlife	Sediment	Soil Gas	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Sediment	Sediment, Radionuclides	Soil	Soil Gas[1]	Groundwater, Vapor Intrusion	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil	Soil Gas[2]	Soil and Structures, Radionuclides	Soil	Soil Gas[1]	Groundwater, Vapor Intrusion	Soil and Structures, Radionuclides	Soil	Soil Gas[2]	Groundwater	Soil and Structures, Radionuclides
Hexachlorobenzene								X																																									
Hexachloroethane											X																																						
Hydrogen-3																		X																				X			X								
Indeno(1,2,3-cd)pyrene	X							X												X						X			X																	X			
Iron	X							X			X									X						X			X																				
Isopropylbenzene										X																																							
Lead	X	X				X		X												X	X					X	X		X					X												X			
Manganese	X				X			X			X			X						X			X			X								X								X							
Mercury	X			X		X		X												X	X					X	X					X																	
Methylene Chloride				X						X	X				X														X							X													
Methoxychlor		X																																															
Molybdenum																					X																												
Naphthalene	X			X				X		X	X					X				X						X			X							X													
Nickel						X		X									X			X						X	X										X												
n-Nitroso-di-n-propylamine								X												X																													
n-Nitrosodiphenylamine																				X																													
Organic Lead								X																																									
Pentachlorophenol					X						X									X																													
Plutonium-239							X						X					X							X								X					X			X								
Potassium-40													X																																				
Radium-226							X						X					X	X						X						X		X					X			X				X				X
Selenium																																																	
Strontium-90							X						X					X	X						X						X		X					X			X				X				X
Tetrachloroethene	X		X	X				X		X	X					X							X						X						X	X													
Thallium					X			X			X									X			X						X																				
Thorium-232													X					X																				X			X								
Total Aroclors		X																			X					X	X					X																	
Total DDT		X																			X					X	X																						
Total HMW PAHs																										X																							
Total PCBs (non-dioxin)																										X																							
Total TPH																				X				X		X				X																			
trans-1,2-Dichloroethene				X						X	X												X																										
trans-1,3-Dichloropropene										X																																							
Trichloroethene	X		X	X	X			X		X	X					X				X			X						X						X	X				X				X				X	
Trichlorofluoromethane				X						X	X																																						
Uranium-235																		X							X								X					X			X								

Table 1. Chemicals of Concern and Contaminated Media *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

	Parcel																																																
	B (including IR-07/18 and B-1 and B-2)							C						D-1					D-2	E						E-2						F		G					UC-1			UC-2				UC-3			
Chemical	Soil	Sediment	Soil Gas[1]	Groundwater, Vapor Intrusion	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil	Soil Gas[3]	Groundwater, Vapor Intrusion	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil	Soil Gas[1]	Groundwater, Vapor Intrusion	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil and Structures, Radionuclides	Soil	Sediment	Soil Gas[3]	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil, Human Health and Terrestrial Wildlife	Sediment	Soil Gas	Groundwater, Domestic Use	Groundwater, Ecological	Soil and Structures, Radionuclides	Sediment	Sediment, Radionuclides	Soil	Soil Gas[1]	Groundwater, Vapor Intrusion	Groundwater, Ecological	Soil and Structures, Radionuclides	Soil	Soil Gas[2]	Soil and Structures, Radionuclides	Soil	Soil Gas[1]	Groundwater, Vapor Intrusion	Soil and Structures, Radionuclides	Soil	Soil Gas[2]	Groundwater	Soil and Structures, Radionuclides
Vanadium	X							X												X						X																							
Vinyl Chloride			X	X				X		X	X												X						X											X									
Xylene (total)																X				X																X													
Zinc	X	X						X				X								X	X					X																							

Notes:

1 = COCs in soil gas exceeding soil gas action levels in risk grids failing Tier 2 human health risk assessment (SES, 2013).

2 = COCs in soil gas exceeding soil gas action levels in risk grids failing Tier 1 human health risk assessment (SES, 2013).

3 = Soil gas investigation to identify COCs has not been completed to date.

BHC = benzene hexachloride

COCs = chemicals of concern

DDD = dichlorodiphenyldichloroethane

DDE = dichlorodiphenyldichloroethene

DDT = dichlorodiphenyltrichloroethane

HMW = high molecular weight

IR = Installation Restoration

PAHs = polycyclic aromatic hydrocarbons

PCBs = polychlorinated biphenyls

SES = Sealaska Environmental Services LLC

TPH = total petroleum hydrocarbons

Table 2. Pre-ROD Response Actions for Parcel B (i.e., IR-07/18 and Parcels B-1 and B-2)
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
1994	SI	Site assessments were completed at Parcels B, C, D, and E and included field investigations at 75 sites. Further investigation was recommended for 28 of the 75 sites assessed. The PA/SI determined that the majority of the potential source areas required additional investigation (PRC, LFR, and Uribe and Associates, 1996a).
6/1996	RI	The RI involved further investigation of sites identified at Parcel B during the initial assessment (IR-06, IR-07, IR-10), Triple A investigation (IR-18, SI-45), the PA (SI-31, IR-20, IR-23, IR-24, IR-25, IR-26, IR-42, IR-46, IR-50, IR-51), and the SI (IR-60, IR-61, IR-62) (PRC, LFR, and Uribe and Associates, 1996a).
1996	FS	Results and analysis in the RI Report were used to identify, screen, and evaluate remedial alternatives and to define areas for proposed remedial action (PRC, 1996b).
1996	Removal Actions at IR-23, IR-26, and IR-50 (sediment in Parcel B storm drains)	About 1,700 cubic yards of soil was removed from five areas (EE-01 through EE-05) (IT Corporation, 1999a). Most of the excavated areas were expanded or deepened during subsequent remedial actions.
10/7/97	Original ROD	The selected remedy documented in the original ROD included excavation and offsite disposal of contaminated soil, long-term monitoring of groundwater, and institutional controls.
8/98	ESD (First)	The first ESD to the 1997 ROD revised the selected remedy to require excavation of contaminated soil to a 10^{-6} cancer risk or to a maximum depth of 10 feet bgs, instead of to groundwater as required by the 1997 ROD.
7/98–9/99	Remedial Action (Phase 1)	The first phase of the remedial action was started (construction mobilization) on July 8, 1998. This action was the trigger for the first five-year review. About 54,400 cubic yards of soil was removed from 84 areas and disposed of off site (ChaduxTt, 2008). COCs included metals, VOCs, PAHs, and PCBs. Many of the excavated areas were expanded in the second remedial action phase in 2000 to 2001.
5/2000	ESD (Second)	The second ESD to the 1997 ROD updated the RGs for soil based on revised risk assessment methods and site-specific data. The second ESD resulted in an amendment to the RD.
5/2000–12/2001	Remedial Action (Phase 2)	During the second phase of the remedial action, about 47,200 cubic yards of soil was removed from 43 areas and disposed of off site (ChaduxTt, 2008). COCs for the second phase were primarily metals. The Navy met the cleanup requirements of the ROD (Navy, 1997) and subsequent ESDs (Navy, 1998 and 2000) at most of the excavation sites. However, the ubiquitous distribution of metals, especially arsenic and manganese, led to the reevaluation of the remedy for soil.

Table 2. Pre-ROD Response Actions for Parcel B (i.e., IR-07/18 and Parcels B-1 and B-2) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
2001	Quarterly Groundwater Monitoring	Quarterly groundwater monitoring results indicate chemical concentrations in groundwater and the extent of those chemicals in groundwater is greater than initially considered in the ROD.
6/2000–9/2002	SVE Treatability Study at IR-10	This study showed the initial effectiveness of SVE to treat soil vapor at IR-10 (IT Corporation 2002a; TtEMI, 2003e).
2003	Investigation of Chromium VI in IR-10 Groundwater	Investigated the extent of chromium VI around well IR10MW12A. This investigation supported characterization of chromium VI in groundwater.
2004	HRA	The HRA designated sites as impacted or non-impacted with respect to radiological contamination. Phase V investigations and surveys were completed at Buildings 103, 113, 130, and 146 and Dry Dock 6. Details of these activities are included in Sections 6 and 8 and Table 6-6 of the HRA (NAVSEA, 2004).
2003–2004	Waste Consolidation and Removal Activities	Basewide actions to address aboveground issues identified previously at and near buildings, including removal of waste material; decontamination or removal of equipment and structures; and abatement of friable, accessible, and damaged asbestos-containing materials. The primary objective of this action was to address potential environmental issues associated with the industrial use of buildings that could affect the planned transfer of the property to the City and County of San Francisco (Tetra Tech FW, Inc., 2004b).
5/2003–6/2003	Characterization and Sampling of Shoreline at IR-07 and IR-26	Samples collected during this investigation provided the basis for the evaluation of potential risk to aquatic receptors, which contributed to the subsequent selection of shoreline revetment as part of the amended remedy (TtEMI and ITSI, 2004a).
9/2003–3/2004	Groundwater Treatability Study at IR-10	Groundwater treatability study at IR-10 using injection of ZVI (ERRG and URS, 2004). This study showed the effectiveness of ZVI in treating VOCs in groundwater at IR-10 and resulted in large concentration reductions.
2005	Soil Gas Survey at IR-07/18	Soil gas survey for evaluation of methane and total VOCs to assess nature and extent of concentrations in soil gas at IR-07/18. The soil gas survey established the presence of methane at IR-07.
2006	Phase III SVE Treatability Study at IR-10	Expanded the treatability study at IR-10 to evaluate SVE for removal of TCE and other VOCs from soil beneath Building 123. The treatability study was the basis for use of SVE in revised remedial alternatives.

Table 2. Pre-ROD Response Actions for Parcel B (i.e., IR-07/18 and Parcels B-1 and B-2) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
12/2007	TMSRA	The TMSRA evaluated site-specific information about Parcel B that became available after signature of the 1997 ROD. The updated information was obtained from (1) the original remedial action (Phases 1 and 2) for soil conducted between 1998 and 2001, (2) groundwater monitoring conducted since 1999, and (3) the HRA and subsequent radiological removal actions.
5/2006–9/2010	Radiological Removal Actions	Radiological removal actions were completed at Parcel B, during which 24,826 linear feet of trench and 69,984 cubic yards of soil were excavated; approximately 3,217 cubic yards of soil was disposed of off site as low-level radioactive waste (TtEC, 2012a and 2012c).
8/2008–10/2008	TCRA for Methane at IR-07	Excavation and offsite disposal of about 17,000 cubic yards of soil from IR-07 to remove a methane source area. The TCRA found that debris was confined to a layer extending from about 2 to 8 feet bgs that was above the water table, which was at about 18 feet bgs at the excavation site. Material below 8 feet bgs was predominantly clean engineered fill without debris or staining. A layer of material at the top of the Bay Mud at about 23 to 25 feet bgs was observed to be highly organic and odiferous. Excavation continued into the native Bay Mud to a depth of about 27 feet bgs to remove the organic layer. The Navy concluded the organic layer was the likely source of methane and debris used as fill located above the water table was not a likely source of methane (SES-TECH, 2009).
9/2008–10/2008	TCRA for Mercury at IR-26	Excavation and offsite disposal of about 6,000 cubic yards of soil from IR-26 to remove a mercury source area. In total, 98 soil and 19 groundwater samples were collected from 21 borings advanced to the underlying bedrock to delineate mercury source areas. Three excavations to bedrock, ranging from 13 to 18 feet bgs, were completed. Excavations were backfilled with controlled density fill to the water table elevation and then with drain rock and clean soil to surface grade (Insight, 2009).
1/26/2009	Amended ROD	The Amended ROD documents the changes to the selected remedy based on the evaluations in the TMSRA. The significant changes to the selected remedy include (1) modification of the soil remedy to include durable covers to address soil contamination, (2) addition of active treatment methods to the groundwater remedy, (3) consideration of potential ecological risks to aquatic receptors, and (4) inclusion of methods and RGs to address radiological contamination.

Table 2. Pre-ROD Response Actions for Parcel B (i.e., IR-07/18 and Parcels B-1 and B-2) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Notes:

1 = The documents listed are available in the Navy's Administrative Record and provide detailed information used to support remedy selection at Parcel B (including IR-07/18 and Parcels B-1 and B-2). Note that at the time of remedy selection, Parcel B had not been subdivided into Parcels B-1 and B-2; separate remedies were selected for IR-07 and IR-18 (excluding the remainder of the former Parcel B) and for the remainder of the former Parcel B (i.e., Parcels B-1 and B-2).

ASTs = aboveground storage tanks
bgs = below ground surface
COCs = chemicals of concern
EE = exploratory excavation
ERRG = Engineering/Remediation Resources Group, Inc.
ESD = Explanation of Significant Differences
FS = Feasibility Study
HRA = Historical Radiological Assessment
Insight = Insight Environmental, Engineering, and Construction, Inc.
IR = Installation Restoration
ITSI = Innovative Technical Solutions, Inc.
ISB = in-situ bioremediation
LFR = Levine Fricke Recon
NAVSEA = Naval Sea Systems Command
Navy = Department of the Navy
PA/SI = Preliminary Assessment/Site Inspection
PAHs = polycyclic aromatic hydrocarbons
PCBs = polychlorinated biphenyls
PRC = PRC Environmental Management, Inc.
RGs = remediation goals
RI = Remedial Investigation
ROD = Record of Decision
SES-TECH = SES-TECH Remediation Services, Inc.
SVE = soil vapor extraction
TCE = trichloroethene
TCRA = time-critical removal action
TMSRA = Technical Memorandum in Support of a ROD Amendment
TtEC = Tetra Tech EC, Inc.
TtEMI = Tetra Tech EM Inc.
URS = URS Corporation
USTs = underground storage tanks
VOCs = volatile organic compounds
ZVI = zero-valent iron

Table 3. RAOs and Remedy Components for Parcel B (i.e., IR-07/18 and Parcels B-1 and B-2)
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Soil, Sediment, and Soil Gas		
Prevent exposure to organic and inorganic chemicals in soil at concentrations above remediation goals developed in the human health risk assessment for the following exposure pathways: ▪ Ingestion of, outdoor inhalation of, and dermal exposure to soil ▪ Ingestion of homegrown produce by residents in research and development and mixed-use reuse areas	▪ Excavation and offsite disposal of soil in select areas where COCs exceed remediation goals	▪ Durable covers ▪ Monitoring, maintenance, and ICs
Prevent exposure to VOCs in soil gas at concentrations that would pose unacceptable risk (i.e., risk greater than 10^{-6}) via indoor inhalation of vapors.	▪ Removal and treatment of vapors in soil gas using SVE at IR-10	▪ Soil gas surveys ▪ Monitoring, maintenance, and ICs
Reduce presence of methane in soil gas such that concentrations do not accumulate and become explosive in structures.[1]	▪ Excavation of soil in IR-07 to remove a methane source	▪ Methane monitoring and ICs
Prevent or minimize exposure of ecological receptors to organic and inorganic chemicals in soil and sediment in shoreline areas at concentrations above remediation goals established for sediment.	▪ Excavation of sediment and debris to permit revetment construction	▪ Durable covers ▪ Monitoring and maintenance
Groundwater		
Prevent exposure to VOCs and mercury in A-aquifer groundwater at concentrations above remediation goals via indoor inhalation of vapors from groundwater. *This RAO for exposure to vapors from groundwater via vapor intrusion has been superseded by action levels established for soil vapor (ChaduxTt, 2011g; SES, 2013).*	▪ In-situ groundwater treatment using biological substrate injections to address VOCs at IR-10	▪ Soil gas surveys ▪ Monitoring (MNA) and ICs

Table 3. RAOs and Remedy Components for Parcel B (i.e., IR-07/18 and Parcels B-1 and B-2) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Groundwater *(continued)*		
Prevent direct exposure to B-aquifer groundwater at concentrations above remediation goals through the domestic use pathway (for example, drinking water or showering).	▪ None	▪ Monitoring (MNA) and ICs
Prevent or minimize exposure of construction workers to metals, VOCs, and SVOCs in A-aquifer groundwater at concentrations above remediation goals from dermal exposure and inhalation of vapors from groundwater.	▪ In-situ groundwater treatment using biological substrate injections to address VOCs at IR-10	▪ Soil gas surveys ▪ Monitoring (MNA) and ICs
Prevent or minimize migration to surface water of San Francisco Bay of chromium VI, copper, lead, and mercury in A-aquifer groundwater that would result in concentrations of chromium VI above 50 µg/L, copper above 28.04 µg/L, lead above 14.44 µg/L, and mercury above 0.6 µg/L in the surface waters of San Francisco Bay. This RAO is intended to protect the beneficial uses of the bay, including ecological receptors.	▪ None	▪ Monitoring (MNA)
Radiologically Impacted Soil and Structures		
Prevent exposure to radionuclides of concern at concentrations that exceed remediation goals for the ingestion or inhalation exposure pathways.	▪ Radiological surface scan and removal of anomalies at IR-07/18 ▪ Radiological surveys and remediation	▪ Durable covers[2] ▪ Monitoring, maintenance, and ICs[2]

Notes:

1 = This RAO applies to IR-07/18 only; it does not apply to Parcels B-1 and B-2 because methane is not present in soil gas within these parcels.

2 = These components of the radiological remedy apply to portions of IR-07/18 only (i.e., within the area requiring ICs for radionuclides). Durable covers and ICs to address radiological contaminants are not required for the remaining areas of IR-07/18 and Parcels B-1 and B-2, where radiological surveys and remediation adequately address radiological contamination.

COCs = chemicals of concern
ICs = institutional controls
IR = Installation Restoration
MNA = monitored natural attenuation
RAOs = remedial action objectives
SES = Sealaska Environmental Services LLC
SVE = soil vapor extraction
SVOCs = semivolatile organic compounds
VOCs = volatile organic compounds
µg/L = micrograms per liter

Table 4. Pre-ROD Response Actions for Parcel C (i.e., Parcels C and UC-2)
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
1994	SI	Site assessments were completed at Parcels B, C, D, and E and included field investigations at 75 sites. Further investigation was recommended for 28 of the 75 sites assessed. The PA/SI determined that the majority of the potential source areas required additional investigation (PRC, LFR, and Uribe and Associates, 1996a).
3/1997	RI	The RI included collection of 1,173 soil samples, 570 groundwater samples, and 129 source samples. Based on the RI results, 12 sites in former Parcel C (plus IR-06 and IR-25) were recommended for further evaluation in an FS.
1996–1997	Exploratory Excavation Removal Action	About 800 cubic yards of coil removed from six exploratory excavation areas (EE-06 through EE-11) (IT Corporation, 1999a).
1996–1997	Storm Drain Sediment Removal	As part of a base-wide removal action, sediment was removed from storm drain lines at Parcels C and UC-2. Sediment in drainage culverts at Dry Dock 4 was partially removed.
1996–1998	FS (initial phase)	Results and analysis in the RI Report were used to identify, screen, and evaluate remedial alternatives and to define areas for proposed remedial action.
7/98–9/99	Soil Removals at IR-06 and IR-25	Contaminated soil was removed from IR-06 and IR-25 during the initial remedial action at former Parcel B before these areas were moved to Parcel C (IT Corporation, 2000). Removed soil was disposed of off site, and the excavations were backfilled with clean material.
1999	RMR	The RMR process used various criteria and decision rules to reevaluate whether remedial actions were required at all of the 14 IR sites in former Parcel C that had been originally identified as requiring remedial actions for soil. Of the 14 IR sites in former Parcel C, six were recommended for action after the RMR process. Based on the RMR results, the sites and chemicals requiring further evaluation and remedial action were revised.
4/2001	Groundwater Treatability Study at Building 253	Treatability study for groundwater at Building 253 using chemical oxidation by potassium permanganate injection (TtEMI, 2004b).
2000–2002	Fuel and Steam Line TCRA	All subsurface fuel lines and contaminated steam lines were removed during a TCRA. About 8,800 cubic yards of soil was also removed and disposed of off site (TtEMI, 2002).
2001–2002	SVE Treatability Studies	Treatability studies were completed for SVE at Buildings 134, 211/253, 231, 251, and 272 (IT Corporation, 2001, 2002b, 2002c, 2002d, and 2002e).
9/2002	Groundwater Treatability Study at Building 272	Treatability study for groundwater using ZVI injection completed at Building 272 (TtEMI, 2003c).

Table 4. Pre-ROD Response Actions for Parcel C (i.e., Parcels C and UC-2) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
2002–2004	Waste Consolidation and Removal Activities	Industrial process equipment was decontaminated, sumps were cleaned, and waste was consolidated for offsite disposal, including waste materials stored in or near buildings and removal or encapsulation of asbestos-containing materials (Tetra Tech FW, Inc., 2004b).
2003	Encapsulation of Drainage Culvert Sediment at Dry Dock 4	Contaminated sediment in two culverts under Dry Dock 4 was encapsulated (TtEMI, 2003a).
2004	Degreaser Pit/Separator Demolition at RU-C5	A degreaser pit and oil-water separator were removed at Building 134.
2004	HRA	The HRA evaluated and designated sites as radiologically impacted or non-impacted. Based on the HRA results, nine sites along with the sanitary sewer and storm drain lines, at Parcel C were determined to have the potential for radiological contamination and require further investigation (NAVSEA, 2004).
4/2004–5/2005	Groundwater Treatability Study at Building 134	Treatability study for groundwater was conducted at Building 134 using in-situ sequential anaerobic-aerobic bioremediation (Shaw, 2005).
8/2004–1/2005	Follow-on Groundwater Treatability Study at Building 272	Follow-on treatability study for groundwater at Building 272 using ZVI injection (ITSI, 2005).
7/2008	Revised FS	Existing RI data were combined with new data obtained after completion of the 1996 (Parcel B, IR-06, and IR-25) and 1997 (former Parcel C) RI Reports. The revised FS considered new information associated with several response actions completed within former Parcel C and at other adjacent parcels. New information included (1) quarterly monitoring of groundwater, (2) updates to toxicity criteria used in the 1997 HHRA, and (3) the findings from removal actions conducted to address chemicals identified during the RMR process and radiological contaminants that were identified in the HRA.
6/2009–6/2010	Groundwater Treatability Study at Building 253	Treatability study for groundwater at Building 253 using anaerobic bioremediation through injection of sodium lactate and emulsified vegetable oil (OTIE, 2011).
5/2010–4/2011	Groundwater Treatability Study at Building 134	Treatability study for groundwater using ZVI injection at Building 134 (CDM Smith, 2012).
9/2010	ROD	The selected remedy documented in the ROD included excavation and offsite disposal of contaminated soil, radiological remediation of soil and structures, soil gas treatment using SVE, durable covers, groundwater treatment with ZVI or ISB, MNA, and institutional controls.

Table 4. Pre-ROD Response Actions for Parcel C (i.e., Parcels C and UC-2) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Notes:

1 = The documents listed are available in the Administrative Record and provide detailed information used to support remedy selection at Parcels C and UC-2.

AST = aboveground storage tank
Battelle = Battelle Memorial Institute
EE = exploratory excavation
FS = Feasibility Study
HHRA = human health risk assessment
HRA = Historical Radiological Assessment
IR = Installation Restoration
ISTI = Innovative Technical Solutions, Inc.
ISB = in-situ bioremediation
LFR = Levine Frick Recon
MNA = monitored natural attenuation
NAVSEA = Naval Sea Systems Command
Navy = Department of the Navy
OTIE = Oneida Total Integrated Enterprises, Inc.
PRC = PRC Environmental Management, Inc.
RI = Remedial Investigation
RMR = risk management review
RU = Remedial Unit
Shaw = Shaw Environmental, Inc.
SVE = soil vapor extraction
TCRA = time-critical removal action
TtEMI = Tetra Tech EM Inc.
UST = underground storage tank
ZVI = zero-valent iron

Table 5. RAOs and Remedy Components for Parcel C
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Soil and Soil Gas		
Prevent or minimize exposure to organic and inorganic chemicals in soil at concentrations above remediation goals developed in the human health risk assessment for the following exposure pathways: ▪ Ingestion of, outdoor inhalation of, and dermal exposure to surface and subsurface soil ▪ Ingestion of homegrown produce in native soil	▪ Excavation and offsite disposal of soil in select areas where COCs exceed remediation goals	▪ Durable covers ▪ Monitoring, maintenance, and ICs
Prevent or minimize exposure to VOCs in soil gas at concentrations that would pose unacceptable risk via indoor inhalation of vapors. Table 7 of the final soil gas memorandum lists the volatile chemicals (ChaduxTt, 2010b). This list includes SVOCs (such as pesticides and PAHs). Remediation goals for VOCs to address exposure via indoor inhalation of vapors may be superseded based on COC identification information from future soil gas surveys. Future action levels would be established for soil gas, would account for vapors from both soil and groundwater, and would be calculated based on a cumulative risk level of 10^{-6} using the accepted methodology for risk assessments at HPNS.	▪ In-situ soil treatment using SVE at eight areas	▪ Soil gas surveys ▪ Monitoring, maintenance, and ICs
Groundwater		
Prevent or minimize exposure to VOCs in A-aquifer groundwater at concentrations above remediation goals via indoor inhalation of vapors from groundwater. *This RAO for exposure to vapors from groundwater via vapor intrusion has been superseded by action levels established for soil vapor (ChaduxTt, 2011g; SES, 2013).*	▪ In-situ groundwater treatment using ZVI or biological substrate injections at RU-C1, RU-C2, RU-C4, and RU-C5	▪ Soil gas surveys ▪ Monitoring (MNA) and ICs

Table 5. RAOs and Remedy Components for Parcel C *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Groundwater *(continued)*		
Prevent or minimize direct exposure to groundwater that may contain COCs through the domestic use pathway in the B-aquifer, RU-C5 only (for example, drinking water or showering).	▪ In-situ groundwater treatment using ZVI or biological substrate injections at RU-C5	▪ Soil gas surveys ▪ Monitoring (MNA) and ICs
Prevent or minimize exposure of construction workers to metals and VOCs in A-aquifer groundwater at concentrations above remediation goals from dermal exposure and inhalation of vapors from groundwater.	▪ In-situ groundwater treatment using ZVI or biological substrate injections at RU-C1, RU-C2, RU-C4, and RU-C5	▪ Soil gas surveys ▪ Monitoring (MNA) and ICs
Prevent or minimize migration to surface water of San Francisco Bay of chromium VI and zinc in A-aquifer groundwater that would result in concentrations of chromium VI above 50 µg/L and nickel above 81 µg/L at the point of discharge to the bay.	▪ In-situ groundwater treatment using ZVI or biological substrate injections at RU-C1, RU-C2, RU-C4, and RU-C5	▪ Monitoring (MNA) and ICs
Radiologically Impacted Soil and Structures		
Prevent or minimize exposure to ROCs in concentrations that exceed remediation goals for all potentially complete exposure pathways (e.g., external radiation, soil ingestion, and inhalation of resuspended radionuclides in soil or dust).	▪ Radiological surveys and remediation	▪ None

Notes:
COCs = chemicals of concern
HPNS = Hunters Point Naval Shipyard
ICs = institutional controls
MNA = monitored natural attenuation
PAHs = polycyclic aromatic hydrocarbons
RAOs = remedial action objectives
ROCs = radionuclides of concern
RU = remedial unit
SES = Sealaska Environmental Services LLC
SVE = soil vapor extraction
SVOCs = semivolatile organic compounds
VOCs = volatile organic compounds
ZVI = zero-valent iron
µg/L = micrograms per liter

Table 6. RAOs and Remedy Components for Parcel UC-2
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Soil and Soil Gas		
Prevent or minimize exposure to inorganic chemicals in soil at concentrations above remediation goals developed in the human health risk assessment for the following exposure pathways: ▪ Ingestion of, outdoor inhalation of, and dermal exposure to surface and subsurface soil ▪ Ingestion of homegrown produce by residents in mixed-use and research and development blocks	▪ None	▪ Durable covers ▪ Monitoring, maintenance, and ICs
Prevent or minimize exposure to VOCs in soil gas at concentrations that would pose unacceptable risk via indoor inhalation of vapors. Remediation goals for VOCs to address exposure via indoor inhalation of vapors have been superseded based on COC identification information from soil gas surveys. Action levels have been established for soil gas that account for vapors from both soil and groundwater and were calculated based on a cumulative risk level of 10^{-6} using the accepted methodology for risk assessments at HPNS (ChaduxTt, 2011g; SES, 2013).	▪ None	▪ Soil gas surveys ▪ Monitoring and ICs
Groundwater		
Prevent or minimize exposure to VOCs in A-aquifer groundwater at concentrations above remediation goals via indoor inhalation of vapors from groundwater. *This RAO for exposure to vapors from groundwater via vapor intrusion has been superseded by action levels established for soil vapor (ChaduxTt, 2011g; SES, 2013).*	▪ MNA at IR-06	▪ Soil gas surveys ▪ Monitoring and ICs
Prevent or minimize direct exposure to groundwater that may contain COCs through the domestic use pathway (e.g., drinking water or showering).	▪ MNA at IR-06	▪ Monitoring and ICs

Table 6. RAOs and Remedy Components for Parcel UC-2 *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Groundwater *(continued)*		
Prevent or minimize exposure of construction workers to VOCs in A-aquifer groundwater at concentrations above remediation goals from dermal exposure and inhalation of vapors from groundwater.	▪ MNA at IR-06	▪ Soil gas surveys ▪ Monitoring and ICs
Radiologically Impacted Soil and Structures		
Prevent exposure to ROCs in concentrations that exceed remediation goals for all potentially complete exposure pathways (e.g., external radiation, soil ingestion, and inhalation of resuspended radionuclides in soil or dust).	▪ Radiological Surveys and Remediation	▪ None

Notes:
COCs = chemicals of concern
ICs = institutional controls
IR = Installation Restoration
MNA = monitored natural attenuation
RAOs = remedial action objectives
ROCs = radionuclides of concern
SES = Sealaska Environmental Services LLC
VOCs = volatile organic compounds

Table 7. Pre-ROD Response Actions for Parcel D (i.e., Parcels D-1, D-2, G, and UC-1)
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
1994	SI	Site assessments were completed at Parcels B, C, D, and E and included field investigations at 75 sites. Further investigation was recommended for 28 of the 75 sites assessed. The PA/SI determined that the majority of the potential source areas required additional investigation (PRC, LFR, and Uribe and Associates, 1996a).
1988–1997	RI	Site conditions were assessed through literature searches; interviews with former onsite employees; geophysical, radiological, and aerial map surveys; installation of soil borings and monitoring wells, and aquifer testing. The following environmental samples were collected: 418 surface soil, 1,938 subsurface soil, 429 A-aquifer groundwater samples, 9 B-aquifer groundwater samples, 7 bedrock water-bearing zone groundwater samples, 185 HydroPunch groundwater samples, 77 water and sediment samples (from utility lines, sumps, and floor drains), 8 sandblast samples, 1 asbestos sample, 29 test pit samples, 2 floor scrape samples, and 2 UST samples. Based on the RI results, all of Parcel D (except for IR-48 and IR-66) was recommended for further evaluation in an FS.
1989	PCB-Contaminated Soil Removal at IR-08	About 1,255 cubic yards of soil contaminated by PCBs removed at IR-08 (ERM-West, 1989).
1991–1993	UST and AST removals	Nine USTs were removed and one was closed in place; three ASTs were removed.
1991–1995	Removal of Sandblast Waste	Sandblast waste was collected and removed basewide (Battelle, 1996).
1994–1996	Contaminated Equipment and Residue Removed from IR-09	Contaminated equipment and residue was removed from IR-09 (pickling and plating yard). Approximately 200,000 pounds of hazardous waste liquids, 1,500 cubic yards of hazardous waste solids, 100,000 of nonhazardous waste liquids, and 350,000 pounds of scrap metal were removed and disposed of off site (SulTech, 2007b).
1996	Removal of Cesium-Impacted Soil	Approximately 1 cubic yard of soil affected by a cesium-137 spill was removed from an area behind Building 364.
1996–1997	Exploratory Excavation Removal Action	Stained soil, asphalt, and concrete were removed from two IR sites (IR-53 and IR-70) within Parcel D-1 and three IR sites (IR-33, IR-37, and IR-70) within Parcel G.
1996–1997	Removal of Storm Drain Sediment	In total, 1,200 tons of contaminated sediment was removed from storm drain lines and appurtenances in Parcel D.
1996–1997	FS	Results and analyses in the RI Report were used to identify, screen, and evaluate remedial alternatives and to define areas for proposed remedial action.

Table 7. Pre-ROD Response Actions for Parcel D (i.e., Parcels D-1, D-2, G, and UC-1) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
1999	RMR	The RMR process used various criteria and decision rules to reevaluate whether remedial actions were required at 19 of the 27 IR sites in Parcel D that had been originally identified as requiring remedial actions for soil. Based on the RMR results, the sites and chemicals requiring further evaluation and remedial action were revised.
2001	TCRA for Non-VOCs in Soil	About 63 cubic yards of soil was removed from IR-08, IR-09, IR-37, IR-53, IR-55, and IR-65. Steam lines saturated with oil were removed; other steam lines were pressure-tested, cleaned, and left in place. About 150 feet of fuel line was also removed (TtEMI and IT Corporation, 2001).
2001–2002	Radiological TCRA	Approximately 15 cubic yards of soil affected by a cesium-137 spill was removed from IR-33 South.
2002	Groundwater Data Gaps Investigation	A data gaps investigation was completed to provide additional understanding of the groundwater conditions underlying the parcel. Groundwater samples were collected and analyzed for various chemicals (including metals and VOCs), and results were used to further define the nature and extent of contamination in groundwater.
4/2002–6/2003	Waste Consolidation and Removal Activities	Decontamination and waste consolidation activities were conducted, including encapsulating or removing asbestos-containing material; removing and disposing of structural materials, paint booths, and numerous abandoned waste items; removing and disposing of hoods, vents, and ducts associated with industrial processes; removing or disabling existing ASTs; and cleaning industrial process-related sumps, vaults, trenches, and equipment foundations (Foster Wheeler Environmental Corporation, 2003).
2003–2004	Soil Stockpile Removal Action	Navy inventoried all the stockpiles at HPNS. Nine soil and waste asphalt stockpiles were removed (TtEMI and ITSI, 2005).
2004	HRA	The HRA evaluated and designated sites as radiologically impacted or non-impacted. Based on the HRA results, one building, four building sites, the gun mole pier, and the sanitary sewer and storm drain lines were identified as radiologically impacted at Parcel D-1; one building and the sanitary sewer and storm drain lines were identified as impacted at Parcel UC-1; and six buildings, one building site, and the sewer and storm drains were identified as radiologically impacted at Parcel G (NAVSEA, 2004).
2006–2011	Storm Drain and Sanitary Sewer Removal Actions	Radiological removal actions, including radiological investigation and removal of storm drains and sanitary sewers, were completed throughout Parcels D-1, D-2, G, and UC-1.

Table 7. Pre-ROD Response Actions for Parcel D (i.e., Parcels D-1, D-2, G, and UC-1) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
2007	Revised FS	Existing RI data were combined with new data collected after completion of the 1996 RI Report. The revised FS considered new information associated with several response actions completed within Parcel D and at other adjacent parcels at HPNS. New information included (1) the widespread presence of metals in soil across Parcel D, (2) quarterly monitoring of groundwater since 2004, (3) updates to toxicity criteria used in the 1997 HHRA, and (4) the findings from removal actions conducted to address chemicals identified by a RMR process and radiological contaminants that were identified by the HRA.
10/2008–4/2009	Treatability Study for Groundwater at Parcels D-1 and G	Treatability study for groundwater at Parcels D-1 and G using ZVI injections (Alliance, 2010). This study showed the effectiveness of ZVI in treating VOCs in groundwater at Parcels D-1 and G and resulted in large reductions in VOC concentrations. All VOC concentrations in groundwater at Parcel D-1 remain below remediation goals established in the ROD.
2/2009	ROD for Parcel G	The selected remedy documented in the ROD included excavation and offsite disposal of contaminated soil, radiological remediation of soil and structures, durable covers, groundwater treatment with ZVI or ISB, groundwater monitoring, and institutional controls.
7/2009	ROD for Parcels D-1 and UC-1	The selected remedy documented in the ROD included excavation and offsite disposal of contaminated soil, radiological remediation of soil and structures, durable covers, groundwater treatment with ZVI or ISB, groundwater monitoring, and institutional controls.
8/2010	NFA ROD for Parcel D-2	The ROD documented that no further action was necessary to ensure protection of human health or the environment.

Notes:

1 = The documents listed are available in the Administrative Record and provide detailed information used to support remedy selection at Parcels D-1, G, and UC-1, as well as the No Further Action determination at Parcel D-2.

Alliance = The Alliance Compliance Group Joint Venture
ASTs = aboveground storage tanks
Battelle = Battelle Memorial Institute
ERM-West = Environmental Resources Management-West, Inc.
FS = Feasibility Study
HHRA = human health risk assessment
HPNS = Hunters Point Naval Shipyard
HRA = Historical Radiological Assessment
IR = Installation Restoration
ISB = in-situ bioremediation
ITSI = Innovative Technical Solutions, Inc.
LFR = Levine Fricke Recon
NAVSEA = Naval Sea Systems Command
Navy = Department of the Navy
NFA = no further action
PCBs = polychlorinated biphenyls
PRC = PRC Environmental Management, Inc.
RI = remedial investigation
RMR = risk management review
ROD = Record of Decision
TCRA = time-critical removal action
TtEMI = Tetra Tech EM Inc.
USTs = underground storage tanks
VOCs = volatile organic compounds
ZVI = zero-valent iron

Table 8. RAOs and Remedy Components for Parcels D-1 and UC-1
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Soil and Soil Gas		
Prevent exposure to metals and PAHs in soil at concentrations above remediation goals developed in the human health risk assessment for the following exposure pathways: ▪ Ingestion of, outdoor inhalation of, and dermal exposure to surface and subsurface soil by industrial workers or construction workers	▪ Excavation and offsite disposal of soil in select areas where COCs exceed remediation goals[1] ▪ Removal and offsite disposal of select soil stockpiles[1]	▪ Durable covers ▪ Monitoring, maintenance, and ICs
Prevent exposure to VOCs in soil gas at concentrations that would pose unacceptable risk via indoor inhalation of vapors. Remediation goals for VOCs to address exposure via indoor inhalation of vapors may be superseded based on COC identification information from future soil gas surveys. Future action levels would be established for soil gas, would account for vapors from both soil and groundwater, and would be calculated based on a cumulative risk level of 10^{-6} using the accepted methodology for risk assessments at HPNS (ChaduxTt, 2011g; SES, 2013).	▪ None	▪ Soil gas surveys ▪ Monitoring and ICs
Groundwater		
Prevent exposure by industrial workers to VOCs in the A-aquifer groundwater at concentrations above remediation goals via indoor inhalation of vapors from groundwater. *This RAO for exposure to vapors from groundwater via vapor intrusion has been superseded by action levels established for soil vapor (ChaduxTt, 2011g; SES, 2013).*	▪ In-situ groundwater treatment using ZVI injections at IR-71[2]	▪ Soil gas surveys ▪ Monitoring (MNA) and ICs
Prevent or minimize exposure of construction workers to metals and VOCs in A-aquifer groundwater at concentrations above remediation goals from dermal exposure and inhalation of vapors from groundwater.	▪ In-situ groundwater treatment using ZVI injections at IR-71[2]	▪ Soil gas surveys ▪ Monitoring (MNA) and ICs

Table 8. RAOs and Remedy Components for Parcels D-1 and UC-1 *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Radiologically Impacted Soil and Structures		
Prevent exposure to ROCs in concentrations that exceed remediation goals for all potentially complete exposure pathways.	▪ Radiological surveys and remediation	▪ None

Notes:

1 = This component of the selected remedy for soil only applies to Parcel D-1.

2 = This component of the selected remedy for groundwater only applies to Parcel D-1.

COCs = chemicals of concern

HPNS = Hunters Point Naval Shipyard

ICs = institutional controls

IR = Installation Restoration

MNA = monitored natural attenuation

PAHs = polycyclic aromatic hydrocarbons

RAO = remedial action objective

ROCs = radionuclides of concern

SES = Sealaska Environmental Services LLC

VOCs = volatile organic compounds

ZVI = zero-valent iron

Table 9. RAOs and Remedy Components for Parcel G
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Soil and Soil Gas		
Prevent exposure to organic and inorganic chemicals in soil at concentrations above remediation goals developed in the HHRA for the following exposure pathways: ▪ Ingestion of, outdoor inhalation of, and dermal exposure to surface and subsurface soil ▪ Ingestion of homegrown produce by residents in mixed-use blocks	▪ Excavation and offsite disposal of soil in select areas where COCs exceed remediation goals ▪ Removal and offsite disposal of select soil stockpiles	▪ Durable covers ▪ Monitoring, maintenance, and ICs
Prevent exposure to VOCs in soil gas at concentrations that would pose unacceptable risk via indoor inhalation of vapors. Remediation goals for VOCs to address exposure via indoor inhalation of vapors have been superseded based on COC identification information from soil gas surveys. Future action levels would be established for soil gas, would account for vapors from both soil and groundwater, and would be calculated based on a cumulative risk level of 10^{-6} using the accepted methodology for risk assessments at HPNS (ChaduxTt, 2011g; SES, 2013).	▪ None	▪ Soil gas surveys ▪ Monitoring and ICs
Groundwater		
Prevent exposure to VOCs in A-aquifer groundwater at concentrations above remediation goals via indoor inhalation of vapors from groundwater. *This RAO for exposure to vapors from groundwater via vapor intrusion has been superseded by action levels established for soil vapor (ChaduxTt, 2011g; SES, 2013).*	▪ In-situ groundwater treatment using ZVI injections at IR-09, IR-33, and IR-71	▪ Soil gas surveys ▪ Monitoring (MNA) and ICs
Prevent direct exposure to groundwater that may contain COCs through the domestic use pathway (e.g., drinking water or showering).	▪ No treatment required	▪ Monitoring (MNA) and ICs

Table 9. RAOs and Remedy Components for Parcel G *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Groundwater *(continued)*		
Prevent or minimize exposure of construction workers to metals and VOCs in A-aquifer groundwater at concentrations above remediation goals from dermal exposure and inhalation of vapors from groundwater.	▪ In-situ groundwater treatment using ZVI injections at IR-09, IR-33, and IR-71	▪ Soil gas surveys ▪ Monitoring (MNA) and ICs
Prevent or minimize migration to surface water of San Francisco Bay of chromium VI and nickel in A-aquifer groundwater that would result in concentrations of chromium VI above 50 µg/L and nickel above 96.5 µg/L at the point of discharge to the bay.	▪ No treatment required	▪ Soil gas surveys ▪ Monitoring (MNA) and ICs
Radiologically Impacted Soil and Structures		
Prevent exposure to ROCs in concentrations that exceed remediation goals for all potentially complete exposure pathways.	▪ Radiological surveys and remediation	▪ None

Notes:
COCs = chemicals of concern
HHRA = human health risk assessment
HPNS = Hunters Point Naval Shipyard
ICs = institutional controls
IR = Installation Restoration
MNA = monitored natural attenuation
RAO = remedial action objective
ROCs = radionuclides of concern
SES = Sealaska Environmental Services LLC
VOCs = volatile organic compounds
ZVI = zero-valent iron
µg/L = micrograms per liter

Table 10. Pre-ROD Response Actions for Parcel E (i.e., Parcels E, E-2, and UC-3)
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
1988–1989	Solid Waste Air Quality Assessment Test	The study included evaluation of meteorological conditions, ambient air quality, landfill gas compositions, surface gas emissions, and subsurface gas migration. Methane was detected in isolated pockets at IR-01/21 and at the northern edge of the IR-01/21 boundary (HLA, 1989).
1988	OU RI Phase 1 Reconnaissance	Evaluated hydrogeologic conditions and identified waste boundaries using ground-penetrating radar, electromagnetic survey, and test pits to delineate the extent of waste depositions in fill material. Results were used to identify data needs for subsequent RI activities.
1988	Basewide Removal of PCB-Containing Electrical Transformers	Forty-eight transformers were removed from Parcel E and disposed of off site.
1988–1992	OU-1 RI	The Parcel E-2 Landfill progressed to the RI stage as IR-01/21 and was grouped (along with IR-02 and IR-03 in Parcel E) into OU-I. The first phase of the OU-I RI (from 1988 to 1989) included a geophysical survey and test pit excavation to delineate the extent of landfill waste, a soil gas survey to evaluate the presence of VOCs in soil and groundwater, and installation of deep soil borings to define subsurface stratigraphy. Subsequent investigation phases involved sampling of soil and groundwater (performed from 1990 to 1992).
1989	Removal of Soil at IR-08 PCB Spill Area	About 1,255 cubic yards of soil contaminated by PCBs was excavated from a PCB spill area, which underlies the southeast portion of Building 606 (ERM-West, 1989).
1991	Removal of Floating Product at IR-03	About 25 gallons of floating petroleum product on the water table and 70 gallons of subsurface waste oil were recovered by pumping and offsite disposal (HLA, 1991).
1991–1992	Intertidal Sediment Study	Sediment samples were collected in the intertidal zone, and the resulting data were used to identify COPECs in the Phase 1A ERA.
1993	Phase II Radiological Investigation	This investigation delineated the subsurface distribution of radium-containing devices in the disposal area at IR-02 Northwest and IR-02 Central. A removal action was recommended to address radiological contamination in this area. The removal action at IR-02 Northwest and IR-02 Central was performed from 2005 to 2007.
1994	SI	Site assessments were completed at Parcels B, C, D, and E and included field investigations at 75 sites. Further investigation was recommended for 28 of the 75 sites assessed. The PA/SI determined that the majority of the potential source areas required additional investigation (PRC, LFR, and Uribe and Associates, 1996a).

Table 10. Pre-ROD Response Actions for Parcel E (i.e., Parcels E, E-2, and UC-3) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
10/1997	RI	Based on the results from more than 4,700 soil and 1,200 groundwater samples, the RI Report recommended that all Parcel E sites be carried forward to an FS. Additionally, the report noted that additional soil and groundwater samples should be collected to better define the nature and extent of contamination at the parcel. The Parcel E RI also included a baseline ERA and HHRA.
1996	Exploratory Excavations at IR-11/14/15	About 36 cubic yards of arsenic- and mercury-contaminated soil was excavated from an area east of Building 521 at IR-11/14/15 (IT Corporation, 1999a).
1996–1997	Removal of Sediment from the Storm Drain System	More than 1,200 tons of sediment and debris was removed from storm drain lines across HPNS, including from storm drain lines in Parcel E.
1996–1997	Phase III Radiological Investigation	The investigation included surveys and swipe sampling at former NRDL buildings at Parcel E. Based on the investigation results, the report recommended (1) further investigation and potential excavation at former Buildings 509 and 517, where anomalous gamma activity was measured; (2) excavation of a potential buried point source behind Building 529; and (3) further investigation of Building 707 and its concrete pad.
1996–1998	Installation of Sheet-Pile Wall and Low-Permeability Cap at the Former Oily Waste Ponds in IR-03	A 900-foot-long sheet-pile wall was installed to a maximum depth of 27 feet bgs to reduce the potential for oil to migrate from IR-03 to San Francisco Bay. A geosynthetic clay liner with a 1-foot topsoil layer was placed over the area to minimize rainfall infiltration (IT Corporation, 1999b).
1997–1998	FS	Based on the data presented in the RI Report, the FS Report identified and evaluated remedial alternatives for Parcel E. However, the FS Report was not finalized because the Navy and regulatory agencies identified additional tasks to better characterize the nature and extent of contamination at Parcel E. These tasks were performed as part of data gaps investigations from 2000 through 2003, and results of these investigations were used in the Revised RI and FS Reports for Parcel E.
1997–1998	Groundwater Extraction System and Containment Barrier	A sheet-pile wall and groundwater extraction system were constructed along the southeastern portion of Parcel E-2 to prevent the potential transport of PCBs in groundwater to the bay (IT Corporation, 1999c).
1998–1999	Phase IV Radiological Investigation	In total, 38 concrete and 38 soil samples were collected from the Building 707 concrete pad area and analyzed for radionuclides. Based on the investigation results, a removal action was recommended to address elevated radioactivity at the concrete pad. The removal action at Building 707 was performed as part of the basewide radiological removal action that was initiated in 2009.

Table 10. Pre-ROD Response Actions for Parcel E (i.e., Parcels E, E-2, and UC-3) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
1999–2000	Parcel E Validation Study and Protective Soil Concentrations Technical Memorandum	Results of the study concluded cadmium, copper, lead, nickel, selenium, and zinc posed a potential unacceptable risk to wildlife at Parcel E. Protective soil concentrations were subsequently derived for these chemicals and used to evaluate risk to wildlife in the Revised Parcel E RI Report.
2000–2001	Interim Landfill Cap Construction	An interim cap was constructed over the landfill. The cap consisted of a multilayer system of sub-base soil, high-density polyethylene membrane, synthetic drainage layer, and topsoil and covered about 14.5 acres. The cap smothered any remaining subsurface smoldering areas following a brush fire on August 16, 2000, and also significantly reduced stormwater infiltration (TtEMI, 2005).
2000–2002	Groundwater Data Gaps Investigation	Water level measurements and results of a tidal study were used to refine the Parcel E hydrogeological conceptual model, and three rounds of groundwater monitoring data were used to develop a basewide groundwater monitoring program and to refine the nature and extent evaluation presented in the Revised RI Report.
2001–2002	Nonstandard Data Gaps Investigation	Separate evaluations were conducted to (1) delineate and characterize LFG, (2) identify the lateral extent of soil waste, and (3) assess the potential for subsurface layers to liquefy during an earthquake (TtEMI, 2003g and 2004g; TtEMI and ITSI, 2004b).
2000–2002	SVE Treatability Study	An SVE treatability study was completed at Building 406. The SVE system, which consisted of 3 SVE wells and 15 vapor monitoring wells, removed about 7 pounds of VOCs, with over 90 percent of the VOC mass attributed to TCE (IT Corporation, 2002f).
2001	Removal of Soil with Non-VOCs at IR-08	About 1,550 cubic yards of soil contaminated by PCBs and PAHs was excavated from four remediation areas at IR-08 (TtEMI and IT Corporation, 2001).
2001	Radiological Investigation of Parcel E Shoreline	Several areas contained gamma activity at levels exceeding background, most notably in the Metal Reef Area in IR-02 Southeast. A removal action was recommended to address radioactive materials in this area. The removal action at the Metal Reef Area was performed from 2005 to 2007.
2001–2002	Wetland Delineation and Wetland Functions Assessment	About 0.73 acres of tidal wetland areas was identified along the Parcel E shoreline. The functions and values assessment found that the value of these wetlands was low, and the most significant function of the wetlands was seasonal wildlife use for wintering and migrating birds.
2001–2005	Radiological Investigations, Phase V (and other interim investigations)	In 2001, a characterization survey of the Parcels E and E-2 shoreline was performed that identified the Metal Slag Area. The Phase V investigation was performed from 2002 to 2003. At Parcel E, 21 buildings or former building locations were evaluated as part of Phase V. Future investigation and cleanup were recommended for several sites, including Building 406; the area around former Buildings 506, 520, and 529; the Building 707 concrete pad and drains; the Shack 80 site; and IR-04.

Table 10. Pre-ROD Response Actions for Parcel E (i.e., Parcels E, E-2, and UC-3) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
2002	Standard Data Gaps Investigation	Data from this investigation were used in the Revised Parcel E RI Report to identify potential source areas of contamination, evaluate the nature and extent of soil contamination in each reuse area, and evaluate risk to human health and the environment.
2002–2004	Waste Consolidation and Removal	Industrial process equipment was decontaminated, and waste was removed and consolidated throughout Parcel E, including waste material stored in or near buildings and removal or encapsulation of ACM. Eight ASTs located at Building 521 were also removed (Tetra Tech FW, Inc., 2004b).
2002–2003	Construction of LFG Control System	A landfill gas control system was constructed along the northern edge of Parcel E-2 to reduce concentrations of methane in the subsurface and to prevent migration of landfill gas onto the nearby UCSF property (TtEMI, 2004a).
2002–2005	Parcels E and E-2 Shoreline Investigation and Risk Assessment	Shoreline investigation and associated ERA identified a potential risk to benthic invertebrates, birds, and mammals from exposure to metals and total PCBs in surface and subsurface sediments along the shoreline. Based on these results, source control measures were recommended for the Parcel E shoreline, particularly in IR-02 Northwest.
2003–2004	HRA	The HRA identified 33 areas in Parcel E as radiologically impacted. These sites included small areas such as former building foundation footprints and fill areas that may contain dials, gauges, deck markers, or sandblast waste. The HRA also identified basewide utility systems as impacted sites, including the underground storm drain and sanitary sewer lines. The HRA reported that no radiological contamination was suspected in groundwater at Parcel E, except at IR-02 and areas where storm drains are present; these areas have a low potential for groundwater contamination. The HRA concluded that further evaluation of the impacted sites was required (NAVSEA, 2004).
2003–2004	Parcel E Shoreline Debris Removal	Bricks and other industrial debris along the Parcel E shoreline were collected for disposal. About 468 cubic yards of non-RCRA hazardous waste debris (poles with creosote), about 400 cubic yards of nonregulated nonhazardous debris, and about 81 tons of recyclable metals were removed (Tetra Tech FW, Inc., 2004).
2003	Stockpile Inventory	The Navy inventoried all stockpiles at HPNS and identified 80 stockpiles at Parcel E.
2003–2004	Removal of Soil Stockpiles	Five soil stockpiles were removed from IR-73 and IR-02 Southeast and disposed of off site (TtEMI and ITSI, 2005).
2003–Present	Landfill Gas Monitoring and Control	Landfill gas is being monitored on a regular basis under the Interim Landfill Gas Monitoring and Control Plan to verify that hazardous concentrations of landfill gas are not migrating beyond the fence line of the landfill and onto the UCSF compound. The landfill gas control system is operated using both passive venting and active extraction.

Table 10. Pre-ROD Response Actions for Parcel E (i.e., Parcels E, E-2, and UC-3) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
2004	Removal of TPH-Contaminated Soil from Various Locations	Six areas at IR-05, IR-36 West, IR-39, and IR-73 were excavated to remove soil containing TPH at concentrations exceeding the screening criterion of 3,500 mg/kg. More than 13,000 cubic yards of soil was removed from these areas and disposed of off site.
2004	Metal Slag Area Characterization	Investigation included characterizing debris and slag in the Metal Slag Area suspected to have originated from the metal foundry (Building 241 in Parcel C) and the smelter (Building 408 in Parcel D) when the shipyard was active (Tetra Tech FW, Inc., 2005).
2005–2007	Metal Debris Reef Removal Action	Approximately 11,200 cubic yards of soil, metal slag, and debris was removed from the Metal Debris Reef area of IR-02 Southeast and the metal slag area of Parcel E-2 and disposed of off site. LLRW, including131 devices and button sources and 31 cubic yards of metal debris, was also removed (TtEC, 2007b).
2005–2007	Removal of Soil at IR-02 Northwest and IR-02 Central Area	Approximately 49,500 cubic yards of soil was removed from the IR-02 Northwest and Central areas and disposed of off site. LLRW, including 11,840 tons of soil, 2,342 devices and button sources, 420 tons of firebrick, 1,940 tons of metal debris, and 58 tons of miscellaneous debris (concrete, plastic, hoses, and rocks), was also removed (TtEC, 2007c).
2005–2007	PCB Hot Spot Area Removal Action (Phase I)	Approximately 44,500 cubic yards of soil and debris was removed from the PCB Hot Spot Area in the southern portion of Parcel E-2 and disposed of off site. LLRW, including 533 cy of soil and fire brick, 40 devices, and 78 cubic yards of metal debris, was also removed (TtEC, 2007a).
2008	Revised RI, including HHRA and ERA	During the Revised RI, additional data were collected to better characterize Parcel E to support remedy evaluation at the site. To address data gaps, additional field investigations were performed to gather supplementary information needed to support the remedy evaluation.
2009–2011	Groundwater Treatability Study at IR-56	Treatability study evaluated the use of ZVI to treat groundwater at IR-56.
2009–2012	Groundwater Characterization and ZVI Treatability Study at Various VOC Groundwater Plumes	The study further characterized VOC groundwater plumes in Parcel E and evaluated the effectiveness of ZVI injection in reducing VOC concentrations at two plumes (IR-12 PCE plume and Building 406 TCE plume). The characterization refined the extent of the VOC groundwater plumes and identified elevated VOC concentrations in soil gas at IR-04 and IR-36 (Building 406). The study determined that ZVI could effectively treat the VOC plumes but recommended additional monitoring to better assess post-injection groundwater conditions.

Table 10. Pre-ROD Response Actions for Parcel E (i.e., Parcels E, E-2, and UC-3) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
2009–present	Basewide Radiological TCRA	TCRA activities identified and removed LLRW with radioactivity levels exceeding the TCRA removal goals and remediation goals at all radiologically affected sites, including storm drain and sewer lines. The fieldwork on Parcel UC-3 was completed in June 2011.
2010–2012	PCB Hot Spot Area Removal Action (Phase II)	Approximately 42,200 cubic yards of additional soil and debris from the PCB Hot Spot Area, mainly bayward of the 2005 to 2007 removal actions, was removed and disposed of off site. LLRW, including 5,800 cubic yards of soil, concrete, fire brick, and metal wire and 56 devices, was also removed (Shaw, 2013e).
2011–2016	Characterization and Treatability Study at IR-03	An initial study (from 2011 to 2012) further characterized the extent of NAPL at IR-03, and tested heating technologies (to enhance NAPL removal) on a bench-scale. A pilot-scale study was completed in 2014 to test two technologies (in-situ stabilization/solidification and thermally enhanced NAPL extraction) in the field. An additional study was completed in 2015 to further characterize the NAPL extents and support a remedial design for IR-03 (ITSI, 2013; Cabrera Insight JV and CDM Smith, 2016a and 2016b).
2012	Ship-Shielding Area Removal Action	The top 1 foot of soil was removed from the 1.1-acre ship shielding range. In total, 3,413 cubic yards of excavated soil was screen to verify cobalt-60 was not detected above the release criterion.
8/2012	Final FS	The FS identified, screened, and evaluated remedial alternatives for cleanup of soil and groundwater at Parcel E.
11/2012	ROD for Parcel E-2	The selected remedy documented in the original ROD included excavation and offsite disposal of contaminated soil and sediment, radiological remediation of soil, sediment, and structures, soil cover with protective liner, shoreline revetment, below-ground barriers, removal and treatment of landfill gas, and monitoring, maintenance, and institutional controls.
2013	Soil Excavation Characterization	A soil investigation was conducted to determine the lateral and vertical extent of COCs associated with excavation areas in Parcel UC-3.
12/2013	ROD for Parcel E	The selected remedy documented in the original ROD included excavation and offsite disposal of contaminated soil and sediment, radiological remediation of soil and structures, SVE, durable covers and shoreline protection, groundwater treatment using ZVI and ISB, MNA, below-ground barriers and protective liners, groundwater monitoring, containment and in-situ stabilization of NAPL at IR-03, and institutional controls.
1/2014	ROD for Parcel UC-3	The selected remedy documented in the original ROD included excavation and offsite disposal of contaminated soil, radiological remediation of soil and structures, clean and close steam lines, soil gas monitoring, durable covers, groundwater treatment using ISB, MNA, and institutional controls.

Table 10. Pre-ROD Response Actions for Parcel E (i.e., Parcels E, E-2, and UC-3) *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Notes:

1 = The documents listed are available in the Administrative Record and provide detailed information used to support remedy selection at Parcels E, E-2, and UC-3.

ACM = asbestos-containing material
ASTs = aboveground storage tanks
Battelle = Battelle Memorial Institute
bgs = below ground surface
Cabrera = Cabrera Services, Inc.
COPECs = chemicals of potential ecological concern
ERA = ecological risk assessment
ERM-West = Environmental Resources Management West, Inc.
FS = Feasibility Study
HHRA = human health risk assessment
HLA = Harding Lawson Associates
HPNS = Hunters Point Naval Shipyard
HRA = Historical Radiological Assessment
Insight = Insight Environmental, Engineering, and Construction, Inc.
IR = Installation Restoration
ITSI = Innovative Technical Solutions, Inc.
ISB = in-situ bioremediation
JV = Joint Venture
LFR = Levine Fricke Recon
LLRW = low-level radioactive waste
mg/kg = milligrams per kilogram
MNA = monitored natural attenuation
NAPL = nonaqueous-phase liquid
NAVSEA = Naval Sea Systems Command
NRDL = Naval Radiological Defense Laboratory
OU = Operable Unit
PAHs = polycyclic aromatic hydrocarbons
PCB = polychlorinated biphenyl
PCE = tetrachloroethene
PRC = PRC Environmental Management, Inc.
RCRA = Resource Conservation and Recovery Act
RI = Remedial Investigation
Shaw = Shaw Environmental, Inc.
SVE = soil vapor extraction
TCE = trichloroethene
TCRA = time-critical removal action
TPH = total petroleum hydrocarbons
TtEMI = Tetra Tech EM Inc.
UCSF = University of California, San Francisco
USTs = underground storage tanks
VOCs = volatile organic compounds
ZVI = zero-valent iron

Table 11. RAOs and Remedy Components for Parcel E
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Soil, Soil Gas, and Shoreline Sediment		
Prevent exposure of humans to COCs in soil at concentrations exceeding remediation goals for (1) ingestion of, outdoor inhalation of, and dermal exposure to soil from 0 to 10 feet bgs by residents in areas zoned for mixed-use reuse; (2) ingestion of homegrown produce in native soil in areas zoned for mixed-use reuse; (3) ingestion of, outdoor inhalation of, and dermal exposure to soil from 0 to 2 feet bgs by recreational users in areas zoned for open space reuse; and (4) ingestion of, outdoor inhalation of, and dermal exposure to soil from 0 to 10 feet bgs by construction workers in all areas.	▪ Excavation and offsite disposal of Tier 1, Tier 2, and TPH locations ▪ Closure of fuel and steam lines	▪ Durable covers ▪ Monitoring, maintenance, and ICs
Prevent exposure of humans to VOCs in soil gas at concentrations that would pose unacceptable risk via indoor inhalation of vapors.	▪ Excavation and offsite disposal of Tier 1 and Tier 2 locations ▪ SVE at Building 406 ▪ In-situ groundwater treatment at Building 406, IR-04, and IR-12	▪ Soil gas surveys ▪ Monitoring and ICs
Prevent exposure of humans to COCs in shoreline sediment at concentrations exceeding remediation goals.	▪ Excavation and offsite disposal of Tier 1, Tier 2, and TPH locations ▪ Shoreline protection (excavate sediment)	▪ Shoreline protection (place protective material) ▪ Monitoring, maintenance, and ICs
Prevent exposure of benthic invertebrates, birds, and mammals to COECs in shoreline sediment at concentrations exceeding remediation goals.	▪ Excavation and offsite disposal of Tier 1, Tier 2, and TPH locations ▪ Shoreline protection (excavate sediment)	▪ Shoreline protection (place protective material) ▪ Monitoring, maintenance, and ICs

Table 11. RAOs and Remedy Components for Parcel E *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Groundwater		
Prevent or minimize exposure of construction workers to VOCs in A-aquifer groundwater by dermal exposure and inhalation of vapors with chemicals exceeding remediation goals.	▪ In-situ groundwater treatment at Building 406, IR-04, and IR-12	▪ Soil gas surveys ▪ Monitoring and ICs
Prevent or minimize exposure of humans to COCs in the B-aquifer at concentrations exceeding remediation goals via the domestic use pathway.	▪ No treatment required	▪ Monitoring (MNA) and ICs
Prevent or minimize migration of arsenic, copper, lead, nickel, zinc, Aroclor-1254, Aroclor-1260, alpha-chlordane, and 4,4'-DDE to prevent discharge (into San Francisco Bay) that would result in concentrations exceeding corresponding surface water quality criteria for aquatic wildlife.	▪ Excavation and offsite disposal of Tier 1 and Tier 2 locations ▪ NAPL source removal and treatment at IR-03	▪ Durable cover (with protective liner) ▪ Groundwater controls (below-ground barrier) at IR-02 Northwest and IR-03 ▪ Monitoring (MNA), maintenance, and ICs
Prevent or minimize migration of A-aquifer groundwater containing total TPH concentrations greater than 1,400 µg/L (where commingled with CERCLA-regulated substances) into San Francisco Bay.	▪ Excavation and offsite disposal of TPH locations ▪ NAPL source removal and treatment at IR-03 ▪ Groundwater treatment at IR-03	▪ Durable cover (with protective liner) ▪ Groundwater controls (below-ground barrier) at IR-02 Northwest and IR-03 ▪ Monitoring (MNA), maintenance, and ICs
NAPL at IR-03 (Former Oily Waste Ponds)		
Prevent or minimize migration of NAPL to prevent discharge that would result in concentrations of COECs exceeding corresponding surface water quality criteria for aquatic wildlife.	▪ NAPL source removal and treatment at IR-03 ▪ Groundwater treatment at IR-03	▪ Durable cover (with protective liner) ▪ Groundwater controls (below-ground barrier) at IR-03 ▪ Monitoring (MNA), maintenance, and ICs

Table 11. RAOs and Remedy Components for Parcel E *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
NAPL at IR-03 (Former Oily Waste Ponds) *(continued)*		
Prevent or minimize migration of NAPL to prevent discharge that would result in total TPH groundwater concentrations greater than 1,400 µg/L into San Francisco Bay.	▪ NAPL source removal and treatment at IR-03 ▪ Groundwater treatment at IR-03	▪ Groundwater controls (below-ground barrier) at IR-03 ▪ Monitoring (MNA), maintenance, and ICs
Radiologically Impacted Media (Soil, Shoreline Sediment, and Structures)		
Prevent exposure to ROCs at activity levels that exceed remediation goals for all potentially complete exposure pathways (which include external exposure, ingestion, and inhalation of soil based on the conceptual site model for human health).	▪ Radiological surveys and remediation ▪ Radiological surface surveys and removal of anomalies	▪ Durable covers (with demarcation layer at IR-02 and IR-03) ▪ Monitoring, maintenance, and ICs

Notes:
bgs = below ground surface
CERCLA = Comprehensive Environmental Response, Compensation, and Liability Act
COCs = chemicals of concern
COECs = chemicals of ecological concern
DDE = dichlorodiphenyldichloroethene
ICs = institutional controls
IR = Installation Restoration
MNA = monitored natural attenuation
NAPL = nonaqueous-phase liquids
RAOs = remedial action objectives
ROCs = radionuclides of concern
SVE = soil vapor extraction
TPH = total petroleum hydrocarbons
VOCs = volatile organic compounds
µg/L = micrograms per liter

Table 12. RAOs and Remedy Components for Parcel E-2
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Soil and Sediment		
Prevent human exposure to inorganic and organic chemicals at concentrations greater than remediation goals for the following exposure pathways: ▪ Ingestion of, outdoor inhalation of, and dermal exposure to solid waste, soil, or sediment from 0 to 2 feet bgs by recreational users throughout Parcel E-2. ▪ Ingestion of, outdoor air inhalation of, and dermal exposure to solid waste, soil, or sediment from 0 to 10 feet bgs by construction workers throughout Parcel E-2.	▪ Excavation and offsite disposal of soil, sediment, and debris at hot spot areas	▪ Soil cover (with protective liner) ▪ Shoreline revetment ▪ Onsite consolidation of waste materials beneath the soil cover ▪ Monitoring, maintenance, and ICs
Prevent terrestrial wildlife exposure to concentrations of inorganic and organic chemicals in solid waste or soil greater than remediation goals from 0 to 3 feet bgs throughout Parcel E-2.	▪ Excavation and offsite disposal of soil, sediment, and debris at hot spot areas	▪ Soil cover (with protective liner) ▪ Onsite consolidation of waste materials beneath the soil cover ▪ Monitoring, maintenance, and ICs
Prevent aquatic wildlife exposure to concentrations of inorganic and organic chemicals in intertidal sediment greater than remediation goals from 0 to 2.5 feet bgs throughout the Shoreline Area.	▪ Excavation and offsite disposal of soil, sediment, and debris at hot spot areas	▪ Shoreline revetment ▪ Monitoring, maintenance, and ICs
Prevent exposure to ROCs at activity levels that exceed remediation goals for all potentially complete exposure pathways.	▪ Radiological surveys and remediation (including radiological screening of excavated material) ▪ Radiological surface survey and removal of anomalies	▪ Soil cover (with demarcation layer) ▪ Monitoring, maintenance, and ICs

Table 12. RAOs and Remedy Components for Parcel E-2 *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Landfill Gas		
Control methane concentrations to 5 percent (by volume in air) or less at subsurface points of compliance.	▪ LFG controls (active LFG collection and treatment)	▪ Monitoring, maintenance, and ICs
Control methane concentrations to 1.25 percent (by volume in air) or less in onsite structures ("on site" defined in the Parcel E-2 ROD as any area within the subsurface points of compliance for landfill gas).	▪ LFG controls (active LFG collection and treatment)	▪ Monitoring, maintenance, and ICs
Prevent exposure to NMOCs at concentrations greater than 500 ppmv at the subsurface points of compliance.	▪ LFG controls (active LFG collection and treatment)	▪ Monitoring, maintenance, and ICs
Prevent exposure to NMOCs at concentrations greater than 5 ppmv above background levels in the breathing zone of onsite workers and visitors.	▪ LFG controls (active LFG collection and treatment)	▪ Monitoring, maintenance, and ICs
Groundwater (Domestic Use)		
Prevent exposure to groundwater that may contain COCs at concentrations greater than remediation goals through the domestic use pathway.	▪ No treatment required	▪ Monitoring (MNA) and ICs
Prevent or minimize migration of B-aquifer groundwater that may contain COCs at concentrations greater than remediation goals beyond the point of compliance (defined in the RI/FS Report at the downgradient boundary of Parcel E-2).	▪ No treatment required	▪ Monitoring (MNA) and ICs
Groundwater (Construction Worker)		
Prevent or minimize dermal exposure to and vapor inhalation from A-aquifer groundwater containing COCs at concentrations greater than remediation goals by construction workers.	▪ No treatment required	▪ Monitoring (MNA) and ICs

Table 12. RAOs and Remedy Components for Parcel E-2 *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Groundwater (Protection of Wildlife)		
Prevent or minimize migration of COPECs to prevent discharge that would result in concentrations greater than the corresponding water quality criteria for aquatic wildlife.	▪ No treatment required	▪ Groundwater controls (consisting of below-ground barriers) to limit contaminant migration ▪ Soil cover (with protective liner that limits surface water infiltration) ▪ Monitoring (MNA), maintenance, and ICs
Prevent or minimize migration of A-aquifer groundwater containing total TPH concentrations greater than the remediation goal (where commingled with CERCLA substances) into San Francisco Bay.	▪ No treatment required	▪ Groundwater controls (consisting of below-ground barriers) to limit contaminant migration ▪ Soil cover (with protective liner that limits surface water infiltration) ▪ Monitoring (MNA), maintenance, and ICs
Surface Water		
Prevent or minimize migration of COPECs to prevent discharge that would result in concentrations greater than the corresponding water quality criteria for aquatic wildlife.	▪ No treatment required	▪ Groundwater controls (consisting of below-ground barriers) to limit contaminant migration ▪ Soil cover (with protective liner to limit surface water infiltration) ▪ Monitoring (MNA), maintenance, and ICs

Notes:
bgs = below ground surface
CERCLA = Comprehensive Environmental Response, Compensation, and Liability Act
COCs = chemicals of concern
COPECs = chemicals of potential ecological concern
ICs = institutional controls
MNA = monitored natural attenuation
NMOCs = nonmethane organic compounds
ppmv = parts per million by volume
RAOs = remedial action objectives
RI/FS = Remedial Investigation/Feasibility Study
ROCs = radionuclides of concern
ROD = Record of Decision
TPH = total petroleum hydrocarbons

Table 13. RAOs and Remedy Components for Parcel UC-3
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Soil and Soil Gas		
Prevent unacceptable exposure of humans to chemicals and radionuclides in soil at concentrations exceeding the remediation goals (see Table 7 of the ROD [Navy, 2014a]) for the following exposure pathways: ▪ Ingestion of, outdoor inhalation of, and dermal exposure to soil from 0 to 10 feet bgs by residents in areas zoned for mixed-use reuse. ▪ Ingestion of homegrown produce in native soil in areas zoned for mixed-use reuse. ▪ Ingestion of, outdoor inhalation of, and dermal exposure to soil from 0 to 10 feet bgs by construction workers in all areas. ▪ Ingestion of, outdoor inhalation of, and dermal exposure to soil from 0 to 10 feet bgs by industrial users of the railroad right-of-way.	▪ Excavation and offsite disposal of soil from Tier 2 and TPH locations ▪ Steam line closure[1]	▪ Durable covers within Redevelopment Block MU-3 ▪ Monitoring, maintenance, and ICs
Prevent exposure of humans to VOCs in soil gas at concentrations that would pose unacceptable risk via indoor inhalation of vapors. Table 7 of the final soil gas memorandum (ChaduxTt, 2011g) lists risk-based action levels for various volatile chemicals, including SVOCs, that may pose an unacceptable risk via indoor inhalation of vapors. *Note: The soil gas action levels referenced in the RAO will be used for an initial risk-based screening of data collected during future soil gas surveys (such as the surveys to be performed at the IR-56 VOC groundwater plume following active treatment). After the initial risk-based screening, areas with unacceptable risk will be further evaluated using location-specific data (i.e., physical characteristics of the soil) to assess potential exposures consistent with the State of California and EPA vapor intrusion guidance. In addition, risks and hazards at these areas will be further characterized using the accepted methodology for risk assessments at HPNS.*	▪ None	▪ Soil gas surveys ▪ Monitoring and ICs

Table 13. RAOs and Remedy Components for Parcel UC-3 *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

RAO	Remedy Component: Removal or Treatment of Contaminant Mass	Remedy Component: Containment, Monitoring, Maintenance, and ICs
Groundwater		
Prevent or minimize unacceptable exposure of humans to COCs in the B-aquifer at concentrations exceeding remediation goals (see Table 8 of the ROD [Navy, 2014a]) via the domestic use pathway.	▪ Anaerobic in-situ bioremediation at IR-56[2]	▪ MNA and ICs
Prevent or minimize unacceptable exposure of construction workers to VOCs in A-aquifer groundwater by dermal exposure and inhalation of vapors with chemicals exceeding remediation goals.	▪ Anaerobic in-situ bioremediation at IR-56[2]	▪ MNA and ICs
Radiologically Impacted Soil and Structures		
Prevent exposure to radiological isotopes at activity levels that exceed remediation goals for all potentially complete exposure pathways (which include external exposure, ingestion, and inhalation of soil based on the conceptual site model for human health. *Note: The RAO for radiologically impacted media was satisfied prior to publication of the ROD through removal actions at Parcel UC-3. Excavation of radiologically impacted sewer and storm drain lines was completed under a TCRA in 2011. The removal action included all sewer and storm drain lines as well as potentially impacted soil. A Radiological RACR for Parcel UC-3 was submitted on March 16, 2012, and received concurrence for radiological unrestricted release from DTSC on October 31, 2012. All work required by the selected radiological remedy, Alternative R-2, has been completed and no additional actions are required. Selection of Alternative R-2 is documented in the ROD (Navy, 2014a).*	▪ Radiological surveys and remediation	▪ None

Table 13. RAOs and Remedy Components for Parcel UC-3 *(continued)*
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Notes:

1 = The steam line closure component of the selected soil remedy was deemed unnecessary to achieve the soil RAO, because the steam lines within Parcel UC-3 were (1) not used for conveying oil; (2) assessed during previous site investigations and found to display no evidence of contamination; and (3) found to be outside the area where previous investigations had identified waste oil contamination in steam lines (Amec Foster Wheeler Environment & Infrastructure, Inc., 2016a).

2 = Groundwater monitoring conducted in Parcel UC-3 revealed that TCE concentrations at the IR-56 plume have been less than the remediation goal in the Final ROD since monitoring began in 1996, and below the vapor intrusion criterion since the end of 2009 (Amec Foster Wheeler Environment & Infrastructure, Inc., 2016a). As a result, remediation of groundwater by in-situ bioremediation, as specified in the Final ROD (Navy, 2014a), was deemed unnecessary to achieve the groundwater RAOs and was excluded from the remedial design.

bgs = below ground surface

COCs = chemicals of concern

DTSC = Department of Toxic Substances Control

EPA = U.S. Environmental Protection Agency

ICs = institutional controls

IR = Installation Restoration

MNA = monitored natural attenuation

Navy = Department of the Navy

RACR = Remedial Action Completion Report

RAOs = remedial action objectives

ROD = Record of Decision

SVOCs = semivolatile organic compounds

TCE = trichloroethene

TCRA = time-critical removal action

TPH = total petroleum hydrocarbons

VOCs = volatile organic compounds

Table 14. Pre-ROD Response Actions for Parcel F
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Date(s)	Response Action[1]	Description
1998	Draft FS	Data from the FS established two remediation footprints for Parcel F based on different decision flow processes. Five areas (I, III, VIII, IX, and X) were identified as the areas of highest ecological hazard (TtEMI and LFR, 1998a).
2000	Validation Study	A Validation Study was conducted to further investigate five areas identified in the FS and to refine the ERA.
2002	Shoreline Characterization to Evaluate Sediment Contamination	Shoreline characterization to evaluate whether contamination in Parcels E and E-2 had the potential to migrate, or had already migrated, to sediments in the adjacent offshore area of Parcel F (SulTech, 2005).
2003	FS Data Gaps Investigation	The data gaps investigation was conducted to collect additional data for subtidal sediment to support the Parcel F FS Report for Areas III and X, and to delineate surface sediments for mercury between Areas VIII and IX (Battelle, Neptune & Company, and Sea Engineering, Inc., 2007).
2006–2007	Sediment Treatability Study	Treatability study for sediment in tidal mudflats using activated carbon for field treatment of PCBs (Cho et al., 2007).
4/2008	Final FS	The FS identified, screened, and evaluated remedial alternatives for cleanup of sediment at Parcel F (Barajas & Associates, Inc., 2008a).
1/2011–9/2011	Removal of Wooden Remnants	Wooden piers and remnants of wooden berths, quay walls, and wharves adjacent to Parcels B and C were removed and disposed of off site (ERS Joint Venture, 2012).
2009–2013	Radiological Data Gaps Investigations	Radiological data gaps investigations (Battelle and Sea Engineering, Inc., 2013 and ITSI Gilbane and SAIC, 2013).
1/2016	FS Addendum	The FS addendum specified that no additional radiological investigation or remediation for radionuclides in sediment is warranted and institutional controls will be implemented to manage the risk associated with future exposure to radiological objects during dredging.
2016–2017	Activated Carbon Field Demonstration	A field study was performed to demonstrate the effectiveness of activated carbon as a means of sequestering PCBs in sediment at Parcel F. The results of the study confirmed the technology's viability as a treatment method for Parcel F.
4/2018	Proposed Plan	The Proposed Plan recommends focused removal/backfill, offsite disposal, capping, and institutional controls for Area III, and focused removal/backfill, in-situ treatment, offsite disposal, monitored natural recovery, and institutional controls for Areas IX and X. The ROD for Parcel F has not been published.

Notes:
Battelle = Battelle Memorial Institute
ERA = ecological risk assessment
FS = Feasibility Study
LFR = Levine Fricke Recon
PCBs = polychlorinated biphenyls
TtEMI = Tetra Tech EM Inc.

Table 15. Soil Cleanup Levels
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Primary COC in Soil	ROD Residential RG[1] (mg/kg)	ROD Industrial RG[1] (mg/kg)	Current Residential RSL[2] (mg/kg)	Current Industrial RSL[2] (mg/kg)	DTSC-SL Residential[3] (mg/kg)	DTSC-SL Industrial[3] (mg/kg)	Laboratory-Specific Limits Soil[4] (mg/kg)		
							DL	LOD	LOQ
Arsenic	11.1 (HPAL)	11.1 (HPAL)	0.68	3.0	0.11	0.36	NA	NA	NA
Benzo(a)pyrene	0.33 (PQL)	0.33 (PQL)	0.11	2.1	0.11	2.1	0.00047	0.0033	0.0066
Aroclor-1260	0.21 (RBC)	1.0 (RBC)	0.24	0.99	0.24	0.99	0.00801	0.01	0.033

Notes:

1 = As provided in the ROD for each parcel.

2 = EPA RSLs dated May 2018 (available online at: <https://www.epa.gov/risk/regional-screening-levels-rsls-generic-tables>).

3 = CalEPA DTSC-SLs in "Human Health Risk Assessment (HHRA) Note; HERO HHRA Note Number: 3, DTSC-Modified Screening Levels (DTSC-SLs). Release Date: January 2018 (available online at: <http://www.dtsc.ca.gov/AssessingRisk/humanrisk2.cfm>).

4 = TestAmerica Laboratory-specific limits for soil using EPA Method 8270D SIM for PAHs and EPA Method 8082A for PCBs.

CalEPA = California Environmental Protection Agency

COC = chemical of concern

DL = detection limit

DTSC-SL = Department of Toxic Substances Control-modified screening level

EPA = U.S. Environmental Protection Agency

HPAL = Hunters Point ambient level

LOD = limit of detection

LOQ = limit of quantitation

mg/kg = milligrams per kilogram

PAHs = polycyclic aromatic hydrocarbons

PCBs = polychlorinated biphenyls

PQL = practical quantitation limit

RBC = risk-based concentration

RG = remediation goal

ROD = Record of Decision

Table 16. Groundwater Cleanup Levels
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Primary COC in Groundwater	ROD Residential RG for Vapor Intrusion[1] (µg/L)	ROD Industrial RG for Vapor Intrusion[1] (µg/L)	Residential VISL[2] (µg/L)	Industrial VISL[2] (µg/L)	Laboratory-Specific Limits for Groundwater[3] (µg/L)		
					DL	LOD	LOQ
Tetrachloroethene	1.0 (PQL)	1.0 (PQL)	15	65	0.18	0.05	1.0
Trichloroethene	2.9 (RBC)	4.8 (RBC)	1.2	7.4	0.25	0.5	1.0
Vinyl chloride	0.5 (PQL)	0.5 (PQL)	0.15	2.5	0.194	0.25	2.0

Notes:

1 = As provided in the ROD for each parcel.

2 = EPA VISLs available as an online calculator at: <https://www.epa.gov/vaporintrusion/vapor-intrusion-screening-level-calculator>.

3 = TestAmerica Laboratory-specific limits for groundwater using EPA Method 8260B.

COC = chemical of concern

DL = detection limit

EPA = U.S. Environmental Protection Agency

LOD = limit of detection

LOQ = limit of quantitation

PQL = practical quantitation limit

RBC = risk-based concentration

RG = remediation goal

ROD = Record of Decision

VISL = vapor intrusion screening level

µg/L = micrograms per liter

Appendix A. List of References and Documents Reviewed

Accord MACTEC Joint Venture, 2009b. "2008/2009 Storm Water Discharge Management Plan Update, Hunters Point Shipyard, San Francisco, California." October.

_____, 2010. "2009/2010 Storm Water Monitoring Report, Hunters Point Shipyard, San Francisco, California." June.

_____, 2013. "2012/2013 Storm Water Monitoring Report, Hunters Point Naval Shipyard, San Francisco, California." June.

AFA Construction Group and Eagle Environmental Construction, 2005. "Final 2004–2005 Annual Report for Storm Water Discharge Management IR-01/21, Industrial Landfill, Parcel E-2, Hunters Point Shipyard, San Francisco, California." June 30.

Amec Foster Wheeler Environment & Infrastructure, Inc., 2016a. "Final Remedial Design and Design Basis Report for Parcel UC-3, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2016b. "Final Work Plan, Petroleum Hydrocarbon Investigation and/or Correction Action (Includes Final Sampling and Analysis Plan, Field Sampling Plan, and Quality Assurance Project Plan), Petroleum Hydrocarbon Investigation and Corrective Action, Hunters Point Naval Shipyard, San Francisco, California." November 18.

Aptim Federal Services, LLC (APTIM), 2017a. "Final Work Plan, Basewide Radiological Support, Hunters Point Naval Shipyard, San Francisco, California." October.

_____, 2017b. "Final Radiation Protection Plan, Radiological Work Tasks, Remedial Action and Maintenance of Remedies at Hunters Point Naval Shipyard, San Francisco, California." October.

_____, 2018a. "Final Post-Construction Operation and Maintenance Plan, Remedial Action in Parcel D-1, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2018b. "Final Interim Remedial Action Completion Report, Parcel C Remedial Action, Remedial Units C1, C4, and C5, and Building 241 (Excludes C2), Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2018c. [draft Phase 1 RAWP for Parcel E]

_____, XXXX. [IRACR for Parcel C]

Aqua Terra Technologies, Inc., 1991. "Environmental Sampling and Analysis Plan for Naval Station, Treasure Island, Hunters Point Annex, San Francisco, California." Volumes I and II. July 31.

ARCADIS U.S., Inc. (ARCADIS), 2012. "Final Parcel E Soil Excavation Characterization Work Plan, Hunters Point Naval Shipyard, San Francisco, California." August.

_____, 2012. "Final Remedial Action Work Plan for Parcel G, Hunters Point Naval Shipyard, San Francisco, California." December.

ARCADIS, 2013. "Final Work Plan, Loading, Transportation, and Removal of Waste Material, Hunters Point Naval Shipyard, San Francisco, California." October 31.

_____, 2014a. "Final Remedial Action Completion Report, Durable Cover, Groundwater Treatment, and Institutional Controls for Parcel G, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2014b. "Final Operation and Maintenance Plan for Parcel G, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2014c. "Final Work Plan, Loading, Transportation, and Removal of Waste Material, Hunters Point Naval Shipyard, San Francisco, California." December 1.

_____, 2015. "Final Operation and Maintenance Inspection Annual Summary Report for Parcel G, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2016. "Final Operation and Maintenance Inspection Annual Summary Report for Parcel G, Hunters Point Naval Shipyard, San Francisco, California." August.

Barajas & Associates, Inc., 2008. "Final Feasibility Study Report, Parcel F, Hunters Point Shipyard, San Francisco, California." April 30.

_____, 2008. "Final Revised Remedial Investigation Report, Parcel E, Hunters Point Shipyard, San Francisco, California." May 2.

Battelle Memorial Institute (Battelle), 1996. "Field Demonstration Report on Recycling Spent Sandblasting Grit into Asphaltic Concrete, Volume I, Field Demonstration Test Methods, Results and Conclusions." January 11.

Battelle and Sea Engineering, Inc., 2012. "Draft Technical Memorandum for Radiological Data Gap Investigation Phase 2a at Parcel F Submarine Areas, Parcel B Revetment Wall Areas, and San Francisco Bay Reference Sites, Hunters Point Naval Shipyard, San Francisco Bay, California." July.

_____, 2013. "Final Technical Memorandum for Radiological Data Gap Investigation Phase 2a at Parcel F Submarine Areas, Parcel B Revetment Wall Areas, and San Francisco Bay Reference Sites, Hunters Point Naval Shipyard, San Francisco Bay, California." April.

Battelle, Entrix, Inc., and Neptune & Company, 2001. "Final Hunters Point Shipyard Parcel F, Validation Study Work Plan, San Francisco Bay, California." November.

Battelle, Neptune and Company, and Sea Engineering, Inc., 2007. "Technical Memorandum, Parcel F Feasibility Study Data Gaps Investigation, Hunters Point Shipyard, San Francisco, California." July.

Battelle, Sea Engineering, Inc., and CH2M HILL, 2011. "Final Work Plan for Radiological Data Gap Investigation at Parcel F, Hunters Point Naval Shipyard, San Francisco Bay, California." August.

Cabrera Insight Joint Venture (CIJV) and CDM Smith, 2013. "Final NAPL Treatment Pilot Study Work Plan for Installation Restoration Site 03, Former Oily Waste Ponds, Parcel E, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014. "Final In Situ Stabilization/Solidification Design, NAPL Treatment Pilot Study, Installation Restoration Program Site 03, Former Oily Waste Ponds, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2015. "Final NAPL Treatment Pilot Study Work Plan Addendum for Installation Restoration Site 03, Former Oily Waste Ponds, Parcel E, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2016a. "Final NAPL Treatment Pilot Study Completion Report for Installation Restoration Site 03, Former Oily Waste Ponds, Parcel E, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2016b. "Final Post-Pilot Study Site-Wide Characterization Technical Memorandum for Installation Restoration Site 03, Former Oily Waste Ponds, Parcel E, Hunters Point Naval Shipyard, San Francisco, California." June.

California Department of Public Health (CDPH). 2013. Concurrence with the Draft IR-07 and IR-18 Radiological Risk and Dose Modeling Review, April 23, 2012, Hunters Point Naval Shipyard, San Francisco Bay, California. May 20.

CB&I Federal Services LLC (CB&I), 2014. "Final Remedial Action Work Plan, Remedial Action in Parcel D-1, Hunters Point Naval Shipyard, San Francisco, California." January.

_____, 2015a. "Final Work Plan Addendum, Groundwater and Soil Vapor Characterization in Support of Parcel C Remedial Action, Remedial Units C1, C4, and C5, Hunters Point Naval Shipyard, San Francisco, California." February.

_____, 2015b. "Final Technical Memorandum, Groundwater and Soil Vapor Characterization in Support of Parcel C Remedial Action, Remedial Unit C5, Hunters Point Naval Shipyard, San Francisco, California." August.

_____, 2015c. "Final Work Plan Addendum 01, Parcel C Remedial Action, Remedial Units C1, C4, C5, and Building 241 (Excludes C2), Hunters Point Naval Shipyard, San Francisco, California." October.

_____, 2015d. "Final Work Plan, Basewide Radiological Support, Hunters Point Naval Shipyard, San Francisco, California." December 8.

_____, 2016a. "Final Revision 1, Final Remedial Action Work Plan, Remedial Action in Parcel D-1, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2016b. "Final Work Plan, Shoreline Revetment; Site Grading and Consolidation of Excavated Soil, Sediment, and Debris; and Upland Slurry Wall Installation, Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." October.

CB&I, 2017a. "Air Monitoring Summary Report, Shoreline Revetment; Site Grading and Consolidation of Excavated Soil, Sediment, and Debris; and Upland Slurry Wall Installation, Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." February.

_____, 2017b. "Air Monitoring Summary Report, Shoreline Revetment; Site Grading and Consolidation of Excavated Soil, Sediment, and Debris; and Upland Slurry Wall Installation, Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2017c. "Air Monitoring Summary Report, Shoreline Revetment; Site Grading and Consolidation of Excavated Soil, Sediment, and Debris; and Upland Slurry Wall Installation, Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." July.

_____, 2017d. "Air Monitoring Summary Report, Shoreline Revetment; Site Grading and Consolidation of Excavated Soil, Sediment, and Debris; and Upland Slurry Wall Installation, Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." October.

CDM Smith, 2012. "Final Treatability Study Completion Report, Remedial Unit-C5, Building 134, Hunters Point Naval Shipyard, San Francisco, California." Volumes 1 and 2. January 27.

CE2-Kleinfelder Joint Venture, 2009. "Semiannual Groundwater Monitoring Report (October 2008 – March 2009), Hunters Point Shipyard, San Francisco, California." July.

_____, 2010a. "Semiannual Groundwater Monitoring Report (April – September 2009), Hunters Point Shipyard, San Francisco, California." February.

_____, 2010b. "Semiannual Groundwater Monitoring Report (October 2009 – March 2010), Hunters Point Shipyard, San Francisco, California." June.

_____, 2011a. "Semiannual Groundwater Monitoring Report (April – September 2010), Hunters Point Shipyard, San Francisco, California." February.

_____, 2011b. "Final Amended Sampling and Analysis Plan (Field Sampling Plan and Quality Assurance Project Plan) for Basewide Groundwater Monitoring Program, Hunters Point Shipyard, San Francisco, California." April.

_____, 2011c. "Semiannual Groundwater Monitoring Report (October 2010 – March 2011), Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2012a. "Semiannual Groundwater Monitoring Report (April – September 2011), Hunters Point Naval Shipyard, San Francisco, California." January.

_____, 2012b. "Final Technical Memorandum for Monitoring Program Optimization in Parcels B, D-1, G, and UC-2, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2012c. "Final Addendum 4 to Final Amended Sampling and Analysis Plan (Field Sampling Plan and Quality Assurance Project Plan) for Basewide Groundwater Monitoring Program, Hunters Point Naval Shipyard, San Francisco, California." June 5.

CE2-Kleinfelder Joint Venture, 2012d. "Semiannual Groundwater Monitoring Report (October 2011 – June 2012), Hunters Point Naval Shipyard, San Francisco, California." October.

_____, 2013a. "Semiannual Groundwater Monitoring Report (July – December 2012), Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2013b. "Final Technical Memorandum for Parcel G CERCLA Tank Closure Sampling, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2013c. "Semiannual Groundwater Monitoring Report (January – June 2013), Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2014a. "Final Addendum 5 to Final Amended Sampling and Analysis Plan (Field Sampling Plan and Quality Assurance Project Plan) for Basewide Groundwater Monitoring Program, Hunters Point Naval Shipyard, San Francisco, California." February.

_____, 2014b. "Semiannual Groundwater Monitoring Report (July – December 2013), Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2014c. "Semiannual Groundwater Monitoring Report (July – December 2013), Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2015a. "Semiannual Groundwater Monitoring Report (July – December 2014), Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2015b. "Semiannual Groundwater Monitoring Report (January – June 2015), Hunters Point Naval Shipyard, San Francisco, California." October.

_____, 2016a. "Semiannual Groundwater Monitoring Report, July – December 2015, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2016b. "Semiannual Groundwater Monitoring Report, July – December 2015, Hunters Point Naval Shipyard, San Francisco, California." December.

CH2M Hill Kleinfelder Joint Venture (KCH), 2012. "Final Remedial Design and Design Basis Report for Parcel C, Hunters Point Naval Shipyard, San Francisco, California." October 5.

_____, 2015a. "Final Sampling and Analysis Plan (Field Sampling Plan and Quality Assurance Project Plan), Activated Carbon Amendments Pilot Study Monitoring at Parcel F, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2015b. "Final Work Plan for the Demonstration of Activated Carbon Amendments, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2016a. "Final Addendum to the Feasibility Study Report for Parcel F, Hunters Point Naval Shipyard, San Francisco, California." January.

CH2M Hill Kleinfelder Joint Venture (KCH), 2016b. "Technical Memorandum, Demonstration of Activated Carbon Amendments – Summary of Field Activities Up to the 8-Month Post-Carbon Amendment Placement Monitoring Event, Hunters Point Naval Shipyard, San Francisco, California." December 1.

_____, 2016c. "Demonstration of Activated Carbon Amendments – Summary of Field Activities, Hunters Point Naval Shipyard, San Francisco, California." August 10.

_____, 2017a. "Final Addendum to the Feasibility Study Report, Parcel F, Hunters Point Naval Shipyard, San Francisco, California." January.

_____, 2017b. "Technical Memorandum, Demonstration of Activated Carbon Amendments – Summary of Field Activities Up to the 14-Month Post Carbon Amendment Placement Monitoring Event, Hunters Point Naval Shipyard, San Francisco, California." June.

ChaduxTt, 2007. "Final Parcel B Technical Memorandum in Support of a Record of Decision Amendment, Hunters Point Shipyard, San Francisco, California." December 12.

_____, 2008. "Final Construction Summary Report for Parcel B, Hunters Point Shipyard, San Francisco, California." July 25.

_____, 2009a. "Shoreline Protection Technical Memorandum, Installation Restoration Site 7, Parcel B, Hunters Point Shipyard, San Francisco, California." April 3.

_____, 2009b. "Draft Finding of Suitability to Lease (FOSL), Parcels B and G, Hunters Point Shipyard, San Francisco, California." December 21.

_____, 2010a. "Final Remedial Design Package, Installation Restoration Sites 7 and 18, Parcel B, Hunters Point Shipyard, San Francisco, California." January 8.

_____, 2010b. "Final Memorandum: Approach for Developing Soil Gas Action Levels for Vapor Intrusion Exposure at Hunters Point Shipyard, Hunters Point Shipyard, San Francisco, California." April 30.

_____, 2010c. "Final Remedial Design Package, Parcel G, Hunters Point Shipyard, San Francisco, California." October 4.

_____, 2010d. "Final Remedial Design Package, Parcel B (Excluding Installation Restoration Sites 7 and 18), Hunters Point Shipyard, San Francisco, California." December 10.

_____, 2010e. "Final Remedial Design Package, Parcels UC-1 and UC-2, Hunters Point Shipyard, San Francisco, California." December 22.

_____, 2011a. "Revised Final Land Use Control Remedial Design, Parcel G, Hunters Point Shipyard, San Francisco, California." January 11.

_____, 2011b. Revised "Final Remedial Design Package, Parcel G, Hunters Point Shipyard, San Francisco, California." January 11.

ChaduxTt, 2011c. "Draft Finding of Suitability to Transfer for Parcels UC-1 and UC-2, Hunters Point Shipyard, San Francisco, California." February 11.

_____, 2011d. "Final Remedial Design Package, Parcel D-1, Hunters Point Shipyard, San Francisco, California." February 11.

_____, 2011e. "Revised Final Remedial Design Package, Parcel B (Excluding Installation Restoration Sites 7 and 18), Hunters Point Shipyard, San Francisco, California." July 5.

_____, 2011f. "Revised Final Land Use Control Remedial Design for Parcel B (Excluding Installation Restoration Sites 7 and 18), Hunters Point Shipyard, San Francisco, California." July 5.

_____, 2011g. "Revised Final Memorandum: Approach for Developing Soil Gas Action Levels for Vapor Intrusion Exposure at Hunters Point Naval Shipyard, Hunters Point Naval Shipyard, San Francisco, California." December 2.

_____, 2012a. "Final Finding of Suitability to Transfer for Parcel D-2, Hunters Point Naval Shipyard, San Francisco, California." March 27.

_____, 2012b. "Draft Finding of Suitability to Transfer for Parcel B – IR Sites 7 and 18, Hunters Point Naval Shipyard, San Francisco, California." September 14.

_____, 2012c. "Final Amendment to Revised Final Design Basis Report for Parcel B (Excluding Installation Restoration Sites 7 and 18), Hunters Point Naval Shipyard, San Francisco, California." September 28.

_____, 2013. "Final Finding of Suitability to Transfer for Parcel B – IR Sites 7 and 18, Hunters Point Naval Shipyard, San Francisco, California." February 4.

Cho, Y.M., D.W. Smithenry, U. Ghosh, A.J. Kennedy, R.N. Milward, T.S. Bridges, and R.G. Luthy, 2007. "Field Methods for Amending Marine Sediment with Activated Carbon and Assessing Treatment Effectiveness." *Marine Environmental Research.* Volume 64, Issue 5. Pages 541–555. December.

CKY Inc., 2011a. "Landfill Gas Monitoring Report for April–June 2011, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." August 10.

_____, 2011b. "Landfill Gas Monitoring Report for July–September 2011, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." November 8.

_____, 2012a. "Landfill Gas Monitoring Report for October–December 2011, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." January 20.

_____, 2012b. "Landfill Gas Monitoring Report for January–March 2012, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." April 25.

CKY Inc., 2012c. "Landfill Gas Monitoring Report for April–June 2012, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." July 17.

_____, 2012d. "Annual Landfill Cap Operation and Maintenance Report for 2012–2013, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." July 24.

_____, 2013a. "Landfill Gas Monitoring Report for October–December 2012, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." January 21.

_____, 2013b. "Landfill Gas Monitoring Report for January–March 2013, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." April 26.

_____, 2013c. "Landfill Gas Monitoring Report for April–June 2013, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." July 18.

_____, 2013d. "Landfill Gas Monitoring Report for July–September 2013, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." October 11.

_____, 2014a. "Landfill Gas Monitoring Report for October–December 2013, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." January 21.

_____, 2014b. "Landfill Gas Monitoring Report for January–March 2014, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." April 3.

_____, 2014c. "Landfill Gas Monitoring Report for April–June 2014, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." July 11.

_____, 2014d. "Annual Landfill Cap Operation and Maintenance Report for 2013–2014, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." July 29.

_____, 2014e. "Landfill Gas Monitoring Report for July–September 2014, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." October 16.

_____, 2014f. "Monthly Landfill Gas Monitoring Letter Report for November 2014, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." November 24.

_____, 2015a. "Monthly Landfill Gas Monitoring Letter Report for January 2015, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." January 23.

CKY Inc., 2015b. "Landfill Gas Monitoring Report for October–December 2014, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." February 4.

_____, 2015c. "Landfill Gas Monitoring Report for January–March 2015, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." April 17.

_____, 2015d. "Monthly Landfill Gas Monitoring Letter Report for April 2015, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." April 23.

_____, 2015e. "Monthly Landfill Gas Monitoring Letter Report for May 2015, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." May 26.

_____, 2015f. "Landfill Gas Monitoring Report for April–June 2015, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." July 10.

_____, 2015g. "Monthly Landfill Gas Monitoring Letter Report for July 2015, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." July 29.

_____, 2015i. "Annual Landfill Cap Operation and Maintenance Report for 2014–2015, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." July 29.

_____, 2015j. "Landfill Gas Monitoring Report for July–September 2015, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." October 16.

_____, 2016a. "Landfill Gas Monitoring Report for October–December 2015, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." January 15.

_____, 2016b. "Monthly Landfill Gas Monitoring Letter Report for August 2016, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." January 18.

_____, 2016c. "Monthly Landfill Gas Monitoring Letter Report for January 2016, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." January 18.

_____, 2016d. "Monthly Landfill Gas Monitoring Letter Report for February 2016, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." February 25.

CKY Inc., 2016e. "Landfill Gas Monitoring Report for January–March 2016, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." April 12.

_____, 2016f. "Monthly Landfill Gas Monitoring Letter Report for April 2016, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." April 13.

_____, 2016g. "Monthly Landfill Gas Monitoring Letter Report for May 2016, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." May 20.

_____, 2016h. "Annual Landfill Cap Operation and Maintenance Report for 2015–2016, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." July 20.

_____, 2016i. "Landfill Gas Monitoring Report for April–June 2016, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." July 20.

_____, 2016j. "Monthly Landfill Gas Monitoring Letter Report for August 2016, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." July 20.

_____, 2016k. "Landfill Gas Monitoring Report for July–September 2016, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." October 31.

_____, 2016l. "Monthly Landfill Gas Monitoring Letter Report for November 2016, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." November 28.

_____, 2017a. "Monthly Landfill Gas Monitoring Letter Report for January 2017, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." January 18.

_____, 2017b. "Monthly Landfill Gas Monitoring Letter Report for February 2017, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." February 16.

_____, 2017c. "Landfill Gas Monitoring Report for January–March 2017, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." April 17.

_____, 2017d. "Monthly Landfill Gas Monitoring Letter Report for April 2017, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." May 1.

_____, 2017e. "Monthly Landfill Gas Monitoring Letter Report for May 2017, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." May 19.

CKY Inc., 2017f. "Landfill Gas Monitoring Report for April–June 2017, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." July 17.

_____, 2017g. "Annual Landfill Cap Operation and Maintenance Report for 2016–2017, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." July 20.

_____, 2017h. "Landfill Gas Monitoring Report for July–September 2017, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." October 9.

_____, 2017i. "Monthly Landfill Gas Monitoring Letter Report for October 2017, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." October 26.

_____, 2018a. "Landfill Gas Monitoring Report for October-December 2017, Post-Removal Action, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." January 11.

_____, 2018b. "Monthly Landfill Gas Monitoring Letter Report for January 2018, Post-Removal Action, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." January 15.

Construction Engineering Services, LLC, 2015. "Final Work Plan for Pre-Design Investigation at Parcel E, Installation Restoration Sites 02, 03, and 12, Hunters Point Naval Shipyard, San Francisco, California." January.

_____, 2018a. "Final Remedial Design Package, Parcel E, Hunters Point Naval Shipyard, San Francisco, California." May 21.

_____, 2018b. "Draft Land Use Control Remedial Design, Parcel E, Hunters Point Naval Shipyard, San Francisco, California." May 31.

Department of the Navy (Navy), 1990. "Federal Facility Agreement for Naval Station Treasure Island—Hunters Point Annex." September.

_____, 1995. "Hunters Point Annex, Parcel A, Record of Decision." Engineering Field Activity West, Naval Facilities Engineering Command. November 16.

_____, 1997. "Hunters Point Shipyard, Parcel B, Final Record of Decision." Engineering Field Activity West, Naval Facilities Engineering Command. October 7.

_____, 1998. "Explanation of Significant Differences, Parcel B, Hunters Point Shipyard Site, San Francisco, California." August 24.

_____, 2000. "Final Explanation of Significant Differences, Parcel B, Hunters Point Shipyard, San Francisco, California." May 4.

Navy, 2006. "Final Basewide Radiological Removal Action, Action Memorandum – Revision 2006, Hunters Point Shipyard, San Francisco, California." April 21.

_____, 2008a. "Final Action Memorandum, Time-Critical Removal Action for the Methane Source Area at IR-07, Parcel B, Hunters Point Shipyard, San Francisco, California." May 16.

_____, 2008b. "Final Action Memorandum, Time-Critical Removal Action for the Mercury Source at IR-26, Parcel B, Hunters Point Shipyard, San Francisco, California." May 29.

_____, 2009a. "Final Amended Parcel B Record of Decision, Hunters Point Shipyard, San Francisco, California." January 14.

_____, 2009b. "Final Record of Decision for Parcel G, Hunters Point Shipyard, San Francisco, California." February 18.

_____, 2009c. "Final Record of Decision for Parcels D-1 and UC-1, Hunters Point Shipyard, San Francisco, California." July 24.

_____, 2009d. "Final Record of Decision for Parcel UC-2, Hunters Point Shipyard, San Francisco, California." December 17.

_____, 2010a. "Final Record of Decision for No Further Action at Parcel D-2, Hunters Point Shipyard, San Francisco, California." August 9.

_____, 2010b. "Final Record of Decision for Parcel C, Hunters Point Shipyard, San Francisco, California." September 30.

_____, 2011a. "Final Community Involvement Plan, Hunters Point Shipyard, San Francisco, California." May.

_____, 2011b. "Navy/Marine Corps Policy for Conducting Comprehensive Environmental Response, Compensation, and Liability Act (CERCLA) Five-Year Reviews." June 7. Available Online at: <https://www.navfac.navy.mil/navfac_worldwide/specialty_centers/exwc/products_and_services/ev/erb/5-yr-rvw.html>.

_____, 2012a. "Final Action Memorandum, Removal of Underground Storage Tank (UST) 113A, IR Site 42, Parcel B, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2012b. "Final Record of Decision for Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." November.

_____, 2013a. "Proposed Plan, Parcels E and UC-3, Hunters Point Naval Shipyard, San Francisco, California." February.

_____, 2013b. "Draft Record of Decision for Parcel E, Hunters Point Naval Shipyard, San Francisco, California." June.

Navy, 2013c. "Draft Record of Decision for Parcel UC-3, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2013d. Memorandum regarding "Groundwater Analytical Results Exceeding Remediation Goals or Trigger Levels, Third Quarter 2013 (3Q2013), Hunters Point Naval Shipyard, San Francisco, California." From Anthony Konzen, BRAC PMO Project Manager. To Base Realignment and Closure Cleanup Team. October 31.

_____, 2013e. "Final Record of Decision for Parcel E, Hunters Point Naval Shipyard, San Francisco, California." December.

_____, 2014a. "Final Record of Decision for Parcel UC-3, Hunters Point Naval Shipyard, San Francisco, California." January.

_____, 2014b. "Final Explanation of Significant Differences to the Final Record of Decision for Parcel C, Hunters Point Shipyard, San Francisco, California." October.

_____, 2015a. "Final Federal Facility Agreement Schedule for Fiscal Year 2015, Hunters Point Naval Shipyard, San Francisco, California." February.

_____, 2015b. Letter regarding "CERCLA Operation and Maintenance Plan Letter Amendment, Hunters Point Naval Shipyard Parcel G and Parcels UC-1/UC-2." From Alan K. Lee, Base Closure Manager. To Lily Lee, EPA; Nina Bacey, DTSC; and Tina Lowe, Water Board. March 18.

_____, 2016. "Final Federal Facilities Agreement Schedule, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2017a. "Final Federal Facilities Agreement Schedule, Hunters Point Naval Shipyard, San Francisco, California." March 15.

_____, 2017b. "Draft Radiological Communication Plan, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2017. "Explanation of Significant Differences to the Final Record of Decision for Parcel G, Hunters Point Naval Shipyard, San Francisco, California." April 18.

_____, 2018. "Hunters Point Naval Shipyard – Parcel F Proposed Plan for Offshore Sediment Cleanup, San Francisco, California." April.

Department of Toxic Substances Control (DTSC), 2011. "Radiological Free Release for Parcels UC-1 and UC-2, Hunters Point Shipyard, San Francisco, California." September 14.

_____, 2012a. "DTSC Concurrence with the Final Removal Action Completion Report, Revision 2, Parcel D-2, Hunters Point Shipyard, San Francisco, California." January 13.

_____, 2012b. "Radiological Unrestricted Release Recommendation for Parcel G, Hunters Point Shipyard, San Francisco, California." March 27.

DTSC, 2012c. "Radiological Unrestricted Release Recommendation for Parcel B—Except IR Site 7 and 18, Hunters Point Shipyard, San Francisco, California." July 31.

_____, 2012d. "DTSC Concurrence with Final Remedial Action Completion Report for Installation Restoration Sites 07 and 18, Hunters Point Naval Shipyard, San Francisco, California." October 16.

_____, 2012e. "Radiological Unrestricted Release Recommendation for Parcel Utility Corridor 3, Hunters Point Shipyard, San Francisco, California." October 31.

_____, 2018. "Department of Toxic Substances Control Screening Levels (DTSC-SL), Human Health Risk Assessment (HHRA) Note; HERO HHRA Note Number: 3, DTSC-Modified Screening Levels (DTSC-SLs)." January. Available online at: <http://www.dtsc.ca.gov/AssessingRisk/humanrisk2.cfm>

Eagle Environmental Construction (EEC), 2006. "Final 2005 – 2006 Annual Report for Storm Water Discharge Management, IR-01/21, Industrial Landfill, Parcel E-2, Hunters Point Shipyard, San Francisco, California." June 30.

EEC, 2007. "Final 2006 – 2007 Annual Report for Storm Water Discharge Management, IR-01/21, Industrial Landfill, Parcel E-2, Hunters Point Shipyard, San Francisco, California." July 31.

ECC-Insight, LLC and CDM Smith, 2017a. "Final Technical Memorandum, Optimized Remedial Alternative for Parcel F, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2017b. "Final Work Plan, Sediment Investigation and Bathymetric Survey for Parcel F, Hunters Point Naval Shipyard, San Francisco, California." November.

_____, 2017c. "Final Remedial Action Work Plan, Parcel C Remedial Units C1, C2, C4, and C5, Hunters Point Naval Shipyard, San Francisco, California." November.

Engineering/Remediation Resources Group, Inc. (ERRG), 2011. "Final Remedial Action Completion Report for Soil Hotspot Locations at Parcels B, D-1, and G and Soil Stockpiles at Parcels D-1 and G, Hunters Point Naval Shipyard, San Francisco, California." October 7.

_____, 2012a. "Final Remedial Action Completion Report for Installation Restoration Sites 07 and 18 at Parcel B, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2012b. "Final Feasibility Study Report for Parcel E, Hunters Point Shipyard, San Francisco, California." August 31.

_____, 2012c. "Annual Operation and Maintenance Summary Report for Installation Restoration Sites 07 and 18 in Parcel B, Hunters Point Naval Shipyard, San Francisco, California." October 4.

_____, 2012d. "Final Operation and Maintenance Plan for Installation Restoration Sites 07 and 18 in Parcel B, Hunters Point Naval Shipyard, San Francisco, California." October.

ERRG, 2012e. "Final Remedial Action Work Plan for Parcel B (Excluding Installation Restoration Sites 07 and 18), Hunters Point Naval Shipyard, San Francisco, California." November.

_____, 2012f. "Final Remedial Action Work Plan for Parcel B (Excluding Installation Restoration Sites 07 and 18), Hunters Point Naval Shipyard, San Francisco, California." December 13.

_____, "Final Technical Memorandum for the Geotechnical Investigation at Parcel E-2 (Installation Restoration Site 01/21), Hunters Point Naval Shipyard, San Francisco, California." January.

_____, 2013b. "First Quarterly Operation and Maintenance Inspection Report for Parcels UC-1 and UC-2, Hunters Point Naval Shipyard, San Francisco, California." January 10.

_____, 2013c. "Final Remedial Action Completion Report for Parcels UC-1 and UC-2, Hunters Point Naval Shipyard, San Francisco, California." February 25.

_____, 2013d. "Final Operation and Maintenance Plan, Parcels UC-1 and UC-2, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2013e. "Second Quarterly Operation and Maintenance Inspection Report for Parcels UC-1 and UC-2, Hunters Point Naval Shipyard, San Francisco, California." April 3.

_____, 2013f. "Draft Remedial Design Package, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." June 28.

_____, 2013g. "Final Parcel UC-1 Soil Gas Investigation Addendum to Final Work Plan for Soil Gas Investigation in Support of Vapor Intrusion Assessment, Parcels B, D-1, G, and UC-2, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2013h. "Annual Operation and Maintenance Summary Report for Installation Restoration Sites 07 and 18 in Parcel B, Hunters Point Naval Shipyard, San Francisco, California." September 25.

_____, 2013i. "Final Addendum 1 to the Final Remedial Action Work Plan for Parcel B (Excluding Installation Restoration Sites 07 and 18), Hunters Point Naval Shipyard, San Francisco, California." December.

_____, 2014a. "Annual Operation and Maintenance Summary Report for Parcels UC-1 and UC-2, Hunters Point Naval Shipyard, San Francisco, California." January.

_____, 2014b. "Year 1, First Quarterly Inspection Record (Preliminary) – Parcel B Excluding IR-07/18, Hunters Point Shipyard, San Francisco, CA." March.

_____, 2014c. "Final Addendum 1 to the Remedial Action Completion Report for Soil Hotspot Locations at Parcel B, D-1, and G and Soil Stockpiles at Parcel D-1 and G, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2014d. "Year 1, Second Quarterly Inspection Record (Preliminary) – Parcel B Excluding IR-07/18, Hunters Point Shipyard, San Francisco, CA." May.

ERRG, 2014e. "Year 1, Third Quarterly Inspection Record (Preliminary) – Parcel B Excluding IR-07/18, Hunters Point Shipyard, San Francisco, CA." July.

_____, 2014f. "Final Remedial Design Package, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." August.

_____, 2014g. "Final Technical Memorandum, Soil Vapor Investigation in Support of Vapor Intrusion Assessment at Parcel UC-1, Hunters Point Naval Shipyard, San Francisco, California." August.

_____, 2014h. "Final Addendum to the Remedial Action Completion Report for Parcels UC-1 and UC-2, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2014i. "Annual Operation and Maintenance Summary Report for Installation Restoration Sites 07 and 18 in Parcel B, Hunters Point Naval Shipyard, San Francisco, California. " September.

_____, 2014j. "Year 1, Fourth Quarterly Inspection Record (Preliminary) – Parcel B Excluding IR-07/18, Hunters Point Shipyard, San Francisco, CA." November.

_____, 2015a. "Final Technical Memorandum, Petroleum Hydrocarbons Data Gaps Investigation at the Combined Site in Parcel B, Hunters Point Naval Shipyard, San Francisco, California." February.

_____, 2015b. "Final Addendum 4 to the Final Remedial Action Work Plan for Parcel B (Excluding Installation Restoration Sites 07 and 18), Hunters Point Naval Shipyard, San Francisco, California." February.

_____, 2015c. "General Inspection Checklist, Hunters Point Naval Shipyard, Parcels UC-1 and UC-2." April.

_____, 2015d. "Annual Operation and Maintenance Summary Report for Parcels UC-1 and UC-2, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2015e. "Inspection Record (Preliminary) – Parcels B-1 and B-2, Hunters Point Shipyard, San Francisco, California." April 16.

_____, 2015f. "General Inspection Checklist, Hunters Point Naval Shipyard, Installation Restoration Sites 07 and 18 at Parcel B." May.

_____, 2015g. "Year 2, First Semiannual Inspection Record (Preliminary) – Parcels B-1 and B-2, Hunters Point Shipyard, San Francisco, CA." May.

_____, 2015h. "General Inspection Checklist, Hunters Point Naval Shipyard, Installation Restoration, Sites 07 and 18 at Parcel B." September 30.

_____, 2015i. "Inspection Record, Parcels B-1 and B-2, Hunters Point Naval Shipyard, San Francisco, California." October.

_____, 2015j. "Year 2, Second Semiannual Inspection Record (Preliminary) – Parcels B-1 and B-2, Hunters Point Shipyard, San Francisco, CA." October.

ERRG, 2015k. "Annual Operation and Maintenance Summary Report for Parcels UC-1 and UC-2, Hunters Point Naval Shipyard, San Francisco, California." October.

_____, 2015l. "Final Addendum 5 to the Final Remedial Action Work Plan for Parcel B (Excluding Installation Restoration Sites 07 and 18), Hunters Point Naval Shipyard, San Francisco, California." November.

_____, 2016. "Final Operation and Maintenance Plan for Parcel B-1, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2017. "Final Remedial Action Completion Report for the Durable Covers Remedy in Parcel B-1, Hunters Point Naval Shipyard, San Francisco, California." January.

ERRG and Radiological Survey and Remedial Services LLC, 2012. "Final Radiological Addendum to the Feasibility Study Report for Parcel E, Hunters Point Shipyard, San Francisco, California." August 31.

ERRG and Shaw Environmental, Inc., 2011. "Final Remedial Investigation/Feasibility Study Report for Parcel E-2, Hunters Point Shipyard, San Francisco, California." May 5.

ERRG and URS Corporation, 2004. "Final Cost and Performance Report, Zero-Valent Iron Injection Treatability Study, Building 123, Parcel B, Hunters Point Shipyard, San Francisco, California." June 25.

Environmental Resources Management-West, Inc. (ERM-West), 1989. "Summary Report, Interim Cleanup of Polychlorinated Biphenyl Contaminated Soils near Former Building 503, Naval Station, Treasure Island, Hunters Point Annex, San Francisco, California." November 15.

ERS Joint Venture (ERS-JV), 2012. "Final Removal Action Completion Summary Report, Pier Radiological Surveys and Removal, Hunters Point Naval Shipyard, San Francisco, California." August 2.

Foster Wheeler Environmental Corporation, 2003. "Final Post-Construction Report, Industrial Process Equipment Survey, Sampling, Decontamination, and Waste Consolidation, Parcel D, Hunters Point Shipyard, San Francisco, California." Revision 0. October 22.

Geosyntec Consultants, 2015. "Risk Management Plan, Hunters Point Naval Shipyard, Parcels UC-1 and UC-2, San Francisco, California." Revision 0. March.

_____, 2016a. "Risk Management Plan, Annual Report Form for Parcel UC-1 Hunters Point Shipyard, September 30, 2016, San Francisco, California." September 30.

_____, 2016b. "Risk Management Plan, Annual Report Form for UC-2, Former Hunters Point Shipyard, 30 September 2016, San Francisco, California." September 30.

Gilbane Federal (Gilbane), 2014. "Final Pre-Excavation Characterization Technical Memorandum, Hot Spot Delineation and Excavation Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." November 7.

Gilbane, 2015a. “”Final Pre-Excavation Characterization Technical Memorandum – T5-EX-1, Hot Spot Delineation and Excavation Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California.” July 31.

_____, 2015b. “Final Work Plan Addendum, Nearshore Slurry Wall Installation, Hot Spot Delineation and Excavation Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California.” August 28.

_____, 2016a. “Final Survey Unit Project Reports, Abstract, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Naval Shipyard, San Francisco, California.” January.

_____, 2016b. “Final Survey Unit Project Report – Zone A, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Shipyard, San Francisco, California.” January.

_____, 2016c. “Final Survey Unit Project Report – Zone F, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Shipyard, San Francisco, California.” January.

_____, 2016d. “Final Survey Unit Project Report – Zone G, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Shipyard, San Francisco, California.” January.

_____, 2016e. “Final Survey Unit Project Report – Zone H, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Shipyard, San Francisco, California.” January.

_____, 2016f. “Final Survey Unit Project Report – Zone I, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Shipyard, San Francisco, California.” January.

_____, 2016g. “Final Survey Unit Project Report – Zone J, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Shipyard, San Francisco, California.” January.

_____, 2016h. “Final Survey Unit Project Report – Zone K, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Shipyard, San Francisco, California.” January.

_____, 2016i. “Final Survey Unit Project Report – Zone L, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Shipyard, San Francisco, California.” January.

_____, 2016j. “Final Survey Unit Project Report – Zone M, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Shipyard, San Francisco, California.” January.

_____, 2016k. “Final Survey Unit Project Report – Zone N, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Shipyard, San Francisco, California.” January.

_____, 2016l. “Final Survey Unit Project Report – Zone O, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Shipyard, San Francisco, California.” January.

_____, 2016m. “Final Survey Unit Project Report – Zone P, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Shipyard, San Francisco, California.” January.

Gilbane, 2016n. "Final Survey Unit Project Report – Zone Q, Parcel D-1 Phase II Sanitary Sewer and Storm Drain Removal, Hunters Point Shipyard, San Francisco, California." January.

_____, 2016o. "Final Work Plan, Remedial Action, Parcel UC-3, Hunters Point Naval Shipyard, San Francisco, California." August 29.

_____, 2017a. "Air Monitoring Summary Report, Hot Spot Delineation and Excavation Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." February.

_____, 2017b. "Air Monitoring Summary Report, Hot Spot Delineation and Excavation Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." April 24.

_____, 2017c. "Air Monitoring Summary Report, Hot Spot Delineation and Excavation Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." April 25.

_____, 2017d. "Air Monitoring Summary Report, Hot Spot Delineation and Excavation Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2017e. "Air Monitoring Summary Report, Hot Spot Delineation and Excavation Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." June 1.

_____, 2017f. "Air Monitoring Summary Report, Hot Spot Delineation and Excavation Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." August.

_____, 2017g. "Air Monitoring Summary Report, Hot Spot Delineation and Excavation Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." August 3.

_____, 2017h. "Air Monitoring Summary Report, Hot Spot Delineation and Excavation Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2017i. "Air Monitoring Summary Report, Hot Spot Delineation and Excavation, Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." October 3.

_____2017j. "Draft Remedial Action Closure Report, Remedial Action, Parcel UC-3, Hunters Point Naval Shipyard, San Francisco, California." December.

_____2018a. "Draft Final Remedial Action Completion Report, Radiological Remediation and Support, Parcel D-1, Phase II, Hunters Point Naval Shipyard, San Francisco, California." February.

_____2018b. "Draft Final, Final Status Survey: Ship Berths 14, 21, 22, & 29, Hunters Point Naval Shipyard, San Francisco, California." February.

_____2018c. "Draft Final, Final Status Survey of the Former Naval Radiological Defense Laboratory Site, Hunters Point Naval Shipyard, San Francisco, California." February.

Gilbane, 2018d. "Final Remedial Action Completion Report, Hot Spot Delineation and Excavation and Nearshore Slurry Wall Installation, Remedial Action, Parcel E-2, Hunters Point Shipyard, San Francisco, California." June 22.

Griggs, G., J. Arvai, D. Cayan, R. DeConto, J. Fox, H.A. Fricker, R.E. Kopp, C. Tebaldi, and E.A. Whiteman (California Ocean Protection Council Science Advisory Team Working Group). "Rising Seas in California: An Update on Sea-Level Rise Science." California Ocean Science Trust. April 2017. Available Online at: <http://www.opc.ca.gov/webmaster/ftp/pdf/docs/rising-seas-in-california-an-update-on-sea-level-rise-science.pdf>.

Harding Lawson Associates, 1989. "Final Draft Solid Waste Air Quality Assessment Test, Hunters Point Annex, San Francisco, California." August 4.

_____, 1991. "Preliminary Draft Ecological Risk Assessment Data Summary Report, Naval Station Treasure Island, Hunters Point Annex, San Francisco, California." November.

Innovative Technical Solutions, Inc. (ITSI), 2005. "Final Zero-Valent Iron Injection Treatability Study Report, Building 272, Parcel C, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2006. "Annual Landfill Cap Operations and Maintenance Report for 2005–2006, Parcel E-2, Industrial Landfill, Hunters Point Shipyard, San Francisco, California." July 17.

_____, 2007. "Annual Landfill Cap Operations and Maintenance Report for 2006–2007, Parcel E-2, Industrial Landfill, Hunters Point Shipyard, San Francisco, California." May 31.

_____, 2008. "Annual Landfill Cap Operations and Maintenance Report for 2007–2008, Parcel E-2, Industrial Landfill, Hunters Point Shipyard, San Francisco, California." August 29.

_____, 2010a. "Annual Landfill Cap Operations and Maintenance Report for 2008–2009, Parcel E-2, Industrial Landfill, Hunters Point Shipyard, San Francisco, California." August 31.

_____, 2010b. "Annual Landfill Cap Operations and Maintenance Report for 2009–2010, Parcel E-2, Industrial Landfill, Hunters Point Shipyard, San Francisco, California." August 31.

_____, 2010c. "Final Post-Excavation Soil Gas Monitoring Report for 2009–2010, Installation Restoration Site IR-07, Hunters Point Shipyard, San Francisco, California." October 8.

_____, 2011a. "Final Petroleum Hydrocarbon Site Closure Report, Parcels D-1, D-2, and G (Former Parcel D), Hunters Point Shipyard, San Francisco, California." January.

_____, 2011b. "Work Plan, Removal of Underground Storage Tank (UST) 113A, IR Site 42, Parcel B, Hunters Point Shipyard, San Francisco, California." January.

_____, 2011c. "Final Petroleum Hydrocarbon Site Closeout Report, Parcel B, Hunters Point Shipyard, San Francisco, California." Volumes 1 and 2. August.

ITSI, 2011d. "Final Petroleum Hydrocarbon Site Closure Report, Parcels D-1, D-2, and G (Former Parcel D), Site-Specific Attachment for AOC 70-A, Hunters Point Shipyard, San Francisco, California." August.

_____, 2011e. "Final Annual Landfill Cap Operation and Maintenance Report for 2010–2011, Parcel E-2, Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." August 17.

_____, 2011f. "Draft Post Construction Summary Report, Petroleum Hydrocarbon Corrective Action, Parcels B, D-1, and G, Hunters Point Naval Shipyard, San Francisco, California." October.

_____, 2012a. "Final Petroleum Hydrocarbon Corrective Action Quarterly Monitoring Report, Second Quarter 2011, Parcel B, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2012b. "Draft Petroleum Hydrocarbon Corrective Action Quarterly Monitoring Report, Fourth Quarter 2011, Parcel B, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2012c. "Final Petroleum Hydrocarbon Corrective Action Quarterly Monitoring Report, Third Quarter 2011, Combined Site Parcel B, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2012d. "Final Petroleum Hydrocarbon Site Closeout Report, Parcel B, Site-Specific Attachment for AOC 46-D, Revision 1, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2013. "Final Site Characterization and Bench-Scale Treatability Study Report for Installation Restoration Site 03, Parcel E, Hunters Point Naval Shipyard, San Francisco, California." February.

ITSI and Tetra Tech EM Inc., 2004. "Final Interim Landfill Gas Monitoring and Control Plan, Parcel E Industrial Landfill, Hunters Point Shipyard, San Francisco, California." August 13.

ITSI Gilbane Company, 2013a. "Final Work Plan, Landfill Gas Survey at Parcel E-2, Parcel E-2 Industrial Landfill, Hunters Point Naval Shipyard, San Francisco, California." May 13.

_____, 2013b. "Final Basewide Radiological Management Plan, Hunters Point Naval Shipyard, San Francisco, California." July.

_____, 2013c. "Final Execution Plan, Radiological Remediation and Support, Parcel D-1 Phase II, Hunters Point Naval Shipyard, San Francisco, California." July.

_____, 2013d. "Final Technical Memorandum for the Radiological Data Gap Investigation Phase 2B, Hunters Point Naval Shipyard, San Francisco, California." September 1.

_____, 2014a. "Final Work Plan, Hot Spot Delineation and Excavation Remedial Action, Parcel E-2. Hunters Point Naval Shipyard, San Francisco, California." March 28.

_____, 2014b. "Final Landfill Gas Evaluation Report, Landfill Gas Survey at Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." May 30.

ITSI Gilbane Company and Science Applications International Corporation (SAIC), 2013. "Final Technical Memorandum for the Radiological Data Gap Investigation Phase 2b at Parcel F, Hunters Point Naval Shipyard, San Francisco, California." September.

Innovex-ERRG Joint Venture (IEJV), 2017. "Operation and Monitoring Status Update for IR-10 SVE System, IR-10 Carveout, Parcel B-1, Hunters Point Naval Shipyard, San Francisco, California." December.

_____, 2018a. "Annual Operation and Maintenance Summary Report for Parcels B-1, B-2, C, and G and Installation Restoration Sites 07 and 18, Hunters Point Naval Shipyard, San Francisco, California." January 25.

_____, 2018b. "Final Remedial Action Completion Report for the Durable Covers Remedy in Parcel B-2, Hunters Point Naval Shipyard, San Francisco, California." April 6.

_____, 2018c. "Draft Operation and Maintenance Plan for Parcel B-2, Hunters Point Naval Shipyard, San Francisco, California." April.

Insight Environmental, Engineering, and Construction, Inc. (Insight), 2009. "Final Hunters Point Shipyard, Parcel B, IR-26 Time Critical Removal Action, Removal Action Closeout Report." January.

IT Corporation, 1999a. "Project Completion Report, Exploratory Excavations, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 1999b. "Final Post-Construction Report, Site IR-03 Waste Oil Reclamation Ponds Removal Action, Sheet Pile Containment Barrier, Cap and Soil Cover, Hunters Point Naval Shipyard, San Francisco, California." July.

_____, 1999c. "Final Post-Construction Report, Site IR 1/21 Industrial Landfill, Groundwater Extraction System/Containment Barrier, Hunters Point Naval Shipyard, San Francisco, California." July.

_____, 2000. "Post-Construction Report, Hunters Point Shipyard, San Francisco, California." March 1.

_____, 2001. "Phase II Soil Vapor Extraction Treatability Study Report, Building 134, IR-25, Parcel C, Hunters Point Shipyard, San Francisco, California." December 31.

_____, 2002a. "Draft Phase II Soil Vapor Extraction Treatability Study Report, Building 123, IR-10, Parcel B, Hunters Point Shipyard, San Francisco, California." February 14.

_____, 2002b. "Draft Phase II Soil Vapor Extraction Treatability Study Report, Building 272, IR-28, Parcel C, Hunters Point Shipyard, San Francisco, California." February 28.

_____, 2002c. "Draft Phase II Soil Vapor Extraction Treatability Study Report, Building 211/253, IR-28, Parcel C, Hunters Pont Shipyard, San Francisco. March 21.

IT Corporation, 2002d. "Draft Phase II Soil Vapor Extraction Treatability Study Report, Building 251, IR-28, Parcel C, Hunters Point Shipyard, San Francisco, California." April 29.

_____, 2002e. "Draft Phase II Soil Vapor Extraction Treatability Study Report, Building 231, IR-28, Parcel C, Hunters Point Shipyard, San Francisco, California." May 23.

_____, 2002f. "Draft Phase II Soil Vapor Extraction Treatability Study Report, Building 406, IR-36, Parcel E, Hunters Point Shipyard, San Francisco, California." June.

Jonas and Associates, Inc. and CDM Federal Programs Corporation, 2008. "Final Second Five-Year Review of Remedial Actions, Hunters Point Shipyard, San Francisco, California." November 11.

KEMRON Environmental Services, Inc., 2018. "Draft Remedial Action Work Plan, Remedial Action, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." February 16.

KMEA MACTEC Joint Venture, 2017. "Draft Final Work Plan for Parcel B-2, Installation Restoration Site 26 Groundwater Treatment at Former Hunters Point Naval Shipyard, San Francisco, California." June.

Kopp R.E., R.M. Horton, C.M. Little, J.X. Mitrovica, M. Oppenheimer, D.J. Rasmussen, B.H. Strauss, and C. Tebaldi, 2014. "Probabilistic 21st and 22nd Century Sea-Level Projections at a Global Network of Tide-Gauge Sites." *Earth's Future*. No. 2. Pages 383–406. June 13. Available Online at: <https://agupubs.onlinelibrary.wiley.com/doi/10.1002/2014EF000239>.

Langan, 2016. "Feasibility Assessment for Evaluating Areas with Residential Land Use Restrictions, Parcel G, Hunters Point Naval Shipyard, San Francisco, California." November 30.

MARRS Services, Inc. (MARRS) and MACTEC Engineering and Consulting, Inc. (MACTEC), 2008. "2007/2008 Storm Water Monitoring Report, Hunters Point Shipyard, San Francisco, California." June.

_____, 2009. "2008/2009 Storm Water Monitoring Report, Hunters Point Shipyard, San Francisco, California." June.

Morrison Knudsen Corporation and Tetra Tech EM Inc., 1999. "Final Remedial Design Documents, Remedial Action, Parcel B, Hunters Point Shipyard, San Francisco, California." August 19.

Naval Sea Systems Command (NAVSEA), 2004. "Final Historical Radiological Assessment, History of the Use of General Radioactive Materials, 1939 – 2003, Hunters Point Shipyard." October.

Oneida Total Integrated Enterprises, Inc. (OTIE), 2011. "Final In Situ Anaerobic Bioremediation Treatability Study Completion Report, Remedial Unit C1, Building 253, Hunters Point Naval Shipyard, San Francisco, California." June 8.

PRC Environmental Management, Inc. (PRC), 1992. "Naval Station Treasure Island, Hunters Point Annex, San Francisco, California, Surface Confirmation Radiation Survey, Draft Report." November.

PRC, 1994. "Phase IA Ecological Risk Assessment, Naval Station Treasure Island, Hunters Point Annex, San Francisco, California." Volumes 1 through 3. July 15.

_____, 1996a. "Phase IB Ecological Risk Assessment, Hunters Point Shipyard, San Francisco, California." Volume I, Part I: Nature and Extent of Contamination, and Part 2: Risk Characterization to Aquatic Receptors. November 15.

_____, 1996b. "Parcel B Feasibility Study, Final Report, Hunters Point Shipyard, San Francisco, California." November 26.

PRC and Harding Lawson Associates, 1993. "Draft Final Parcel A Site Inspection Report, Naval Station Treasure Island, Hunters Point Annex, San Francisco, California." October 15.

_____, 1994. "Final Site Assessment Report, Potentially Contaminated Sites, Parcels B, C, D, and E, Naval Station Treasure Island, Hunters Point Annex, San Francisco, California." April 15.

_____, 1995. "Draft Final Parcel A Remedial Investigation Report, Hunters Point Annex, San Francisco, California." September 22.

PRC and Levine-Fricke-Recon, Inc. (LFR), 1997. "Parcel D Feasibility Study, Draft Final Report, Hunters Point Shipyard, San Francisco, California." January 24.

PRC, LFR, and Uribe & Associates, 1996a. "Parcel B Remedial Investigation, Draft Final Report, Hunters Point Shipyard, San Francisco, California." June 6.

_____, 1996b. "Parcel D Remedial Investigation, Draft Final Report, Hunters Point Shipyard, San Francisco, California." October 25.

_____, 1997. "Parcel C Remedial Investigation, Draft Final Report, Hunters Point Shipyard, San Francisco, California." March 13.

Rore, Inc., 2013. "Final Technical Memorandum, Exit Strategy for Parcels, Hunters Point Naval Shipyard, San Francisco, California." November 1.

San Francisco Bay Regional Water Quality Control Board (Water Board), 2000. Letter regarding "Case Closure, UST S-812 at Hunters Point Shipyard, San Francisco, California." From Lawrence P. Kolb, Assistance Executive Officer. To Richard Powell, Commanding Officer, Engineering Field Activity West, Naval Facilities Engineering Command. January 14.

_____, 2012a. "No Further Action for Areas of Concern (AOCs) 07-F and 18-A, Parcel B, Hunters Point Naval Shipyard, San Francisco County." February 2.

_____, 2012b. "No Further Action for Areas of Concern (AOCs) 46-D, Parcel B, Hunters Point Naval Shipyard, San Francisco County." July 23.

_____, 2012c. "Concurrence with the Final Remedial Action Completion Report for Installation Restoration Sites 07 and 18, Hunters Point Naval Shipyard, San Francisco." Revisions issued October 12, 2012.

San Francisco Redevelopment Agency (SFRA), 1997. "Hunters Point Shipyard Redevelopment Plan." July 14.

_____, 2010. "Hunters Point Shipyard Redevelopment Plan." August 3 (amendment to July 14, 1997, redevelopment plan).

Sealaska Environmental Services, LLC (SES), 2010. "Final Work Plan for Soil Gas Investigation in Support of Vapor Intrusion Assessment, Parcels B, D-1, G, and UC-2, Hunters Point Shipyard, San Francisco, California." December.

_____, 2013. "Final Technical Memorandum, Soil Vapor Investigation in Support of Vapor Intrusion Assessment, Parcels B, D-1, G and UC-2, Hunters Point Naval Shipyard, San Francisco, California." March.

SES-TECH Remediation Services, Inc. (SES-TECH), 2009. "Final Removal Action Completion Report, Time-Critical Removal Action for the Methane Source Area at IR-07, Parcel B, Hunters Point Shipyard, San Francisco, California." May.

Shaw Environmental, Inc. (Shaw), 2005. "Final In Situ Sequential Anaerobic–Aerobic Bioremediation Treatability Study, Remedial Unit C5, Building 134, Installation Restoration Site 25, Hunters Point Shipyard, San Francisco, California." November 23.

_____, 2007. "Final New Preliminary Screening Criteria and Petroleum Program Strategy, Hunters Point Shipyard, San Francisco, California." December 21.

_____, 2008. "Final Petroleum Hydrocarbon Corrective Action Plan, Parcel B, Revision 2008, Hunters Point Shipyard, San Francisco, California." June 25.

_____, 2010. "Final Work Plan Addendum, Time-Critical Removal Action for the PCB Hot Spot Area at Parcel E-2, Hunters Point Shipyard, San Francisco, California." June 17.

_____, 2011. "Final Parcel E Groundwater Treatability Study, Technical Report, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2012. "Draft Work Plan, Parcel C Remedial Action, Remedial Units C1, C4, and C5, and Building 241 (Excludes C2), Hunters Point Naval Shipyard, San Francisco, California." November.

_____, 2013a. "Final Removal Action Completion Report, Time-Critical Removal Action for the Experimental Ship Shielding Range, Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." February.

_____, 2013b. "Final Status Survey Report, Building 383 Area, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013c. "Final Parcel E Groundwater Treatability Study, Technical Report Addendum, Hunters Point Naval Shipyard, San Francisco, California." March.

Shaw, 2013d. "Final, Final Status Survey Report, Former Building 313, 313A, and 322 Sites, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013e. "Final Removal Action Completion Report, Phase II, Time-Critical Removal Action for the PCB Hot Spot Area at Parcel E-2, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2013f. "Final, Final Status Survey Report, South Pier Area, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014a. "Final Radiological Removal Action Completion Report, Radiological Surveys of Buildings and Ground Surfaces, and Storm Drain and Sanitary Sewer Removal, Parcel D-1, Phase 1, Hunters Point Naval Shipyard, San Francisco, California." January.

_____, 2014b. "Final Status Survey Report, Gun Mole Pier Area, Hunters Point Naval Shipyard, San Francisco, California." January.

_____, 2015. "Final Work Plan Addendum 01, Parcel C Remedial Action, Remedial Units C1, C4, and C5, and Building 241 (Excludes C2), Hunters Point Naval Shipyard, San Francisco, California." October.

SulTech, 2007a. "Draft Parcels E and E-2 Shoreline Characterization Technical Memorandum, Hunters Point Shipyard, San Francisco, California." June 29.

_____, 2007b. "Final Revised Feasibility Study for Parcel D, Hunters Point Shipyard, San Francisco, California." November 30.

_____, 2008. "Final Feasibility Study Report for Parcel C, Hunters Point Shipyard, San Francisco, California." July 31.

Tetra Tech EC, Inc. (TtEC), 2005. "Final Removal Action Design and Implementation Work Plan, Metal Debris Reef and Metal Slag Areas, Parcels E and E-2, Revision 0, Hunters Point Shipyard, San Francisco, California." November 10.

_____, 2007a. "Final Removal Action Completion Report, PCB Hot Spot Soil Excavation Site, Parcels E and E-2, Hunters Point Shipyard, San Francisco, California." October 31.

_____, 2007b. "Final Removal Action Completion Report, Metal Debris Reef and Metal Slag Area Excavation Sites, Parcels E and E-2, Hunters Point Shipyard, San Francisco, California." November 30.

_____, 2007c. "Final Removal Action Completion Report, Installation Restoration Site 02 – Northwest and Central, Parcel E, Hunters Point Shipyard, San Francisco, California." December 12.

_____, 2008a. "Final Status Survey Results, Revision 1, Building 813. March 21.

_____, 2008b. "Final Base-Wide Radiological Work Plan, Revision 2, Hunters Point Shipyard, San Francisco, California." May.

TtEC, 2010a. "Final Completion Letter Report, Pickling Vault Removal, Parcel G, Hunters Point Shipyard, San Francisco, California." July 2.

_____, 2010b. "Final Basewide Dust Control Plan, Revision 1, Hunters Point Shipyard, San Francisco, California." November 29.

_____, 2011a. "Final Removal Action Completion Report, Parcels UC1 and UC2, Hunters Point Shipyard, San Francisco, California." March 2.

_____, 2011b. "Final Removal Action Completion Report, Parcel G, Hunters Point Naval Shipyard, San Francisco, California." December 2.

_____, 2011c. "Final Radiological Removal Action Completion Report, Revision 2, Parcel D-2, Hunters Point Naval Shipyard, San Francisco, California." December 16.

_____, 2012a. "Final Radiological Removal Action Completion Report, Parcel B, Hunters Point Naval Shipyard, San Francisco, California." March 2.

_____, 2012b. "Final Radiological Removal Action Completion Report, Parcel UC3, Hunters Point Naval Shipyard, San Francisco, California." March 16.

_____, 2012c. "Final Radiological Remedial Action Completion Report, Installation Restoration Site 07, Hunters Point Naval Shipyard, San Francisco, California." May 11. (Included as Attachment 3 in ERRG, 2012a).

_____, 2012d. "Final Radiological Remedial Action Completion Report, Installation Restoration Site 18, Hunters Point Naval Shipyard, San Francisco, California." May 11. (Included as Attachment 3 in ERRG, 2012a).

_____, 2012e. "Final, Final Status Survey Results, Building 500, Hunters Point Naval Shipyard, San Francisco, California." October 9.

_____, 2012f. "Final, Final Status Survey Results, Former Building 529 Site, Hunters Point Naval Shipyard, San Francisco, California." October 16.

_____, 2012g. "Final, Final Status Survey Results, Former Building 509 Site, Hunters Point Naval Shipyard, San Francisco, California." October 24.

_____, 2012h. "Final, Final Status Survey Results, Building 521, Hunters Point Naval Shipyard, San Francisco, California." October 25.

_____, 2013a. "Final Radiological Dose and Risk Modeling for the IR-07 and IR-18 Radiologically Impacted Area Requiring Institutional Controls, Parcel B, Hunters Point Naval Shipyard, San Francisco, California." January.

_____, 2013b. "Final, Final Status Survey Results, Former Building 510/510A Site, Hunters Point Naval Shipyard, San Francisco, California." January.

TtEC, 2013c. "Final, Final Status Survey Results, Former Building 507 Site, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013d. "Final, Final Status Survey Results, Former Building 508 Site, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013e. "Final Survey Unit 225 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013f. "Final Survey Unit 228 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013g. "Final Survey Unit 229 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013h. "Final Survey Unit 230 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013i. "Final Survey Unit 235 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013j. "Final Survey Unit 240 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013k. "Final Survey Unit 241 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013l. "Final Survey Unit 245 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013m. "Final Survey Unit 246 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013n. "Final Survey Unit 248 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013o. "Final Survey Unit 249 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013p. "Final Survey Unit 300 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013q. "Final Survey Unit 301 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013r. "Final Survey Unit 305 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

TtEC, 2013s. "Final Survey Unit 306 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013t. "Final Survey Unit 307 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013u. "Final Survey Unit 308 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013v. "Final Survey Unit 309 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013w. "Final Survey Unit 310 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013x. "Final Survey Unit 311 Project Report, Parcel E Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2013y. "Final Status Survey Results, Former Building 506 Site, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2013z. "Final, Final Status Survey Results, Former Building 520 Site, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2013aa. "Final Survey Unit Project Reports Abstract for Sanitary Sewer and Storm Drain Removal Conducted After September 1, 2012, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2013ab. "Final, Final Status Survey Results, Former Building 503 Site, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2013ac. "Final Design Plan, Parcel E, Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." November.

_____, 2014a. "Final Survey Unit 244 Project Report, Parcel C Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2014b. "Final Survey Unit 247 Project Report, Parcel C Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2014c. "Final Survey Unit 302 Project Report, Parcel C Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2014d. "Final Survey Unit 303 Project Report, Parcel C Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2014e. "Final Survey Unit 304 Project Report, Parcel C Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." March.

TtEC, 2014f. "Final, Final Status Survey Results, Former Building 517 Site, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2014g. "Investigation Conclusion, Anomalous Soil Samples at Hunters Point Naval Shipyard, Revision 1, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2014h. "Final Survey Unit 312 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014i. "Final Survey Unit 314 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014j. "Final Survey Unit 315 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014k. "Final Survey Unit 317 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014l. "Final Survey Unit 319 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014m. "Final Survey Unit 320 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014n. "Final Survey Unit 321 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014o. "Final Survey Unit 322 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014p. "Final Survey Unit 324 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014q. "Final Survey Unit 328 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014r. "Final Survey Unit 329 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014s. "Final Survey Unit 330 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014t. "Final Survey Unit 331 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014u. "Final Survey Unit 332 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

TtEC, 2014v. "Final Survey Unit 323 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2014w. "Final, Final Status Survey Results, Revision 1, Former Shack 79 and 80 Sites, Hunters Point Naval Shipyard, San Francisco, California." August.

_____, 2015a. "Final Survey Unit Project Reports Abstract for Parcel C Sanitary Sewer and Storm Drain Removal Containing Naturally Occurring Radioactive Material (NORM) Fill Material Conducted After March 1, 2013, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2015b. "Final Remedial Action Work Plan for the Installation of Durable Covers in Parcel C, Hunters Point Naval Shipyard, San Francisco, California." July.

_____, 2015c. "Final Survey Unit 236 Project Report, Parcel C Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." October.

_____, 2015d. "Final Survey Unit 238 Project Report, Parcel C Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." October.

_____, 2015e. "Final Survey Unit 242 Project Report, Parcel C Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." October.

_____, 2015f. "Final Survey Unit 243 Project Report, Parcel C Storm Drain and Sanitary Sewer Removal, Hunters Point Naval Shipyard, San Francisco, California." October.

_____, 2016a. "Final Survey Unit 337 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." February.

_____, 2016b. "Final Survey Unit 339 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." February.

_____, 2016c. "Final Execution Plan, Parcel C Phase III Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2016d. "Final Radiological Construction Summary Report, Parcel C Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." June 20.

_____, 2016e. "Final, Final Status Survey Results, Ship Berths 1, 2, 3, 4, and 5, Hunters Point Naval Shipyard, San Francisco, California." August.

_____, 2016f. "Final Survey Unit 340 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2016g. "Final Survey Unit 341 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

TtEC, 2016h. "Final Survey Unit 342 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2016i. "Final Survey Unit 343 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2016j. "Final Survey Unit 344 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2016k. "Final Survey Unit 345 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2016l. "Final Survey Unit 346 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2016m. "Final Survey Unit 347 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2016n. "Final Survey Unit 348 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2016o. "Final Survey Unit 349 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2016p. "Final Survey Unit 350 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2016q. "Final Survey Unit 351 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2016r. "Final Survey Unit 352 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2016s. "Final Survey Unit 353 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

TtEC, 2016t. "Final Survey Unit 354 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2016u. "Final Survey Unit 355 Project Report, Parcel E Sanitary Sewer and Storm Drain Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2017a. "Final, Final Status Survey Report, Building 224, Parcel C Phase III Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." February.

_____, 2017b. "Final Operation and Maintenance Plan for the Durable Covers in Parcel C, Hunters Point Naval Shipyard, San Francisco, California." February.

_____, 2017c. "Final Remedial Action Completion Report for the Durable Covers Remedy in Parcel C, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2017d. "Characterization Survey Results, Building 211, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2017e. "Characterization Survey Results, Building 253, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2017f. "Final Construction Summary Report, Parcel C Phase III, Characterization Study Performed on Storm Drain and Sanitary Sewer Lines Located Within the 10-Foot Buffer Zone of Buildings 204, 205, 207, and 208, Hunters Point Naval Shipyard, San Francisco, California." June.

_____, 2017g. "Final Technical Memorandum to Support No Further Action for Building 205, Including the Suction Channels and Discharge Piping, Parcel C Phase III Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." July.

_____, 2017h. "Final Annual Operation and Maintenance Summary Report for the Durable Covers Remedy in Parcel C, Hunters Point Naval Shipyard, San Francisco, California." August.

_____, 2017i. "Final Survey Unit 318 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." August.

_____, 2017ji. "Final Survey Unit 325 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." August.

_____, 2017k. "Final Survey Unit 326 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." August.

_____, 2017l. "Final Survey Unit 327 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." August.

TtEC, 2017m. "Final Survey Unit Project Reports Abstract for Parcel C Sanitary Sewer and Storm Drain Removal Containing Naturally Occurring Radioactive Material (NORM) Fill Material Conducted After March 1, 2013, Revision 1, Hunters Point Naval Shipyard, San Francisco, California." August.

_____, 2017n. "Final Survey Unit 313 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2017o. "Final Survey Unit 316 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2017p. "Final Survey Unit 333 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2017q. "Final Survey Unit 334 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2017r. "Final Survey Unit 335 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2017s. "Final Survey Unit 336 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

_____, 2017t. "Final Survey Unit 338 Project Report, Parcel C Phase II Radiological Remediation and Support, Hunters Point Naval Shipyard, San Francisco, California." September.

Tetra Tech EM Inc. (TtEMI), 1998a. "Parcel E Feasibility Study, Draft Report, Hunters Point Shipyard, San Francisco, California." January.

_____, 1998b. "Final Basewide Environmental Baseline Survey, Revision 01, Hunters Point Shipyard, San Francisco, California." September 4.

_____, 2001a. "Revised Information Package for the Phase I Groundwater Data Gaps Investigation, Hunters Point Shipyard, San Francisco, California." January 8.

_____, 2001b. "Final Remedial Design Amendment, Parcel B, Hunters Point Shipyard, San Francisco, California." February 20.

_____, 2001c. "Parcel E Information Package, Phase II Groundwater Data Gaps Investigation, Hunters Point Shipyard, San Francisco, California." August 10.

_____, 2002a. "Revised Parcel D Information Package, Phase II Groundwater Data Gaps Investigation, Hunters Point Shipyard, San Francisco, California." March 8.

_____, 2002. "Final Parcel C Time-Critical Removal Action Closeout Report, Hunters Point Shipyard, San Francisco, California." July 12.

TtEMI, 2003a. "Final Emergency Removal Action Closeout Report, Encapsulation of Drainage Culvert Sediment at Dry Dock 4, Installation Restoration Site 57, Parcel C, Hunters Point Shipyard, San Francisco, California." February 20.

_____, 2003b. "Final Operation and Maintenance Plan, IR-01/21, Industrial Landfill, Parcel E, Hunters Point Shipyard, San Francisco, California." May 30.

_____, 2003c. "Final Cost and Performance Report Ferox Injection Technology Demonstration, Parcel C, Remedial Unit C4, Hunters Point Shipyard, San Francisco, California." July 11.

_____, 2003d. "Final Parcel E Nonstandard Data Gaps Investigation, Wetlands Delineation and Functions and Values Assessment, Parcels B and E, Hunters Point Shipyard, San Francisco, California." August 14.

_____, 2003e. "Final Soil Vapor Extraction Confirmation Study Summary, Building 123, Installation Restoration Site 10, Parcel B, Hunters Point Shipyard, San Francisco, California." August 19.

_____, 2003f. "Final First Five-Year Review of Remedial Actions Implemented at Hunters Point Shipyard, San Francisco, California." December 10.

_____, 2003g. "Final Parcel E Nonstandard Data Gaps Investigation, Landfill Gas Characterization, Hunters Point Shipyard, San Francisco, California." December 23.

_____, 2004a. "Draft Removal Action Closeout Report, Parcel E Landfill Gas Time-Critical Removal Action Closeout Report, Parcel E, Hunters Point Shipyard, San Francisco, California." March 19.

_____, 2004b. "Revised Final Parcel C Groundwater Summary Report, Phase III Groundwater Data Gaps Investigation, Hunters Point Shipyard, San Francisco, California." May 11.

_____, 2004c. "Revised Final Parcel E Groundwater Summary Report, Phase III Groundwater Data Gaps Investigation, Hunters Point Shipyard, San Francisco, California." May 11.

_____, 2004d. "2003–2004 Annual Report for Storm Water Discharge Management, IR-01/21, Industrial Landfill, Parcel E, Hunters Point Shipyard, San Francisco, California." July 1.

_____, 2004e. "Final Sampling and Analysis Plan (Field Sampling Plan and Quality Assurance Project Plan), Basewide Groundwater Monitoring Program, Hunters Point Shipyard, San Francisco, California." August 20.

_____, 2004f. "Final Finding of Suitability to Transfer for Parcel A (Revision 3), Hunters Point Shipyard, San Francisco, California." October 14.

_____, 2004g. "Final Parcel E Nonstandard Data Gaps Investigation, Landfill Lateral Extent Evaluation, Hunters Point Shipyard, San Francisco, California." October 29.

_____, 2005. "Final Removal Action Landfill Cap Closeout Report, Parcel E-2, Hunters Point Shipyard, San Francisco, California." February 7.

TtEMI and IT Corporation, 2001. "Final Parcel D Time Critical Removal Action Closeout Report, Hunters Point Shipyard, San Francisco, California." December 6.

TtEMI and ITSI, 2004a. "Final Parcel B Shoreline Characterization Technical Memorandum, Hunters Point Shipyard, San Francisco, California." March 23.

_____, 2004b. "Final Parcel E Nonstandard Data Gaps Investigation, Landfill Liquefaction Potential, Hunters Point Shipyard, San Francisco, California." August 13.

_____, 2005. "Final Closeout Report, Time-Critical Removal Action for Parcel D Excavation Sites, Hunters Point Shipyard, San Francisco, California." May 13.

TtEMI and LFR, 1998a. "Draft Parcel F Feasibility Study Report, Hunters Point Shipyard, San Francisco, California." April 3.

_____, 1998b. "Parcel C Feasibility Study, Draft Final Report, Hunters Point Shipyard, San Francisco, California." July 15.

_____, 2000. "Draft Final Ecological Risk Assessment Validation Study Report, Parcel E, Hunters Point Shipyard, San Francisco, California." March 14.

TtEMI, LFR, and Uribe and Associates, 1997. "Parcel E Remedial Investigation, Draft Final Report, Hunters Point Shipyard, San Francisco, California." October 27.

Tetra Tech FW, Inc. (TtFW), 2004a. "Base-wide Radiological Work Plan. Hunters Point Naval Shipyard, San Francisco, California." July 9.

_____, 2004b. "Final Post-Construction Report, Revision 0, Decontaminate Process Equipment, Conduct Waste Consolidation, and Provide Asbestos Services in Parcels B, C, D, and E, Hunters Point Shipyard, San Francisco, California." November 2.

The Alliance Compliance Group Joint Venture (Alliance), 2008. "Final Work Plan for Groundwater Treatability Study, Parcel G, Hunters Point Shipyard, San Francisco, California." September 1.

_____, 2010. "Final Parcels D-1 and G Groundwater Treatability Study Technical Report, IR-09, IR-33, and IR-71, Hunters Point Shipyard, San Francisco, CA." March.

_____, 2013. "Final Remedial Action Work Plan, Remedial Unit C2, Hunters Point Naval Shipyard, San Francisco, CA." March.

TPA-CKY Joint Venture, 2005. "Draft Final Site Closeout Report, Total Petroleum Hydrocarbon Program Corrective Action Implementation Soil Removal for Parcels B, C, D, and E, Hunters Point Shipyard, San Francisco, California." June.

TPS Tech, Cabrera-Insight JV, and CDM Smith, 2013. "Final In Situ Thermal Remediation Design, NAPL Treatment Pilot Study, Installation Restoration Program Site 03, Former Oily Waste Ponds, Hunters Point Naval Shipyard, San Francisco, California." October.

Trevet, Inc., 2017a. "Final Management and Monitoring Approach Sampling and Analysis Plan for Basewide Groundwater Monitoring Program, Hunters Point Naval Shipyard, San Francisco, California." April.

_____, 2017b. [REFERNCE BGMP SEMIANNUAL REPORT]

_____, 2018. [REFERNCE BGMP SEMIANNUAL REPORT]

TriEco-Tetra Tech Sustainable Resources Joint Venture (TriEco-Tt), 2013a. "Final Parcel E Pothole Area Characterization Work Plan, Hunters Point Naval Shipyard, San Francisco, California." May.

_____, 2013b. "Final Third Five-Year Review of Remedial Actions, Hunters Point Naval Shipyard, San Francisco, California." November 8.

_____, 2014. "Final Parcel E Pothole Area Characterization Technical Memorandum, Hunters Point Naval Shipyard, San Francisco, California." March.

_____, 2015a. "Final Finding of Suitability to Transfer for Parcels UC-1 and UC-2, Hunters Point Naval Shipyard, San Francisco, California." March 25.

_____, 2015b. "Final Mercury Evaluation Work Plan, Installation Restoration Site 26, Parcel B-2, Hunters Point Naval Shipyard, San Francisco, California." July.

_____, 2016. "Final Mercury Evaluation Technical Memorandum, Installation Restoration Site 26, Parcel B-2, Hunters Point Naval Shipyard, San Francisco, California." May.

U.S. Environmental Protection Agency (EPA), 2001. "Comprehensive Five-Year Review Guidance." June. Available Online at: <https://www.epa.gov/superfund/writing-five-year-reviews-superfund-sites#general_anchor>.

_____, 2011. "Recommended Evaluation of Institutional Controls: Supplement to the 'Comprehensive Five-Year Review Guidance,' OSWER Directive 9355.7-18." September 13. Available Online at: <https://www.epa.gov/superfund/writing-five-year-reviews-superfund-sites#general_anchor>.

_____, 2012a. "Memorandum: Clarifying the Use of Protectiveness Determinations for Comprehensive Environmental Response, Compensation, and Liability Act Five-Year Reviews." September 13. Available Online at: <https://www.epa.gov/superfund/writing-five-year-reviews-superfund-sites#general_anchor>.

_____, 2012b. "Assessing Protectiveness at Sites for Vapor Intrusion, Supplement to the 'Comprehensive Five-Year Review Guidance,' OSWER Directive 9200.2-84." December 3. Available Online at: <https://www.epa.gov/superfund/writing-five-year-reviews-superfund-sites#general_anchor>.

_____, 2014. "Human Health Evaluation Manual, Supplemental Guidance: Update of Standard Default Exposure Factors. OSWER 9200.1-120."

EPA, 2016. "Five-Year Review Recommended Template, OLEM 9200.0-89." January 20. Available Online at: <https://www.epa.gov/superfund/writing-five-year-reviews-superfund-sites#general_anchor>.

_____, 2018. "Regional Screening Levels (RSL)" May. Available Online at: <https://www.epa.gov/risk/regional-screening-levels-rsls-generic-tables>.

Appendix B. Interview and Survey Records

Appendix B1. Regulatory Agency Interview Records

INTERVIEW RECORD

SITE IDENTIFICATION		
Site Name: Hunters Point Naval Shipyard	EPA ID: CA1170090087	
Subject: Five-Year Review of Remedial Actions	Time: 12:11 PM	Date: 2/22/2018
Type: ☐ Telephone ☒ Visit ☒ Email ☐ Other		
Location of Visit: 101 California Street, 48th Floor, San Francisco, California		

CONTACT MADE BY:		
Name: Stephen Banister	Title: Remedial Project Manager	Organization: Navy
Name: John Sourial	Title: Project Manager	Organization: Innovex-ERRG JV
Name: Spencer Johnson	Title: Project Engineer	Organization: Innovex-ERRG JV

INDIVIDUAL CONTACTED			
Name: Lily Lee	Title: EPA Site Manager	Organization: EPA Region 9	
Telephone: (415) 947-4187		Address: 75 Hawthorne Street SFD-8	
Fax: (415) 947-3520	City: San Francisco	State: CA	Zip: 94105
E-mail address: Lee.Lily@epa.gov			

SUMMARY OF CONVERSATION

In-person interview held with Lily Lee (EPA) on 2/22/2018. Interview team transmitted notes from the meeting to Lily Lee on 2/26/2018. Formal responses provided on the following pages provided to the interview team on 03/14/2018.

INTERVIEW RECORD

1. What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth Five-Year Review (2013 to present)?

I have been working on HPNS since June 2014. My overall impression of the cleanup work at HPNS is that the Navy has made this cleanup project a high priority and a great deal of Navy resources and effort are going into the cleanup. The emergence of widespread falsification of radiological data by Tetra Tech EC Inc. has been a significant problem that will require substantial rework and that has undermined trust in the integrity of the cleanup by all stakeholders. The vast scope of the signs of falsification found is unprecedented nationally. As EPA wrote in December, 2016, "the Navy's technical review needs to be comprehensive and holistic to scientifically address protectiveness questions. In addition, proactive and transparent community involvement will be key to address public confidence in the scientific review and its conclusions."

2. Have there been routine communications or activities (site visits, inspections, reporting activities, etc.) conducted by your office regarding the site? If so, please give purpose and results.

Over the past five years, U.S. EPA has worked with its state and local regulatory partners to conduct periodic onsite inspections of the Navy's cleanup work at HPNS to understand field conditions. Originally EPA did joint inspections with the State Regional Water Quality Control Board and the State Department of Toxic Substances Control (DTSC). In 2104, because community members continued to raise concerns about dust, EPA also invited the Bay Area Air Quality Management District inspectors to join inspections, and we observed gaps in dust control during such field visits. The Navy improved its dust control practices, and dust complaints have decreased. More recently, the State of California Department of Toxic Substances Control has started sending Industrial Hygienists to perform regular inspections at the site. Reports of those appear on the DTSC's website. They have made no observations of violations. EPA also attends regular monthly BRAC Cleanup Team (including Navy, EPA, and the State) where we review the status of ongoing cleanup actions and provide input.

However, given the egregious failures by Tetra Tech EC Inc. to follow its own workplans, more oversight is clearly necessary. Therefore, EPA has gathered a team of national expert health physicists and a statistician to do detailed reviews of Tetra Tech EC Inc. previous work and Navy plans for rework. When resampling of these locations is conducted, EPA and its state regulatory partners commit to monitoring the rework in person at the site.

3. Have there been any complaints, violations, or other incidents related to the site requiring a response by your office? If so, please give details of the events and results of the responses.

EPA receives frequent strong complaints from stakeholders regarding concerns about health risks and about meaningful community involvement. EPA also receives frequent press questions. The predominant concern in the last five years by far has been the falsification of radiological data by Tetra Tech EC Inc.

Examples of radiological-related activities that have prompted regular discussion amongst EPA, the Navy, and stakeholders include the following:

- *the Nuclear Regulatory Commission (NRC) documented violations regarding soil in trenches in one part of Parcel C.*
- *Non governmental organizations have filed petitions to the NRC and to the State that are relevant to radiological cleanup at this site.*
- *EPA stated in its comments to the Navy on its Draft Radiological Data Evaluation for Parcels B and G, "The data analyzed demonstrate a widespread pattern of practices that appeared to show potential deliberate falsification, potential failure to perform the work required to ensure ROD requirements were met, or both. The data revealed not only potential purposeful falsification and fraud in terms of sample and/or data manipulation, they also reveal the potential failure to conduct adequate scans, a lack of proper chain of custody for ensuring samples were not tampered with, extensive data quality*

issues (including off-site laboratory data) and general mis-management of the entire characterization and cleanup project."

The above are serious concerns. The Navy, as the lead on cleanup, has responded through a comprehensive radiological data evaluation, increased oversight of ongoing radiological work, development of plans to resample all radiological survey units on site that involved Tetra Tech EC Inc., and increased community involvement outreach. In its oversight role, EPA has also significantly increased its resources devoted to all these steps to ensure protectiveness at the site. EPA staff also participate in Navy community outreach events (community meetings and bus tours) to ensure community members get the information they need on the cleanup and can express their concerns. EPA also provides input to the Navy on how to make community involvement practices more effective.

4. Do you feel well informed about the site's activities and progress?

The BRAC Cleanup Team meets monthly and the Navy project managers provide general updates on some cleanup project at HPNS. The Navy also provides updates to the comprehensive project schedule under the HPNS Federal Facility Agreement (FFA), which identifies major milestones in each parcel. In addition to the technical deliverables required under the FFA, Navy project managers email me and my State counterparts with project updates and uses technical meetings to solve more complex issues concerning a cleanup project area. The amount of information provided at the BCT Meetings, especially with respect to non-radiation sites/issues, has decreased over the past five years. Thus, at times EPA has sometimes not understood the Navy's intentions when we have received documents for review, so more discussion, longer comments, and more meetings have been needed. As another example, the Navy changed the locations of wells in the Basewide Groundwater Sampling Plan without prior notification and justification to the regulatory agencies. More proactive sharing of information would improve efficiency in document reviews and ensure adequate oversight.

5. Do you have any comments, suggestions, or recommendations regarding the site?

As EPA stated in its comments on the draft Radiological Data Evaluation Report for Parcels B and G, "In the bigger picture, beyond the scope of this specific Report, prior to resampling efforts, a thorough review of work plans, process review, documentation, and data quality should be of primary concern to ensure that high quality defensible data is obtained. Ongoing onsite oversight by the Navy and regulatory agencies should be conducted frequently." The Navy hired a third-party contractor for oversight of ongoing radiological work, both in the field and review of procedures and documents. This practice is helpful and should be expanded. More broadly, please address in the Five-Year Review the steps the Navy has already taken and will take in the future to improve contractor oversight.

In addition, the radiological data falsification has dramatically increased the level of community concern about health risks and credibility of the cleanup. As EPA wrote in 2016 recommendations for the Tetra Tech EC Inc. evaluation, "The overall objective of the following recommendations is to maximize public confidence in the Tetra Tech investigation process by establishing a consistent flow and transparent exchange of information with the public as the Navy's workplan unfolds. Consistently throughout the process, not just at project milestones, the community is expected to be 'brought along' for input and participation with regulators as investigatory processes are established and decisions are made." While the Navy has stepped up its community involvement efforts, EPA continues to recommend more practices to improve meaningful dialogue, e.g. that the Navy should fully advertise all its public presentations, including those hosted by other organizations and that the Navy should be ready to discuss radiological issues upon request in an open forum at any public meeting, not just at those where that is the advertised topic. Also, EPA has repeatedly recommended that the Navy, as the lead on the cleanup, attend local community meetings, especially when invited to do so. These recommendations should be part of the 2018 Community Involvement Plan update. Doing so will help maximize the opportunity for the public to receive factually correct information and will demonstrate that the Navy is committed to a transparent process.

INTERVIEW RECORD

As part of this Five-Year Review, the most current information related to potential climate change impacts should be evaluated to ensure protectiveness of site remedies. For example, please review the containment plans for the landfill using the most current projections for sea level rise.

Please address PFAS compounds in the Five-Year Review. The military specifications for aqueous film forming foam (AFFF) were adopted in December 1969, so AFFF could have been used to fight fires for about 4 to 5 years. In addition, starting in the early 1950s, PFAS compounds were added to liquids for nearly every process involved in plating. PFAS compounds were also used in liquid shields to reduce vapors from plating operations.

INTERVIEW RECORD

SITE IDENTIFICATION		
Site Name: Hunters Point Naval Shipyard	EPA ID: CA1170090087	
Subject: Five-Year Review of Remedial Actions	Time: 1:00 PM	Date: 2/22/2018
Type: ☐ Telephone ☒ Visit ☒ Email ☐ Other		
Location of Visit: 101 California Street, 48th Floor, San Francisco, California		

CONTACT MADE BY:		
Name: Stephen Banister	Title: Remedial Project Manager	Organization: Navy
Name: John Sourial	Title: Project Manager	Organization: Innovex-ERRG JV
Name: Spencer Johnson	Title: Project Engineer	Organization: Innovex-ERRG JV

INDIVIDUAL CONTACTED			
Name: Nina Bacey	Title: Project Manager	Organization: CalEPA – California Department of Toxic Substances Control	
Telephone: (510) 540-3480		Address: 700 Heinz Ave., Bldg. F, Suite 200	
Fax: (510) 540-3819	City: Berkeley	State: CA	Zip: 94710-2721
E-mail address: Juanita.Bacey@dtsc.ca.gov			

SUMMARY OF CONVERSATION

In-person interview held with Nina Bacey (DTSC) on 2/22/2018. Interview team transmitted notes from the meeting to Nina Bacey on 2/26/2018. Formal responses provided on the following pages provided to the interview team on 3/3/2018.

INTERVIEW RECORD

1. What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

I have been working on the HPNS project Site since early 2015. Cleanup work of chemicals of concern (COCs) in soil, soil gas and groundwater is generally moving at an adequate pace and work quality has generally fine since I began working on the Site.

When I started working on this Site, the finalization of radiological survey reports for various buildings were on hold. The California Department of Public Health and the Navy were discussing the path forward after discovering the Navy contractor had not performed all surveys at the speed required in the approved work plan. An agreement was reached in approximately one year and additional surveys were conducted within another six months. The Navy and regulatory agencies conducted more extensive oversight of the resurveying activities. Some reports were then finalized. However, in late 2016 additional accusations were made against the Navy's contractor alleging more extensive sampling and data issues. Therefore, the finalization of the remaining building reports has again been put on hold. These issues have shown that the Navy needs to improve its oversight of its radiologic investigation and cleanup contractors.

2. Have there been routine communications or activities (site visits, inspections, reporting activities, etc.) conducted by your office regarding the site? If so, please give purpose and results.

I have conducted periodic site visits to observe the Navy's remediation fieldwork in Parcels B-1, B-2, C, E-2, F. I conducted periodic inspections and oversight for rescanning of radiological field work. The Navy provides occasional reporting on the status of remediation fieldwork to the Base Closure Team (BCT). The Navy also provides updates upon DTSC request. DTSC conducts periodic perimeter dust monitoring at Parcel E-2 to ensure that the Navy contractor is conducting their required dust control measures and controlling dust emissions appropriately. I attend monthly BCT meetings and technical meetings (conference calls). Regular communication between the Navy and DTSC is daily via email and/or telephone calls. The frequency is adequate. Communication and coordination between the DTSC, US EPA, the Water Board and CDPH is great.

3. Have there been any complaints, violations, or other incidents related to the site requiring a response by your office? If so, please give details of the events and results of the responses.

Dust: The community raised concerns related to dust generation and offsite migration at Parcel E-2, so DTSC initiated its own dust monitoring twice weekly for 1-2 hours per event. This was subsequently reduced to once per month based on results. The air monitoring results are available on Envirostor.

Radionuclides: Protection of the community (human health and the environment) is a high concern of the community due to public allegations of data falsification. Therefore, the community is very concerned about the adequacy of the Navy's radiological cleanup activities. DTSC has received numerous inquiries and/or requests for DTSC to play a more active role with regard to the soil falsification issue, and to make sure the Navy redoes the cleanup work at the Hunters Point Site. DTSC is working with the US EPA, CDPH and the Navy to

determine appropriate steps to resolve this issue. These requests have come from the community, press, and environmental justice groups. We have received Public Records Act requests for records from the press, environmental justice groups and others. DTSC responds accordingly to those requests.

4. Do you feel well informed about the site's activities and progress?

Yes, I generally feel well informed. Radiological issues have complicated the cleanup process, slowed the property transfer progress, and diverted DTSC staff resources, delaying review of other non-radiological documents. As the lead regulatory agency, EPA Region 9 communicates more regularly with the Navy and promptly relays information to DTSC. The DTSC and US EPA Project Managers communicate daily on project issues. Currently, DTSC also communicates nearly daily with Navy staff on non-radiological site activities, and daily with CDPH on radiological site activities.

5. Do you have any comments, suggestions, or recommendations regarding the site?

The FFA schedule should be adjusted to permit adequate time for non-radiological document reviews. The radiological soil and building evaluations have taxed DTSC's ability to meet review deadlines. The radiological documents are time-consuming to review and evaluate.

Greater oversight by Navy RPMs and RASO of contractor field work and document review may be necessary. At times, some documents appear to lack thorough review by the Navy (both in ensuring field documentation is complete and in providing adequate reports). Poor document quality was an issue in 2016, but it currently occurs infrequently. Quality control issues have been seen on both radiological and non-radiological field forms/notes and documents.

INTERVIEW RECORD

SITE IDENTIFICATION		
Site Name: Hunters Point Naval Shipyard	EPA ID: CA1170090087	
Subject: Five-Year Review of Remedial Actions	Time: 2:00 PM	Date: 2/22/2018
Type: ☒ Telephone ☐ Visit ☒ Email ☐ Other		
Location of Visit: Phone conference.		

CONTACT MADE BY:		
Name: Stephen Banister	Title: Remedial Project Manager	Organization: Navy
Name: John Sourial	Title: Project Manager	Organization: Innovex-ERRG JV
Name: Spencer Johnson	Title: Project Engineer	Organization: Innovex-ERRG JV

INDIVIDUAL CONTACTED			
Name: David Tanouye	Title: Engineering Geologist	Organization: CalEPA – San Francisco Bay Regional Water Quality Control Board	
Telephone: (510) 622-2360		Address: 1515 Clay Street, Suite 1400	
Fax: (510) 622-2460	City: Oakland	State: CA	Zip: 94612
E-mail address: david.tanouye@waterboards.ca.gov			

SUMMARY OF CONVERSATION

Telephone conference interview held with David Tanouye (RWQCB) on 2/22/2018. Interview team transmitted notes from the meeting to David Tanouye on 2/26/2018. Formal responses provided on the following pages provided to the interview team on 03/05/2018.

INTERVIEW RECORD

1. What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

I began working on HPNS team for the Regional Water Board in Dec 2017, and took on the role of project manager in Feb 2018 after Tina Ures left her position. My initial impression is that cleanup is being conducted satisfactorily. I attend basewide meetings, interaction is frequent, and responsiveness of the Navy is good.

2. Have there been routine communications or activities (site visits, inspections, reporting activities, etc.) conducted by your office regarding the site? If so, please give purpose and results.

I have been on monthly site inspections since I started on the HPNS project. The fieldwork tracking sheet is a useful tool to permit coordination with field teams. I attended weekly meetings or conference calls for various aspects of projects, and review/respond to questions on documents, as needed. I am not really involved in commenting on radiological issues and documents, but the technical team meetings keep me informed on the status of the radiological cleanup. I am aware of when FFA documents are due. I attend community meetings. I find that communication is adequate. In the past, meetings on petroleum program were not frequent or regular. We worked with the Navy to established a monthly call to maintain regular interaction and receive regular updates.

3. Have there been any complaints, violations, or other incidents related to the site requiring a response by your office? If so, please give details of the events and results of the responses.

I have not received any complaints, violations, etc. I have seen emails regarding complaints received by EPA (via email). One concern the RWQCB has relates to buildings releasing paint chips that can migrate to swales and San Francisco Bay.

4. Do you feel well informed about the site's activities and progress?

I attend monthly meetings on petroleum. I find it useful to have regular phone calls and meetings. I am deferring commenting on progress, as I have not been involved for very long. My impression is that site activities are well organized.

5. Do you have any comments, suggestions, or recommendations regarding the site?

I would like to see additional organization for petroleum site activities. Document tracking, field activities, etc.

In certain cases, especially those related to commingled petroleum contamination, we have received RTCs that deflect our comments and point to another document without citing specific language to address the concern. We understand that corrective actions for petroleum have not been consistent, and in some cases fall behind the CERCLA schedule. However, we expect RTCs to adequately respond to our comments, with fully paraphrased responses when referencing another document.

INTERVIEW RECORD

SITE IDENTIFICATION		
Site Name: Hunters Point Naval Shipyard	EPA ID: CA1170090087	
Subject: Five-Year Review of Remedial Actions	Time: 2:35 PM	Date: 2/22/2018
Type: ☐ Telephone ☒ Visit ☒ Email ☐ Other		
Location of Visit: 101 California Street, 48th Floor, San Francisco, California		

CONTACT MADE BY:		
Name: Stephen Banister	Title: Remedial Project Manager	Organization: Navy
Name: John Sourial	Title: Project Manager	Organization: Innovex-ERRG JV
Name: Spencer Johnson	Title: Project Engineer	Organization: Innovex-ERRG JV

INDIVIDUAL CONTACTED			
Name: Amy Brownell	Title: Environmental Engineer	Organization: San Francisco Department of Public Health	
Telephone: (415) 252-3967		Address: 1390 Market St., Suite 210	
Fax: (415) 252-3889	City: San Francisco	State: CA	Zip: 94102
E-mail address: amy.brownell@sfdph.org			

SUMMARY OF CONVERSATION

In-person interview held with Amy Brownell (SFDPH) on 2/22/2018. Interview team transmitted notes from the meeting to Amy Brownell on 2/26/2018. Formal responses provided on the following pages provided to the interview team on 3/8/2018.

INTERVIEW RECORD

1. What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

There has been a tremendous amount of work and progress. There has been significant and very visible earthwork, especially in Parcel E-2, completion of durable covers across the base, transfers of D-2, UC-1, UC-2 (which required cooperation by all parties for the post-CERCLA process and OCII approval). There would have been more transfers had the problems with the Tetratech radiological data not arisen. Progress is continuing and there's still good progress being made, despite the "road block" of the radiological issues. Unfortunately, the delays may have impacts on OCII's and the developer's schedule and planning.

2. Have there been routine communications or activities (site visits, inspections, reporting activities, etc.) conducted by your office regarding the site? If so, please give purpose and results.

Our office plays two roles in the HPNS cleanup. We are both the independent Health Agency for the City and County of San Francisco and we also provide technical advice to many City departments; most prominently the Department of Public Health, the Office of Community Investment and Infrastructure and the Mayor's office and the Mayor's HPNS Citizens Advisory Committee about the Navy's cleanup. In these unique roles, we can assist the Navy in verifying that their cleanup will be compatible the planned redevelopment and ensure that the cleanup protects human health and the environment. We communicate on a daily basis with the Navy and Regulatory Agencies and participate in the Base Closure Team. We have independent technical consultants who review the Navy's information and assist in providing independent comments on the Navy's work. Communication is more than adequate. Recent issues have made communication more robust. There has been communication on an almost daily basis between all parties about all the Navy cleanup issues and the Regulatory Agencies oversight of those issues. SFPDH is kept well informed by all parties.

3. Have there been any complaints, violations, or other incidents related to the site requiring a response by your office? If so, please give details of the events and results of the responses.

We do not have an independent regulatory oversight role. As described above, we work closely with the Navy and Regulatory Agencies. However, we do not directly respond to incidents related to Navy activities, that responsibility rests with the Navy and the Regulatory Oversight Agencies. SFDPH gets complaints and inquiries along the same lines as other agencies. Typical protocol is to refer the inquirer to the appropriate agencies and assist by providing contact information or specific background about the issues. A typical question is "Do you think the site is safe?" SFDPH shares all information about the work that has been done, the CERCLA process, and requirements for transfer, and the fact that the site is safe in the current condition and will be safe for the current and future uses because of the detailed CERCLA process and the requirement that the Regulatory Agencies verify that the property is suitable for the intended uses prior to transfer.

4. Do you feel well informed about the site's activities and progress?

I am very well informed.

INTERVIEW RECORD

5. Do you have any comments, suggestions, or recommendations regarding the site?

In 2008, San Francisco voters passed Proposition G that makes it City Policy to encourage timely development of the land for the Hunters Point Shipyard and Candlestick Point development https://sfpl.org/index.php?pg=2000027201&propid=1800. As the Department in charge of maintaining public health, we are committed to working with the Navy and Regulatory Agencies to ensure public health and safety as part of the transfer and timely development. We will continue in our role of promoting open communication with the public about the land use restoration and cooperate with all parties to meet the will of the SF voters.

Appendix B2. Community Member Survey Records

#1

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Monday, February 26, 2018 7:37:15 PM
Last Modified:	Monday, February 26, 2018 7:40:15 PM
Time Spent:	00:02:59
IP Address:	72.34.102.48

Page 1

Q1 Please enter your contact information here:

Name	**Elizabeth**
Address	**250 friedell street**
City	**San Francisco**
State	**Ca**
ZIP	**94124**
Email Address	**elizabethfineteacher@gmail.com**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

There seems to be more questions than answers. Im not certain we know the true results of the testing and its unclear as to whether its safe to live here.

Q3 What effects have site operations had on the surrounding community?

None

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

Yes. People do not believe it is safe to live herd.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

No

Q6 Do you feel well informed about the site's activities and progress?

No

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

Yes

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

Newspapers, local news, Facebook

#2

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Monday, February 26, 2018 7:37:04 PM
Last Modified:	Monday, February 26, 2018 7:46:40 PM
Time Spent:	00:09:36
IP Address:	72.34.103.125

Page 1

Q1 Please enter your contact information here:

Name	**David Springer**
Address	**150 Avocet Way**
City	**San Francisco**
State	**California**
ZIP	**94124**
Email Address	**dave.springer62@gmail.com**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

Total fraud. The cleanup was rushed and botched and fraudulent so that Lennar could make a fast buck and the city could start collecting taxes.

Q3 What effects have site operations had on the surrounding community?

Engender a lot of mistrust. The site operations keep feeding us a bunch of obviously sanitized PR messages. No transparency at all.

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

Most of the people in the Bayview are very concerned about health issues caused by toxicity in the Hunter's Point Shipyard.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

There is a regular, but low-level of criminal activity here, but the most pressing concern is abandoned vehicles and homelessness.

Q6 Do you feel well informed about the site's activities and progress?

I feel like we are fed a bunch of PR releases that are not based on truth. This latest TetraTech fraud has cast the Navy and Lennar as very duplicitous.

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

Get some people here who will speak transparently and directly to the issues that the residents and community members ask about. Thing like, how can the build-out get back on track, in spite of this fraud? How will the Navy and Lennar take ownership of this current issue of fraudulent soil sampling? It would be a huge gesture of goodwill if Lennar paid current owners damages based on how home values have been negatively affected by this scandal.

This latest issue has many of us regretting our purchases here in the Shipyard. And the current home-owners are either Lennar's best or worst advertising.

So: take ownership of this situation. Don't pass the buck or blame someone else. Be mature and thoughtful. Both Lennar and the Navy need to do this.

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

Yes! Provide some transparency and claim some ownership of the current fraudulent soil sample issue. Talk about how this is being resolved. Be truthful. Stop with the bogus PR stunts.

#3

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Monday, February 26, 2018 7:37:27 PM
Last Modified:	Monday, February 26, 2018 8:01:23 PM
Time Spent:	00:23:55
IP Address:	72.34.102.159

Page 1

Q1 Please enter your contact information here:

Name	**Hazel Bautista-Romero**
Address	**451 Donahue Street, Unit 403**
City	**San Francisco**
State	**CA**
ZIP	**94124**
Email Address	**hazel124@gmail.com**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

First of all, I was already in the impression that the site is cleaned up and that a trusted company was able to test it and declared it to be “safe”. I am very disappointed with the turn-out and I would like to see REAL work being done AND making sure that they are also transparent with the residents in the area.

Q3 What effects have site operations had on the surrounding community?

Although some efforts of precaution has been made, this is not enough for the community. I would like to see more efforts in making sure that we go beyond precautions and that we attain the goal of making sure that the area is a safe environment for all.

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

Not recently but I know people, who used to live in this area, suffered consequences of the radioactive material that was released in the environment.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

Yes, there were a few vandalism which included: breaking into cars (inside a garage), packages being stolen, and individuals walking in the neighborhood being robbed or treated with malicious intent such as throwing a water bottle to a passerby.

Q6 Do you feel well informed about the site's activities and progress?

My community has been really good in informing and communicating with us about different developments that occur in our neighborhood.

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

None. This site is simple, visually well organized and easy to use.

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

I would like for the Navy to continue to open avenues for communication to build better relationship with the community.

#4

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Monday, February 26, 2018 9:22:17 PM
Last Modified:	Monday, February 26, 2018 9:31:34 PM
Time Spent:	00:09:17
IP Address:	72.34.103.231

Page 1

Q1 Please enter your contact information here:

Name	**Jonathan Lee**
Organization	**SFUSD**
Address	**172 Coleman St**
City	**San Francisco**
State	**CA**
ZIP	**94124**
Email Address	**leej14@sfusd.edu**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

With all of the controversy surrounding tetra techs blatant falsification of data, my overall impression is of doubt. My wife and I have lived in the shipyard for a couple of years as some of the first occupants and we were hopeful that this could be a thriving community to raise our daughter. There are serious health concerns for the neighborhood, and the Navy needs to rectify this as soon as possible.

Q3 What effects have site operations had on the surrounding community?

Haven't really seen the Navy presence (or I am not aware of it), so the effect is a feeling of uncertainty whether anything is actually being done. The Navy could send notices to residents of the Shipyard to let us know when they are here doing work.

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

The community would like Parcel A to be retested to give everyone peace of mind.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

There are random thefts of packages from residences that are reported to local authorities, but that seems normal for San Francisco.

Q6 Do you feel well informed about the site's activities and progress?

Negative. Need more transparency about activity on site.

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

Retest Parcel A to give residents peace of mind and build trust again

---

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

Join the SF shipyard residents Facebook group and regularly post updates.

#5

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Monday, February 26, 2018 9:47:36 PM
Last Modified:	Monday, February 26, 2018 9:51:59 PM
Time Spent:	00:04:23
IP Address:	107.77.214.224

Page 1

Q1 Please enter your contact information here:

Name	**Cicely Tan**
Address	**555 Innes Avenue #303**
City	**San Francisco**
State	**California**
ZIP	**94124**
Email Address	**crumpie37@yahoo.com**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

Please retest Parcel A. Everyone says that it is safe but I need to know from the Navy and with recent tests. I am pregnant and want to be sure I am raising my child in a healthy environment. Thank you!!! My family and I appreciate it greatly. Please continue the residents and our requests as it is our lives in your hands.

Q3 What effects have site operations had on the surrounding community?

N/a

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

No concerns although I don't like to hear negative news about all his retesting. Just get it done please.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

No

Q6 Do you feel well informed about the site's activities and progress?

No, not at all

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

as mentioned, please retest Parcel A. This is my life and my family's first home.

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

Better communication and representation at community meetings.

#6

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Tuesday, February 27, 2018 7:04:03 AM
Last Modified:	Tuesday, February 27, 2018 7:12:11 AM
Time Spent:	00:08:07
IP Address:	72.34.103.171

Page 1

Q1 Please enter your contact information here:

Name	**Conor Mulherin**
Address	**50 Jerrold Ave**
City	**San Francisco**
State	**CA**
ZIP	**94124**
Email Address	**conor.mulherin@gmail.com**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

Disappointed that whistleblower claims were denied until obviously proven.

Q3 What effects have site operations had on the surrounding community?

Navy's actions are untrustworthy

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

Yes, there's concern in the community over the refusal to retest parcel A, to see minds

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

No

Q6 Do you feel well informed about the site's activities and progress?

Somewhat. Recent discoveries have impacted the sense of being informed.

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

Would like to understand the new cleanup timelines

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

The website and general comms from the navy are good in terms of method but there’s a loss of trust now in the overall process

---

#7

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Tuesday, February 27, 2018 12:03:25 PM
Last Modified:	Tuesday, February 27, 2018 1:02:40 PM
Time Spent:	00:59:14
IP Address:	159.45.186.46

Page 1

Q1 Please enter your contact information here:

Name	**Joseph Fraga**
Address	**207 Friedell Street**
City	**San Francisco**
State	**CA**
ZIP	**94124**
Email Address	**joseph7787@yahoo.com**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

More needs to be done and faster. The Navy response to the Tetra Tech whistleblowers and the subsequent Navy sample data review / report took too long. Given the reported issues with a high percentage of the samples by Tetra Tech, the Navy must move quickly to retest and remediate as needed.

Q3 What effects have site operations had on the surrounding community?

We see the occasional letter of notification that contaminated dust has been kicked up. The Navy must do a better job at containing contaminated dust due to it's operations.

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

The community is concerned with the radiological & other confirmation at the site, and ensuring it gets retested and remediated quickly for turnover to the city of SF. The amount of time for the Navy to move on these issues is especially concerning.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

I'm not aware of anything noted above.

Q6 Do you feel well informed about the site's activities and progress?

Marginally. The Navy should reach out more directly to the residents of the area- in particular the new SF Shipyards residents which live on the already turned over and built on land parcels at the Shipyard. Specifically the Navy could send updates to the Home Owners Association to then send out to the residents via email. A Quarterly update seems like a good idea noting how to contact the Navy and listing your website that has additional information on the cleanup, etc..

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

see question 6 on reaching out to the Residents

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

see question 6 on reaching out to the Residents

#8

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Tuesday, February 27, 2018 5:47:30 PM
Last Modified:	Tuesday, February 27, 2018 5:53:15 PM
Time Spent:	00:05:44
IP Address:	72.34.102.157

Page 1

Q1 Please enter your contact information here:

Name	**Jason Fried**
Title	**resident**
Organization	**Resident at the Shipyard**
Address	**451 Donahue**
City	**San Francisco**
State	**CA**
ZIP	**94124**
Email Address	**jasonlfried@hotmail.com**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

Not imopressed. Have been told for years everything is fine only to find out things are not fine

Q3 What effects have site operations had on the surrounding community?

The delays in all this means delays in getting the services we want out here.

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

Many of us who are concerned about what is in the ground and how long it will be before it is fixed. We are also concerned that everything we have been told about Parcel A, where we live, is not correct. Navy should do re-testing on Parcel A as well as the areas to help relieve concerns we have and future residents may have.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

No

Q6 Do you feel well informed about the site's activities and progress?

Not really. I learn more from the news and have a hard time getting real answers from Navy.

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

Need more transparency and getting all of the shipyard retested, even the parts that have already been turned over.

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

More meetings with people who can give real answers and not side step the concerns.

#9

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Tuesday, February 27, 2018 5:50:11 PM
Last Modified:	Tuesday, February 27, 2018 5:59:42 PM
Time Spent:	00:09:31
IP Address:	174.7.68.88

Page 1

Q1 Please enter your contact information here:

Name	**Christina Laffin**
Address	**451 Donahue St. Unit 507**
City	**San Francisco**
State	**CA**
ZIP	**94124**
Email Address	**Christina.Laffin@ubc.ca**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

I am concerned with the lack of transparency and evidence of fraudulent results. As someone who purchased a home recently in this area, I worry about health and safety issues and, to a lesser extent, impact on property values.

Q3 What effects have site operations had on the surrounding community?

The failure to address doubts about the clean-up process in a thorough and timely manner has sown discord and lack of trust among residents.

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

Yes, there is general concern and doubt among residents about the veracity and reliability of testing.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

Only the fraudulent test results outlined by the media which are of crucial importance and yet remain largely unaddressed from the perspective of residents.

Q6 Do you feel well informed about the site's activities and progress?

No. There is a general lack of clarity about how soon things will progress and what will be redone/retested to ensure clean-up has been done thoroughly and correctly.

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

Spend the time and money necessary to make sure the clean-up is carried out thoroughly while communicating a clear time-line that is actually followed.

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

Yes, since media sources seem to provide the most up-to-date information, communicate to media outlets regularly and openly.

#10

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Tuesday, February 27, 2018 6:08:33 PM
Last Modified:	Tuesday, February 27, 2018 6:19:05 PM
Time Spent:	00:10:31
IP Address:	199.212.218.22

Page 1

Q1 Please enter your contact information here:

Name	**Alex Deschamps**
Address	**551 Hudson Avenue, #203**
City	**SAN FRANCISCO**
State	**California**
ZIP	**94124**
Email Address	**hladeschamps@gmail.com**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

My overall impression is that the Tetra Tech clean up was falsified and we have been mislead for years to believe that all land has been clean and is ready for residential use. As a homeowner in the Shipyard I am very troubled by the lack of transparency around the clean up and do not feel safe for me our my family. I would hope that Parcel A would be retested to confirm the soil to be at safe levels, but have little hope that anyone of authority will initiate such a study on parcel A.

Q3 What effects have site operations had on the surrounding community?

The Shipyard lack adequate amenities to be consider a viable residential neighborhood. I purchased my home with the understanding of this, but that such amenities would be part of later phases. Delays caused by the falsified studies only cause me to live in an area that cannot satisfy a families day to day needs.

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

There have been numerous reports of falsified soil samplings and the mere fact I am filling out this survey only further stresses that something was handled improperly.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

n/a

Q6 Do you feel well informed about the site's activities and progress?

No

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

Retesting of parcel A would reaffirm the stance that it is safe for residential use.

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

Yes, more transparency as to the status and results of testing and action plans to remedy any errors so we can get development back on schedule.

#11

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Tuesday, February 27, 2018 6:23:59 PM
Last Modified:	Tuesday, February 27, 2018 6:30:18 PM
Time Spent:	00:06:19
IP Address:	50.203.12.50

Page 1

Q1 Please enter your contact information here:

Name	**Jenna Hansen**
Title	**Director of Product**
Organization	**Taylor Stitch**
Address	**50 Jerrold Avenue, Unit 406**
City	**San Francisco**
State	**CA**
ZIP	**94124**
Email Address	**jennahansen312@gmail.com**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

Terrible - I have no trust.

Q3 What effects have site operations had on the surrounding community?

Lost all trust in the integrity.

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

Yes, as a resident I'm very aware of the continue falsification. I demand that Parcel A be tested.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

Yes, there was a drive-by shooting at Innes & Jerrold the first week I moved in. There have been cars broken into in private garages. Multiple packages stolen.

Q6 Do you feel well informed about the site's activities and progress?

I have to seek out the information. The progress is very ambiguous.

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

TEST PARCEL A to dismiss the speculation that it's also contaminated. People including myself are living there!

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

Yes - put up signs around the Shipyard to notify everyone of the upcoming meetings. Make a facebook group. Attend every master's meeting with updates.

#12

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Tuesday, February 27, 2018 6:28:25 PM
Last Modified:	Tuesday, February 27, 2018 6:41:15 PM
Time Spent:	00:12:50
IP Address:	50.232.37.10

Page 1

Q1 Please enter your contact information here:

Name	**Anil Vittal**
Title	**Business Operations Manager**
Organization	**Tile**
Address	**570 Innes Ave #302**
City	**San Francisco**
State	**California**
ZIP	**94124**
Email Address	**avittal86@gmail.com**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

Awful. I don't have a great idea of what is safe and what isn't. I have no idea how long it is going to take to clean up the Shipyard. They say Parcel A is safe...but how do I know for sure?

Q3 What effects have site operations had on the surrounding community?

My day to day isn't affected.

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

No one understands anything that is going on. The Navy had a meeting a few weeks ago for Shipyard residents and each station or booth we went to had different people saying different things. No one knew the big picture they only knew a bit about their section. Once the protesters came the residents were ignored.

All we know is that Tetra falsified reports and there is still clean up going on. We don't know if things are still contaminated, how long it will take, or any other additional information.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

Not that I know of.

Q6 Do you feel well informed about the site's activities and progress?

Absolutely not. The Navy has done a terrible job of informing us. Beyond terrible. Other than the basics no one has any idea of what is going on.

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

Tell us what is going on. Have one point of contact that comes down and explains to all the Lennar residents what is happening and have them answer any questions that we have. Like I said above, the Navy came before but there wasn't any one person that knew the whole story. Also, a lot of those people didn't have answers to many of our questions.

I can't explain how frustrated I am by this whole process. It has been beyond terrible.

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

YES!!!!

-Have one person hold a town hall type meeting for the residents of Lennar. Please make sure that person knows what they are talking about and has a good idea of the whole story. Have this person prepared to be here for a couple of hours at least. The residents here are owed that much.

-Continue to send updates on where you are in the process of the cleanup (email or mail)

-Update us on if you found anything alarming

-Give us some tentative timelines on when you expect to be done with testing of each parcel

---

#13

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Tuesday, February 27, 2018 7:27:27 PM
Last Modified:	Tuesday, February 27, 2018 7:34:30 PM
Time Spent:	00:07:02
IP Address:	72.34.102.186

Page 1

Q1 Please enter your contact information here:

Name	**RILEY M SMITH**
Address	**451Donahue Street**
City	**SAN FRANCISCO**
State	**CA**
ZIP	**94124**
Email Address	**riley.smith23@gmail.com**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

It's being done transparently (as compared to the Tetra Tech) mishaps. I have confidence in what has been described to me in in-person meetings, but can not be 100% confident considering I'm not on the ground day-to-day.

Q3 What effects have site operations had on the surrounding community?

It's delay in clean-up, from my understanding, has delayed the hand-over to the City, pushing development of Phase 2 back. This affects and speed of which people move here and the resulting community. Construction of the development proves to have a larger daily effect than the work done on the Navy property.

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

N/A

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

N/A

Q6 Do you feel well informed about the site's activities and progress?

Adequately. With the recent SF Curbed article and past Tetra Tech efforts, it is important that the Navy continue to build awareness and listening sessions for current residents. My biggest concern is that a) somehow Parcel A was not tested adequately, b) that Parcel A actually has above normal radiation, and c) consequently, the negative press affects our community development and our individual property values.

Your ability to communicate this out and show progress helps qualm these 3 concerns. Any time you question whether you're doing enough, side on doing more.

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

Do it correctly; overshare; be transparent; do it as quickly as possible w/o doing it incorrectly; and make sure our community can flourish.

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

NA

#14

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Tuesday, February 27, 2018 7:53:03 PM
Last Modified:	Tuesday, February 27, 2018 8:01:12 PM
Time Spent:	00:08:09
IP Address:	72.34.103.87

Page 1

Q1 Please enter your contact information here:

Name	**Susan Campbell**
Address	**50 Jerrold Avenue #213**
City	**San Francisco**
State	**CA**
ZIP	**94124**
Email Address	**soupy50@yahoo.com**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

Moved here one year ago- unclear about cleanup work.

Q3 What effects have site operations had on the surrounding community?

Again, unclear.

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

I've spoken to a few people- most everyone wants a clean environment to live in. Safe for all.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

No

Q6 Do you feel well informed about the site's activities and progress?

Somewhat

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

Like everyone I've spoken to - I want a clean, safe living environment .

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

Meetings, and email communications.

#15

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Tuesday, February 27, 2018 8:57:01 PM
Last Modified:	Tuesday, February 27, 2018 9:09:14 PM
Time Spent:	00:12:12
IP Address:	72.34.102.172

Page 1

Q1 Please enter your contact information here:

Name **Paloma**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

Very concerning as a new shipyard resident and home owner. First and foremost we want to ensure our health is not being affected by living here. Secondary the clean up needs to be completed correctly asap so the development can continue to flourish. Its not attractive for businesses or other home owners to move out here the level of uncertainty surrounding the toxic clean up.

Q3 What effects have site operations had on the surrounding community?

disruption, noise, parking issues, dust in homes

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

the community is concerned on any levels of radiation or other toxic, life threatening issues.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

yes there has been theft and vandalism inside the Merchant building (451 Donahue St). We've had car break ins inside the merchant garage and also looters stealing mail packages.

Q6 Do you feel well informed about the site’s activities and progress?

no

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

Let the residents of the community have a voice that actually matters. We are aware of meetings, but these meetings rarely area chance for people's opinions to be taken into consideration.

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

Yes, send emails with a google calendar link

#16

COMPLETE

Collector:	Web Link 1 (Web Link)
Started:	Wednesday, February 28, 2018 11:04:37 AM
Last Modified:	Wednesday, February 28, 2018 11:17:33 AM
Time Spent:	00:12:56
IP Address:	75.37.27.97

Page 1

Q1 Please enter your contact information here:

Name	**Micharl Hamman**
Organization	**IBNA, EDOT**
Address	**702 Earl Street**
City	**San Francisco**
State	**CA**
ZIP	**94124**
Email Address	**mhamman@igc.org**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

Slow, slower that it should be. This project should have been completed years ago.

Q3 What effects have site operations had on the surrounding community?

Few effects

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

a.) How could the Navy allow such a massive fraud. Why are not the guilty parties going to jail? What steps have been taken (if any) to prevent this from happening again?

b.) What other assurance does the Navy have that the clean up was actually done correctly other than the fraudulent test results for Tetra-Tech? Was there any other supervision of the clean up work? Did the Navy not have it's own staff observing this work? If not why not?

c.) Why is the retesting not being done in an expedited manor? Why will it take so long to retest the site?

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

No

Q6 Do you feel well informed about the site's activities and progress?

Yes

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

This project is so far behind the original schedule that the remaining work should be done on an "emergency" basis and completed a quickly as is possible. This community has been put on hold long enough and needs to get on with it's life. The projected schedule for completion of the clean-up and transfer is unacceptable.

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

No

#17

COMPLETE

Collector: Web Link 1 (Web Link)
Started: Wednesday, February 28, 2018 11:21:13 AM
Last Modified: Wednesday, February 28, 2018 11:38:19 AM
Time Spent: 00:17:05
IP Address: 23.118.69.85

Page 1

Q1 Please enter your contact information here:

Name	**Bodo Klawonn**
Address	**555 Innes Ave #214**
City	**San Francisco**
State	**CA**
ZIP	**94124**
Email Address	**bodoklawonn@gmail.com**

Q2 What is your overall impression of the cleanup work conducted at Hunters Point Naval Shipyard (HPNS) over the period of the fourth five-year review (2013 to present)?

Needs to improve accuracy of soil testing.

Q3 What effects have site operations had on the surrounding community?

Have not notice any side effects.

Q4 Are you aware of any community concerns regarding the site or its operation and maintenance? If so, please give details.

Yes, the soil testing was falsified.

Q5 Are you aware of any events, incidents, or activities that have occurred at the site, such as vandalism, trespassing, or anything that required emergency response from local authorities? If so, please give details.

NO

Q6 Do you feel well informed about the site's activities and progress?

Not enough information is coming forward regarding the toxicity of the super fund site.

Q7 Do you have any comments, suggestions, or recommendations regarding the site?

Please have Parcel A retested as it affects my neighborhood.

Q8 Are there ways that the Navy can better communicate with the local community? If you answer is "yes", please provide your suggestions.

Yes thru social media and outreach.

Appendix C. Site Inspection Checklists and Photographic Logs

Appendix C. Site Inspection Checklist and Photographic Logs

Appendix C1. Site Inspection Checklist

FIVE-YEAR REVIEW SITE INSPECTION CHECKLIST

I. SITE INFORMATION	
Site Name: Hunters Point Naval Shipyard	**Date of Inspection:** January 29, 2018
Location and Region: San Francisco, CA (EPA Region 9)	**EPA ID:** CA1170090087
Agency, Office, or Company leading the Five-Year Review: Department of the Navy	**Weather/Temperature:** Partly Cloudy, 58°F

Remedy Includes: (Check all that apply)

☒ Landfill cover/containment
☒ Access controls
☒ Institutional controls
☐ Groundwater pump and treatment
☒ Groundwater monitoring
☒ Monitored natural attenuation
☐ Groundwater containment
☐ Vertical barrier walls
☐ Surface water collection and treatment
☒ Other: Cover/containment remedies apply at multiple parcels; however, they are not traditional landfill caps (except for Parcel E-2). Durable cover remedies are completed for IR-07/IR-18 and Parcels B-1, B-2, C, G, UC-1, UC-2, and UC-3. Other parcels (D-1, E, and E-2) are in varying stages of planning or construction. Other remedies include SVE and in-situ groundwater treatment using ZVI injection, aerobic ISB, and/or anaerobic ISB.

This inspection only focuses on the sites with completed durable cover remedies, except for Parcels UC-1 and UC-2 (both are actively under construction by a non-Navy redevelopment contractor).

Attachments: ☐ Inspection team roster attached ☒ Site map attached

II. INTERVIEWS (Check all that apply)

A. O&M Site Manager

John Sourial, PE (IEJV)	Project Manager	01/29/18
Name	Title	Date

Interviewed: ☒ at site ☐ at office ☐ by phone Phone No. 415-848-7103

☐ Report Attached:

Problems or suggestions: None

B. O&M Staff

Steven Hoeft, PE (IEJV)	Project Engineer	01/29/18
Name	Title	Date

Interviewed: ☒ at site ☐ at office ☐ by phone Phone No. 415-848-7109

☐ Report attached:

Problems or suggestions: None

C. Local Regulatory Authorities and Response Agencies (i.e., State and Tribal offices, emergency response office, police department, office of public health or environmental health, zoning office, recorder of deeds, or other city and county offices, etc.) Fill in all that apply.

Agency: San Francisco Department of Public Health

Contact: Amy Brownell	Environmental Engineer	2/22/18	415-252-3967
Name	Title	Date	Phone No.

Interviewed: ☐ at site ☒ at office ☐ by phone

☒ Report attached: See Appendix A

Problems or suggestions: See Appendix A

D. Other interviews

Community residents, EPA, DTSC, and Water Board

☒ Report attached: See Appendix A

III. ON-SITE DOCUMENTS & RECORDS VERIFIED (Check all that apply)

A. O&M Documents

☒ O&M plan	☒ Readily available	☒ Up to date	☐ N/A
☒ As-built drawings	☒ Readily available	☒ Up to date	☐ N/A
☒ Maintenance logs	☒ Readily available	☒ Up to date	☐ N/A

Remarks: Documents are available in the Administrative Record and in the offices of the O&M contractors.

B. Site-Specific Health and Safety Plan ☒ Readily available ☒ Up to date ☐ N/A

☐ Contingency plan/emergency response plan	☐ Readily available	☐ Up to date	☒ N/A

Remarks: SSHPs confirmed for contractors with continuous site presence.

C. O&M and OSHA Training Records ☒ Readily available ☒ Up to date ☐ N/A

Remarks: OSHA training records confirmed for contractors with continuous site presence.

D. Permits and Service Agreements

☐ Air discharge permit	☐ Readily available	☐ Up to date	☒ N/A
☐ Effluent discharge	☐ Readily available	☐ Up to date	☒ N/A
☐ Waste disposal, POTW	☐ Readily available	☐ Up to date	☒ N/A
☐ Other permits_____	☐ Readily available	☐ Up to date	☒ N/A

Remarks: None

E. Gas Generation Records ☐ Readily available ☐ Up to date ☒ N/A

Remarks: None

F. Settlement Monument Records ☒ Readily available ☒ Up to date ☐ N/A

Remarks: Multiple settlement monuments have been installed at parcels with completed durable cover remedies. Survey results are published in documents available in the Administrative Record.

G. Groundwater Monitoring Records ☒ Readily available ☒ Up to date ☐ N/A

Remarks: Historical groundwater monitoring records are readily available in the Administrative Record.

H. Leachate Extraction Records ☐ Readily available ☐ Up to date ☒ N/A

Remarks:

I. Discharge Compliance Records

☐ Air	☐ Readily available	☐ Up to date	☒ N/A
☐ Water (effluent)	☐ Readily available	☐ Up to date	☒ N/A

Remarks:

J. Daily Access/Security Logs ☐ Readily available ☐ Up to date ☒ N/A

Remarks: Guarded security gates at Robinson Street and Crisp Road restrict access to HPNS. City of San Francisco provides security and maintains access logs. The Navy also employs security companies to perform roving patrols.

IV. O&M COSTS

A. O&M Organization

☐ State in-house ☐ Contractor for State

☐ PRP in-house ☐ Contractor for PRP

☐ Federal Facility in-house ☒ Contractor for Federal Facility

☒ Other

Remarks: O&M on Navy property is currently performed by contractors employed by the Navy. O&M on non-Navy property is performed by contractors employed by CCSF's developer.

B. O&M Cost Records

☐ Readily available ☒ Up to date

☒ Funding mechanism/agreement in place
Original O&M cost estimate: Not Available

Costs for O&M performed by Navy contractors aligns with the budgets set aside by the Navy for that work. Costs for O&M non-Navy parcels were not readily available for review.

C. Unanticipated or Unusually High O&M Costs During Review Period

Describe costs and reasons: None

V. ACCESS AND INSTITUTIONAL CONTROLS ☒ Applicable ☐ N/A

A. Fencing

☐ Fencing damaged ☐ Location shown on site map ☒ Gates secured ☐ N/A

Remarks: The overall perimeter of HPNS and each parcel boundary is controlled by chain-link fence and gates. All fencing was inspected and found to be generally in good condition.

B. Other Access Restrictions

☒ Signs and other security measures ☐ Location shown on site map ☐ N/A

Remarks: Signs are posted around the perimeter of each parcel to warn against ground disturbance. Additionally, signs are posted throughout HPNS warning of hazardous materials and/or radioactive hazards. All signs are intact and in good condition.

C. Institutional Controls (ICs)

1. **Implementation and enforcement**

Site conditions imply ICs not properly implemented ☐ Yes ☒ No ☐ N/A

Site conditions imply ICs not being fully enforced ☐ Yes ☒ No ☐ N/A

Type of monitoring (e.g., self-reporting, drive by): Routine inspection

Frequency: Annually

Responsible party/agency: Navy and Navy O&M contractors

Contact:			
John Sourial, PE (IEJV)	Project Manager	1/15/18	415-848-7103
Name	Title	Date	Phone No.

Reporting is up-to-date	☒ Yes	☐ No	☐ N/A
Reports are verified by the lead agency	☒ Yes	☐ No	☐ N/A
Specific requirements in deed or decision documents have been met	☒ Yes	☐ No	☐ N/A
Violations have been reported	☐ Yes	☒ No	☐ N/A

Other problems or suggestions: ☐ Report attached

IC compliance reports for IR-07/IR-18 and Parcels B-1, B-2, C, and G found IC elements in compliance. These reports are included in the Administrative Record.

2. **Adequacy** ☒ ICs are adequate ☐ ICs are inadequate ☐ N/A

Remarks: None

D. General

1. **Vandalism/trespassing** ☐ Location shown on site map ☒ No vandalism evident

Remarks: No vandalism/trespassing evident during the site inspection; however, fence breaches and theft are common at HPNS. Remedies are typically not affected by common acts of vandalism/trespassing.

2. **Land use changes on site** ☒ N/A

Remarks:

3. **Land use changes off site** ☒ N/A

Remarks:

VI. GENERAL SITE CONDITIONS

A. Roads ☒ Applicable ☐ N/A

Roads damaged ☐ Location shown on site map ☒ Roads adequate ☐ N/A

Remarks: Roads are generally in good condition and are maintained by O&M contractors where durable cover remedies have been installed.

B. Other Site Conditions

Remarks: Some minor trash accumulation and weeds are present; however, they are addressed during periodic maintenance events.

VII. COVERS ☐ Applicable ☐ N/A

(Inspected durable covers at IR-07/IR-18 and Parcels B-1, B-2, C, G, and UC-3)

A. Cover Surface

1. **Settlement** (Low spots) ☐ Location shown on site map ☒ Settlement not evident

Areal extent _____ Depth _____ No settlement _____

Remarks:

2. **Cracks** ☐ Location shown on site map ☒ Cracking not evident

Lengths _____ Widths _____ Depths _____

Remarks: Some minor cracking observed in Parcels B-1 and UC-3 due to heavy traffic (see Appendix D2 and Appendix D-6, respectively); however, the cover still adequately prevents exposure to underlying soil. The cracks are monitored and addressed during periodic maintenance events.

3.	**Erosion**	☐ Location shown on site map	☒ Erosion not evident
	Areal extent _____ Depth _____		
	Remarks: Erosion from storm events is not evident.		
4.	**Holes**	☐ Location shown on site map	☒ Holes not evident
	Areal extent _____ Depth _____		
	Remarks: Some minor burrow holes were observed in Parcels B-1 and C (see Appendix D2 and Appendix D-4, respectively); however, they were observed to extend only a few inches below the surface. The holes are monitored and repaired during periodic maintenance events.		
5.	**Vegetative Cover**	☒ Grass	☒ Cover properly established ☒ No signs of stress
	☐ Trees/Shrubs (indicate size and locations on a diagram)		
	Remarks: Vegetation is generally well established. A small bare spot was observed in IR-07/IR-18 (see Appendix D-1). Any bare spots are seeded during periodic O&M events.		
6.	**Alternative Cover (armored rock, concrete, etc.)**	☐ N/A	
	Remarks: Riprap revetment and armoring is in good condition. Concrete utility corridors, secured manholes, and monitoring well lids have also been incorporated into the durable cover and are in good condition. Some concrete sidewalks in Parcel UC-3 were observed to be cracked (see Appendix D-6); however, the cover still adequately prevents exposure to underlying soil.		
7.	**Bulges**	☐ Location shown on site map	☒ Bulges not evident
	Areal extent _____ Height _____		
	Remarks:		
8.	**Wet Areas/Water Damage**	☐ Wet areas/water damage not evident	
	☐ Wet areas	☐ Location shown on site map	Areal extent_____
	☒ Ponding	☐ Location shown on site map	Areal extent_____
	☐ Seeps	☐ Location shown on site map	Areal extent_____
	☐ Soft subgrade	☐ Location shown on site map	Areal extent_____
	Remarks: The only ponding that was observed during the inspection was within a swale in Parcel B-1 (see Appendix D2); however, ponding has also been observed during storm events over mild depressions in paved areas within all parcels. These areas are monitored for damage during periodic inspections.		
9.	**Slope Instability**	☐ Slides ☐ Location shown on site map	☒ No evidence of slope instability
	Areal extent _____		
	Remarks:		
B.	**Benches**	☐ Applicable	☒ N/A
	(Horizontally constructed mounds of earth placed across a steep landfill side slope to interrupt the slope in order to slow down the velocity of surface runoff and intercept and convey the runoff to a lined channel.)		
1.	**Flows Bypass Bench**	☐ Location shown on site map	☒ N/A or okay
	Remarks:		
2.	**Bench Breached**	☐ Location shown on site map	☒ N/A or okay
	Remarks:		

3.	**Bench Overtopped**	☐ Location shown on site map	☒ N/A or okay
	Remarks:		
C.	**Letdown Channels**	☒ Applicable	☐ N/A
	(Channel lined with erosion control mats, riprap, grout bags, or gabions that descend down the steep side slope of the cover and will allow the runoff water collected by the benches to move off of the landfill cover without creating erosion gullies.)		
	Remarks: In IR-07/IR-18, a drainage channel exists along the toe of the steeply sloped portion in the southwest corner and was observed to be in good condition (Appendix D-1).		
1.	**Settlement**	☐ Location shown on site map	☒ No evidence of settlement
	Areal extent _____ Depth _____		
	Remarks:		
2.	**Material Degradation**	☐ Location shown on site map	☒ No evidence of degradation
	Material type _____ Areal Extent _____		
	Remarks:		
3.	**Erosion**	☐ Location shown on site map	☒ No evidence of erosion
	Areal extent _____ Depth _____		
	Remarks:		
4.	**Undercutting**	☐ Location shown on site map	☒ No evidence of undercutting
	Areal extent _____ Depth _____		
	Remarks:		
5.	**Obstructions**	☐ Location shown on site map	☒ No obstructions
	Type _____ Areal Extent _____ Size _____		
	Remarks:		
6.	**Excessive Vegetative Growth**	☐ Location shown on site map	☒ No evidence of excessive growth
	☐ Vegetation in channels does not obstruct flow		
	Type _____ Areal extent _____		
	Remarks:		
D.	**Cover Penetrations**	☒ Applicable	☐ N/A
1.	**Gas Vents**		
	☐ Active	☐ Passive	☐ Properly secured/locked
	☐ Functioning	☐ Routinely sampled	☐ Good condition
	☐ Evidence of leakage at penetration	☐ Needs Maintenance	☒ N/A
	Remarks:		

2.	**Gas Monitoring Probes**		
	☐ Properly secured/locked	☒ Functioning	☐ Routinely sampled
	☒ Good condition	☐ Evidence of leakage at penetration	
	☐ Needs Maintenance	☐ N/A	
	Remarks: Gas monitoring probes located in Parcel B-1 (Building 123) and Parcel C and are in good condition.		
3.	**Monitoring Wells** (within surface area of landfill)		
	☒ Properly secured/locked	☒ Functioning	☒ Routinely sampled
	☒ Good condition	☐ Evidence of leakage at penetration	
	☐ Needs Maintenance	☐ N/A	
	Remarks: Monitoring wells are located in every parcel and are generally in good condition. Wells are maintained under the BGMP. Well surface completions are maintained under the O&M programs in areas where durable covers are present.		
4.	**Leachate Extraction Wells**		
	☐ Properly secured/locked	☐ Functioning	☐ Routinely sampled
	☐ Good condition	☐ Evidence of leakage at penetration	
	☐ Needs Maintenance	☒ N/A	
	Remarks:		
5.	**Settlement Monuments**	☒ Located	☒ Routinely surveyed ☐ N/A
	Remarks: None		
E.	**Gas Collection and Treatment**	☐ Applicable	☒ N/A
1.	**Gas Treatment Facilities**		
	☐ Flaring	☐ Thermal destruction	☐ Collection for reuse
	☐ Good condition	☐ Needs Maintenance	☒ N/A
	Remarks:		
2.	**Gas Collection Wells, Manifolds and Piping**		
	☐ Good condition	☐ Needs Maintenance	
	Remarks:		
3.	**Gas Monitoring Facilities** (e.g., gas monitoring of adjacent homes or buildings)		
	☐ Good condition	☐ Needs Maintenance	☒ N/A
	Remarks:		
F.	**Cover Drainage Layer**	☐ Applicable	☒ N/A
1.	**Outlet Pipes Inspected**	☐ Functioning	☒ N/A
	Remarks:		
2.	**Outlet Rock Inspected**	☐ Functioning	☒ N/A
	Remarks:		

G. Detention/Sedimentation Ponds ☐ Applicable ☒ N/A	
1. **Siltation** Areal extent _____ Depth _____ ☒ N/A ☐ Siltation not evident Remarks:	
2. **Erosion** Areal extent _____ Depth _____ ☐ Erosion not evident Remarks:	
3. **Outlet Works** ☐ Functioning ☒ N/A Remarks:	
4. **Dam** ☐ Functioning ☒ N/A Remarks:	
H. Retaining Walls ☒ Applicable ☐ N/A	
1. **Deformations** ☐ Location shown on site map ☐ Deformation not evident Horizontal displacement _____ Vertical displacement_____ Rotational displacement _____ Remarks: Retaining walls are located in IR-07/IR-18 and Parcel B-1 (see Appendix D-1 and Appendix D-2, respectively). Both retaining walls are intact and in good condition.	
2. **Degradation** ☐ Location shown on site map ☐ Degradation not evident Remarks: None	
I. Perimeter Ditches/Off-Site Discharge ☒ Applicable ☐ N/A Remarks: Swales are located in IR-07/IR-18 and Parcels B-1, B-2, C, and G.	
1. **Siltation** ☐ Location shown on site map ☐ Siltation not evident Areal extent _____ Depth _____ Remarks: Minor sediment/debris accumulation occurs in the drainage swales and is cleaned out during periodic maintenance events.	
2. **Vegetative Growth** ☐ Location shown on site map ☐ N/A ☒ Vegetation does not impede flow Areal extent _____ Type _____ Remarks: The only vegetation-lined swale is located in the northeastern corner of IR-07/IR-18 (see Appendix D-1). The vegetation does not impede flow, and the swale is functioning as intended.	
3. **Erosion** ☐ Location shown on site map ☒ Erosion not evident Areal extent _____ Depth _____ Remarks:	

4. **Discharge Structure** ☒ Functioning ☐ N/A

Remarks: Outfalls to SF Bay are located in Parcels B-1, B-2, and C. Outfalls are functioning as intended.

VIII. VERTICAL BARRIER WALLS ☐ Applicable ☒ N/A

1. **Settlement** ☐ Location shown on site map ☐ Settlement not evident

Areal extent _____ Depth _____

Remarks:

2. **Performance Monitoring** Type of monitoring_____

☒ Performance not monitored

Frequency _____ ☐ Evidence of breaching

Head differential _____

Remarks:

IX. GROUNDWATER/SURFACE WATER REMEDIES ☒ Applicable ☐ N/A

A. Groundwater Extraction Wells, Pumps, and Pipelines ☐ Applicable ☒ N/A

1. **Pumps, Wellhead Plumbing, and Electrical**

☐ Good condition ☐ All required wells properly operating ☐ Needs Maintenance

Remarks:

2. **Extraction System Pipelines, Valves, Valve Boxes, and Other Appurtenances**

☐ Good condition ☐ Needs Maintenance

Remarks:

3. **Spare Parts and Equipment**

☐ Readily available ☐ Good condition ☐ Requires upgrade ☐ Needs to be provided

Remarks:

B. Surface Water Collection Structures, Pumps, and Pipelines ☐ Applicable ☒ N/A

1. **Collection Structures, Pumps, and Electrical**

☐ Good condition ☐ Needs Maintenance

Remarks:

2. **Surface Water Collection System Pipelines, Valves, Valve Boxes, and Other Appurtenances**

☐ Good condition ☐ Needs Maintenance

Remarks:

3. **Spare Parts and Equipment**

☐ Readily available ☐ Good condition ☐ Requires upgrade ☐ Needs to be provided

Remarks:

C. Treatment System	☐ Applicable	☒ N/A

1. **Treatment Train** (Check components that apply)

☐ Metals removal ☐ Oil/water separation ☐ Bioremediation

☐ Air stripping ☐ Carbon absorbers

☐ Filters _____

☐ Additive (*e.g.*, chelation agent, flocculent) _____

☐ Others _____

☐ Good condition ☐ Needs Maintenance

☐ Sampling ports properly marked and functional

☐ Sampling/maintenance log displayed and up to date

☐ Equipment properly identified

☐ Quantity of groundwater treated annually _____

☐ Quantity of surface water treated annually _____

Remarks:

2. **Electrical Enclosures and Panels** (properly rated and functional)

☐ Good condition ☐ Needs Maintenance

Remarks:

3. **Tanks, Vaults, Storage Vessels**

☐ Good condition ☐ Proper secondary containment ☐ Needs Maintenance

Remarks:

4. **Discharge Structure and Appurtenances**

☐ Good condition ☐ Needs Maintenance

Remarks:

5. **Treatment Building(s)**

☐ Good condition (esp. roof and doorways) ☐ Needs repair

☐ Chemicals and equipment properly stored

Remarks:

D. Monitoring Data

1. **Monitoring Wells**

☒ Properly secured/locked ☒ Functioning ☒ Routinely sampled ☒ Good condition

☒ All required wells located ☐ Needs Maintenance

Remarks:

2. **Monitoring Data**

☒ Is routinely submitted on time ☒ Is of acceptable quality

Remarks: BGMP issues reports semiannually and approximately 6 months after sample collection.

3. **Monitoring data suggests:**

☐ Groundwater plume is effectively contained ☐ Contaminant concentrations are declining

Remarks: Collection of performance monitoring data for active treatment remedies in Parcel B-1 IR-10 and Parcel C is underway. No reports describing long-term remedy performance have been published to date.

E. Monitored Natural Attenuation

1. **Monitoring Wells** (natural attenuation remedy)

☒ Properly secured/locked ☒ Functioning ☒ Routinely sampled ☒ Good condition

☒ All required wells located ☐ Needs Maintenance

Remarks:

X. OTHER REMEDIES

If there are remedies applied at the site which are not covered above, attach an inspection sheet describing the physical nature and condition of any facility associated with the remedy. An example would be soil vapor extraction.

Remarks: SVE systems are also located in Parcels B-1 and C. The only currently active SVE system is located within Parcel B-1, IR-10, although systems in Parcel C have been operated in the past. The system in IR-10 is functional.

XI. OVERALL OBSERVATIONS

A. Implementation of the Remedy

Describe issues and observations relating to whether the remedy is effective and functioning as designed. Begin with a brief statement of what the remedy is to accomplish (i.e., to contain contaminant plume, minimize infiltration and gas emission, etc.).

Durable covers have been installed in Parcels B-1, B-2, C, G, and UC-3 and IR-07/IR-18 to prevent or minimize exposure to soil and sediment and to prevent migration of sediment to SF Bay. The durable covers in these parcels are generally intact and functioning as intended.

Groundwater monitoring is performed across HPNS by the BGMP to support performance monitoring for groundwater remedies, including active remedies (e.g., ISB, ZVI) and MNA. Data are collected semiannually. The program collects data that are usable and of high quality and the well network is intact and functioning as intended.

ICs are implemented at Parcels B-1, B-2, C, G, and UC-3 and IR-07/IR-18 to prevent exposure to COCs and protect the completed remedies. LUC compliance monitoring is performed annually and has verified that no violations have occurred to date.

B. Adequacy of O&M

Describe issues and observations related to the implementation and scope of O&M procedures. In particular, discuss their relationship to the current and long-term protectiveness of the remedy.

Inspections reports verify that O&M procedures are adequately maintaining the performance of the remedies. The use of qualified professionals to perform the inspections and direct the maintenance ensures the long-term success of the O&M programs.

C. Early Indicators of Potential Remedy Problems

Describe issues and observations such as unexpected changes in the cost or scope of O&M or a high frequency of unscheduled repairs that suggest that the protectiveness of the remedy may be compromised in the future.

No early indicators of potential problems were identified.

D. Opportunities for Optimization
Describe possible opportunities for optimization in monitoring tasks or the operation of the remedy. The Navy switched to performing off-schedule (as-needed) O&M inspections and maintenance, rather than planned/scheduled inspections and maintenance on a set frequency in 2017. This approach has facilitated the implementation of the O&M programs. Maintenance activities can occur when optimal (e.g., mowing in May prior to fire hazard season, cleaning of swales in September prior to the start of the wet season). Recommend continued implementation of this approach to optimize remedy performance and lifespan.

Appendix C2. Photographic Log, IR Sites 07 and 18

Photograph C2-1: View of soil cover near revetment crest. Cover vegetation is generally well established and in good condition. No evidence of erosion, subsidence, or settlement observed. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-2: View of soil cover near revetment crest. Cover vegetation is generally well established and in good condition. No evidence of erosion, subsidence, or settlement observed. Facing southwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-3: View of soil cover in southwest corner of site. Cover vegetation is generally well established and in good condition. No evidence of erosion, subsidence, or settlement observed. Facing southwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-4: View of soil cover near Innes Avenue. Cover vegetation is generally well established and in good condition. No evidence of erosion, subsidence, or settlement observed. Facing northeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-5: View of soil cover near entrance gate. Cover vegetation is generally well established and in good condition. No evidence of erosion, subsidence, or settlement observed. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-6: View of soil cover near main gate. Cover vegetation is generally well established and in good condition. No evidence of erosion, subsidence, or settlement observed. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-7: View of soil cover near intersection of Galvez Avenue and Donahue Street. Small areas along the grass swale where the cover has been disturbed will require seeding during the next O&M event. Facing west.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-8: View of drainage channel north of Building 117. Channel is free of sediment and functioning as intended. Facing south.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-9: View of retaining wall. Retaining wall is stable with no evidence of settlement or cracking. Facing southwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

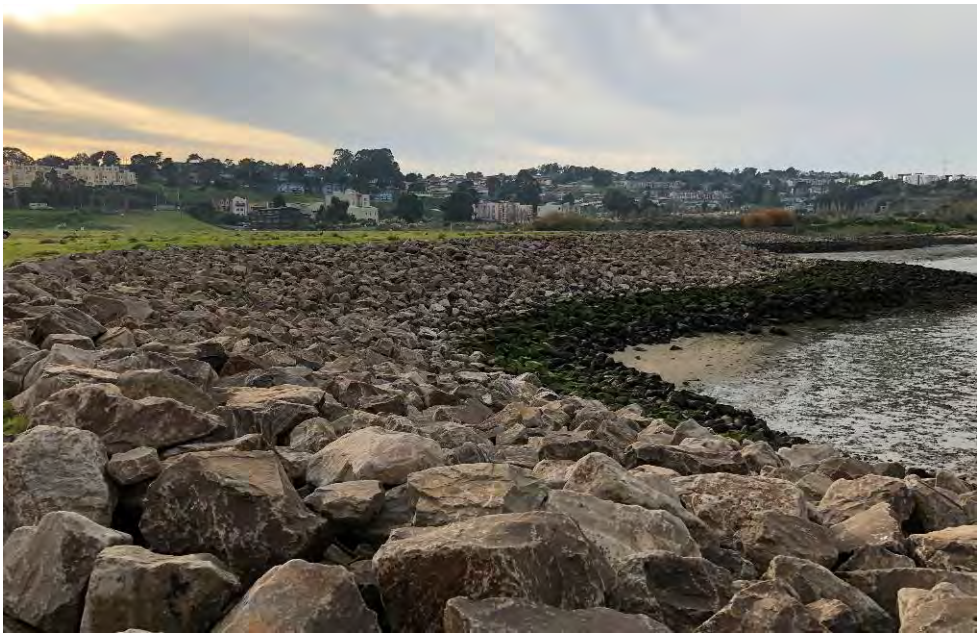

Photograph C2-10: View of shoreline revetment north of Building 117. Revetment is stable with no evidence of settlement or movement. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-11: View of shoreline revetment near non-Navy boundary. Revetment is stable with no evidence of settlement or movement. Facing southeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-12: View of durable asphaltic pavement at bump-out area north of Building 117. Cover is generally intact and in good condition. Minor cover damage caused by weed growth along fence line; typical of cover damage that is documented and addressed during periodic O&M repair events. Facing east.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-13: All warning signs are intact and legible with current BRAC contact information. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-14: Chain-link fence along Donahue Street is intact and in good condition. Facing northeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-15: Chain-link fence along non-Navy property is intact and in good condition. Facing southwest.
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California
Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-16: Monitoring well completions (typical) intact and in good condition.
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California
Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C2-17: Survey monument (typical) intact and in good condition.
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California
Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

2018-04-24 W:\2017\20170042_HPNS_Innovex_ERRG\5YR_C-1_PhotoLocMap_IR7_18_10_4.mxd ERRG-Martinez pmead

Figure C-1. Photo Location and View Map – IR Sites 07 and 18

Hunters Point Naval Shipyard, San Francisco, California

Appendix C3. Photographic Log, Parcel B-1

Photograph C3-1: View of soil cover on slope southwest of Building 113. Cover vegetation is generally well established and in good condition. No evidence of erosion, subsidence, or settlement. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-2: View of retaining wall along toe of soil cover southwest of Building 113. Retaining wall is stable with no evidence of settlement or cracking. Facing southeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-3: View of soil cover adjacent to Galvez Avenue. Minor areas of disturbed soil visible in foreground caused by burrowing rodents; typical of soil cover damage that has been documented and addressed during periodic O&M repair events. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-4: View of outfall protection for storm drain pipe southwest of Building 120. Riprap armoring is in good condition, and outfall is functioning as intended. Facing southwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-5: View of durable asphaltic pavement cover southwest of Building 121. Cover is generally intact and in good condition. Facing northeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-6: View of durable asphaltic pavement cover northeast of Building 121. Cover is generally intact and in good condition. Facing southwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-7: View of drainage swale in durable asphaltic pavement cover southwest of Dry Docks 5, 6, and 7. Cover is in good condition and swale is free of debris. Facing southeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-8: View of drainage swale in durable asphaltic pavement cover northwest of Building 156. Asphalt pavement in the swale is damaged due to vehicle traffic, but it adequately prevents exposure to underlying soil. Facing southeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-9: View of durable asphaltic pavement cover along Donahue Street. Cover is generally intact and in good condition. Facing northeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-10: View of drainage swale in durable asphaltic pavement cover southwest of Building 123, with small accumulation of water. Minor cover damage caused by weed growth along edge of swale; typical of cover damage that has been documented and addressed during periodic O&M repair events. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-11: View of shoreline revetment north of Building 145. Revetment is stable, with no evidence of settlement or movement. Facing southwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-12: Monitoring well completions (typical) intact and in good condition. Facing southwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-13: Settlement monument (typical) intact and in good condition. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-14: Chain-link fence and gate at site entrance on Robinson Street. Fence and gate are intact and in good condition. Entrance sign is intact and legible with current BRAC information. Facing northeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-15: SVE wells and conveyance piping at IR-10 (inside Building 123) intact and in good condition. Facing southwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C3-16: SVE treatment system at IR-10 is intact and functioning as intended. Facing northeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

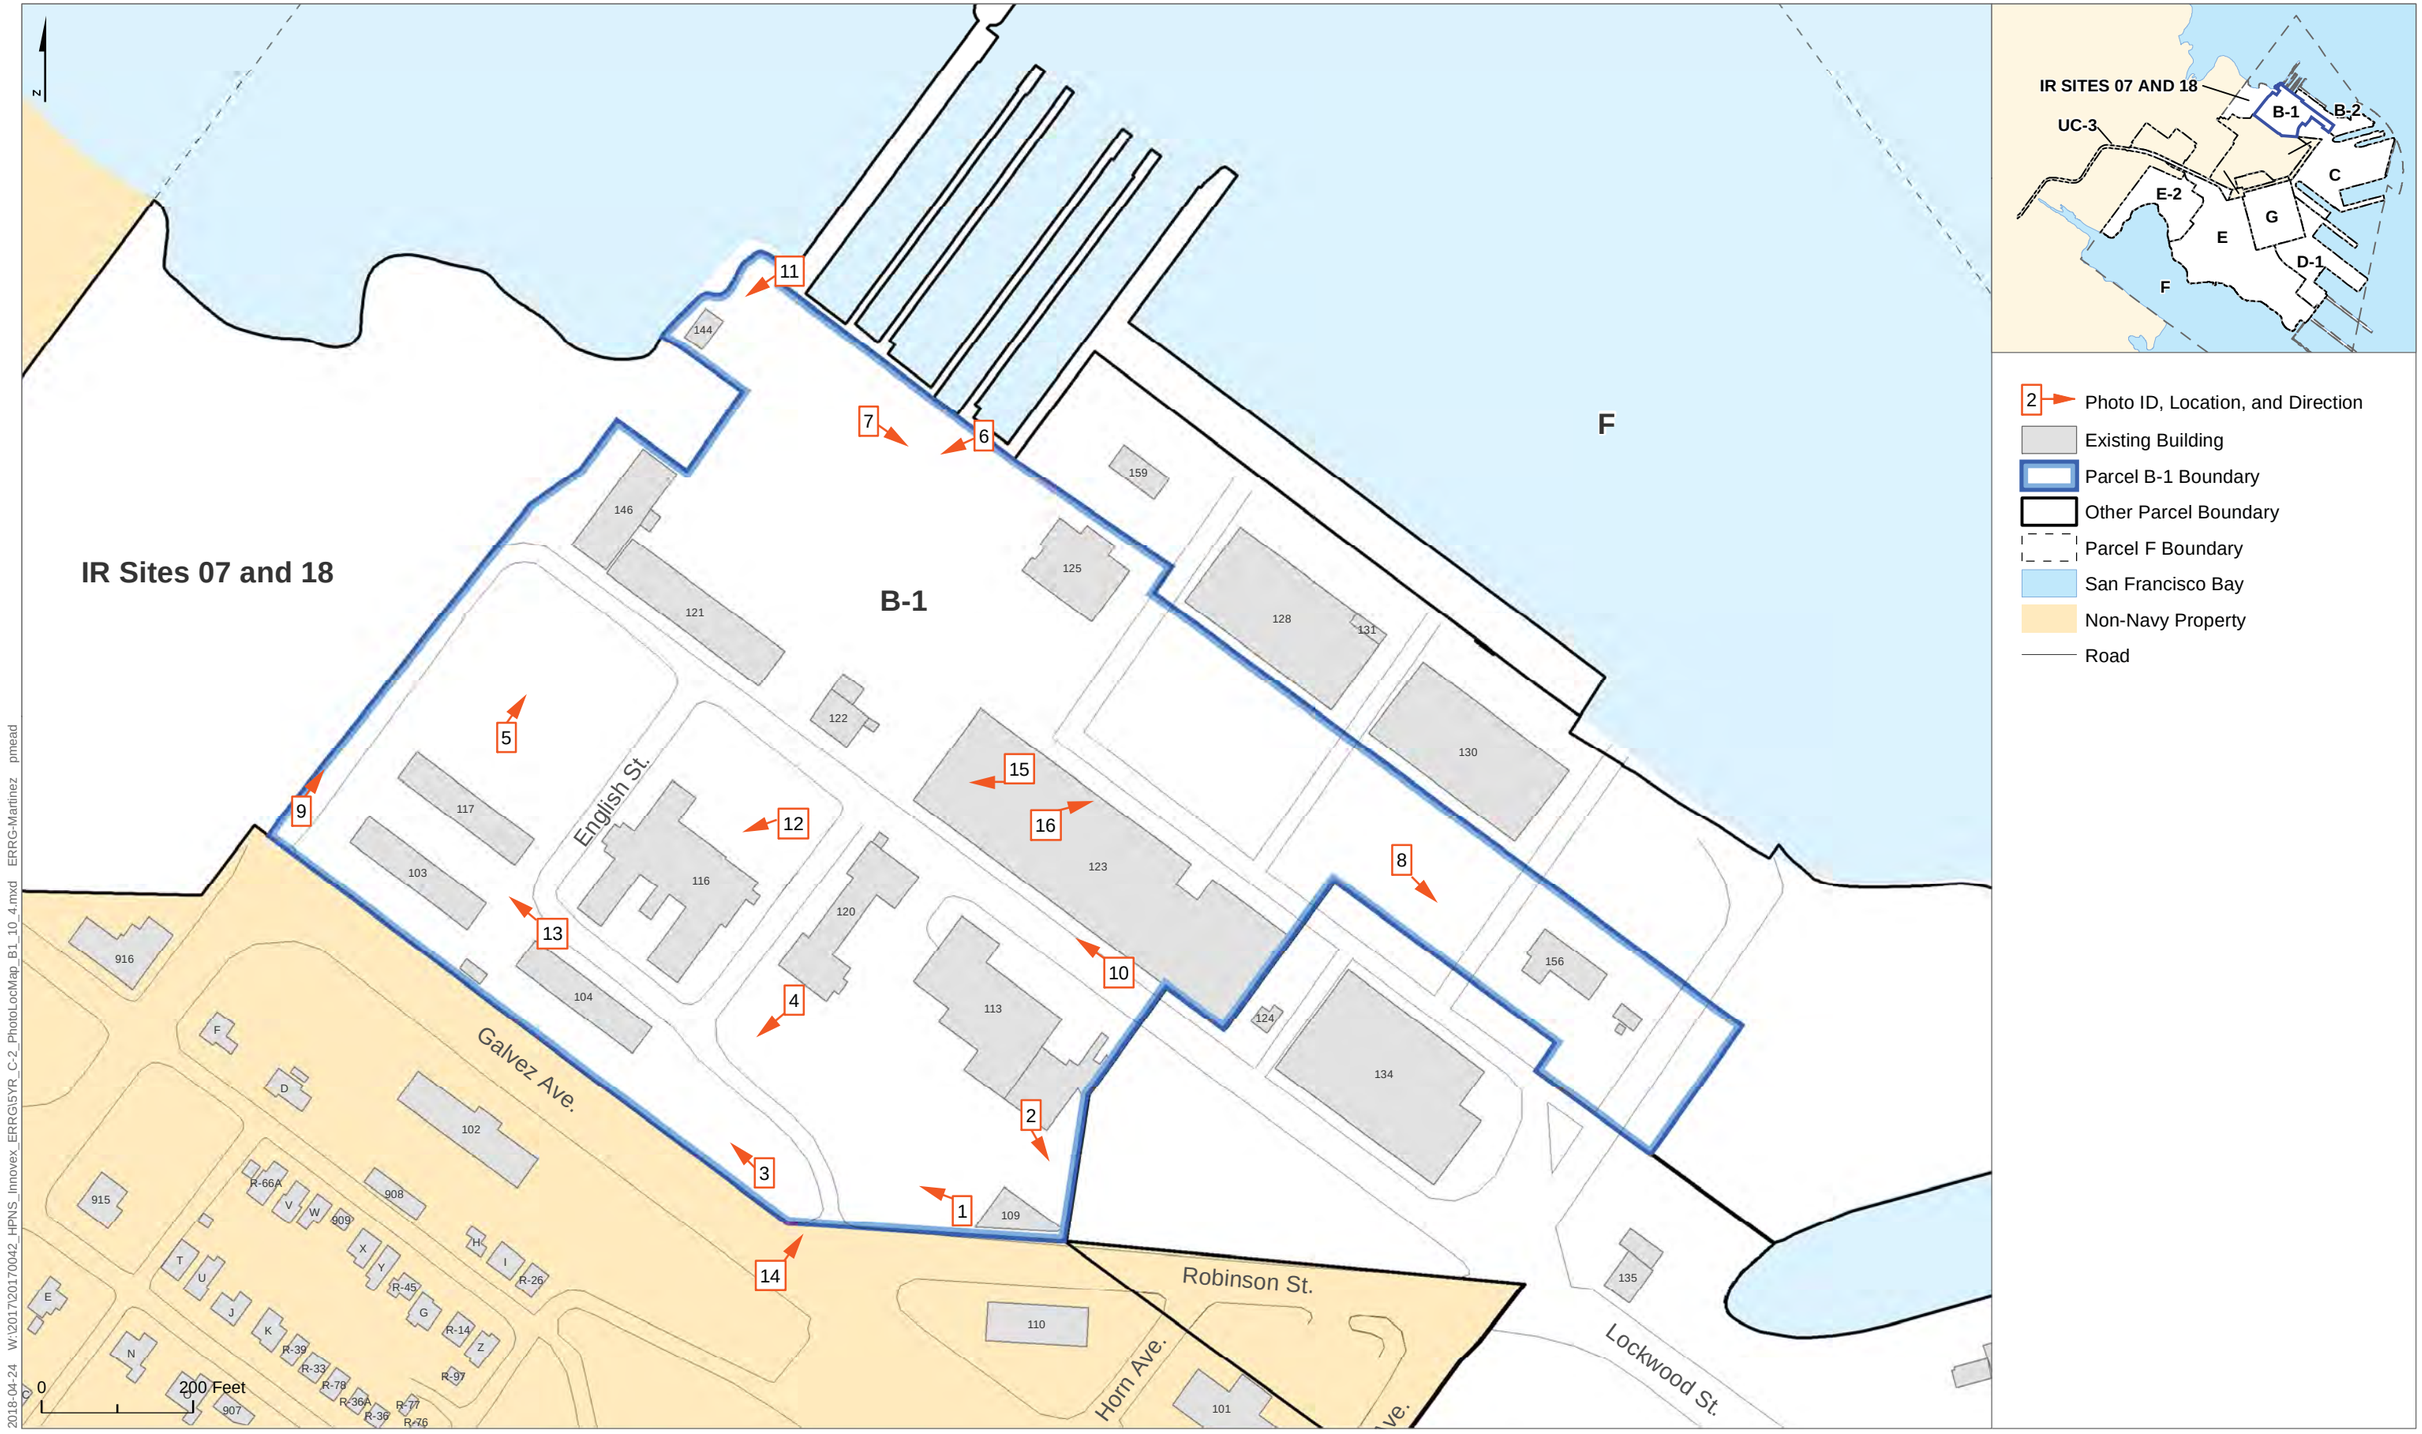

Figure C-2. Photo Location and View Map – Parcel B-1

Hunters Point Naval Shipyard, San Francisco, California

Appendix C4. Photographic Log, Parcel B-2

Photograph C4-1: View of durable asphaltic pavement cover near Parcel C boundary. Cover is generally intact and in good condition. Facing east.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C4-2: View of durable asphaltic pavement cover west of Building 140. Cover is generally intact and in good condition. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C4-3: View of durable asphaltic pavement cover near IR-26. Cover is generally intact and in good condition. Facing south.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C4-4: View of durable asphaltic pavement cover north of Building 130. Cover is generally intact and in good condition. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C4-5: View of drainage swale in durable asphaltic pavement cover northwest of Building 159. Cover is in good condition and swale is free of debris. Facing east.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

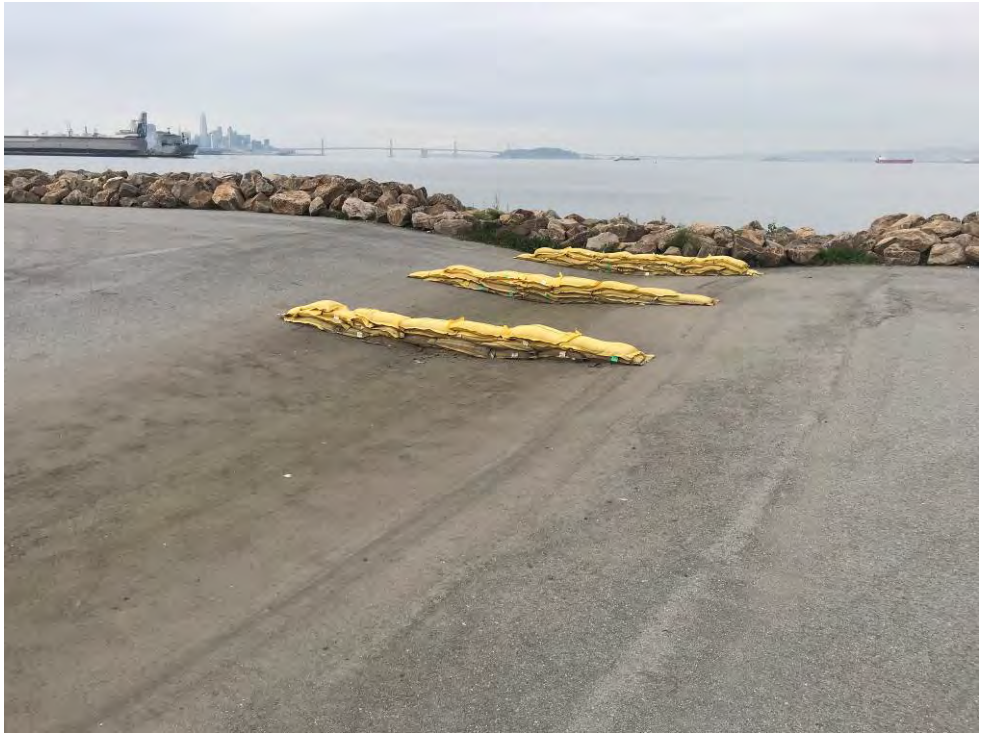

Photograph C4-6: View of swale outfall north of Building 140. Check dams are intact and functioning as intended. Facing north.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

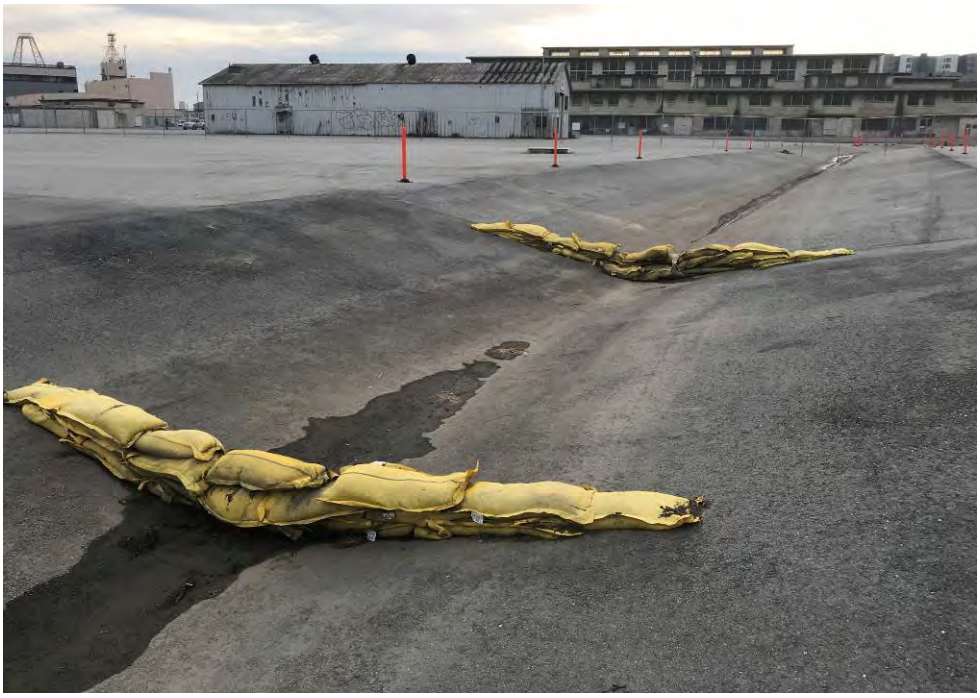

Photograph C4-7: View of swale outfall east of Building 130. Check dams are intact and functioning as intended. Facing south.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

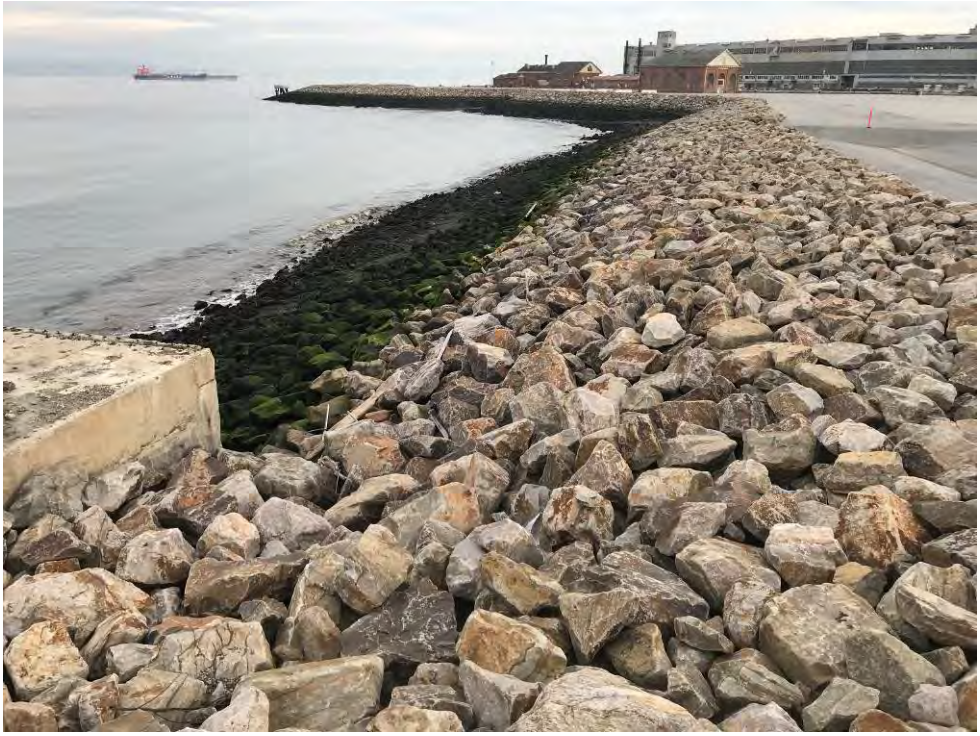

Photograph C4-8: View of shoreline revetment north of Building 130. Revetment is stable, with no evidence of settlement or movement. Facing southeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

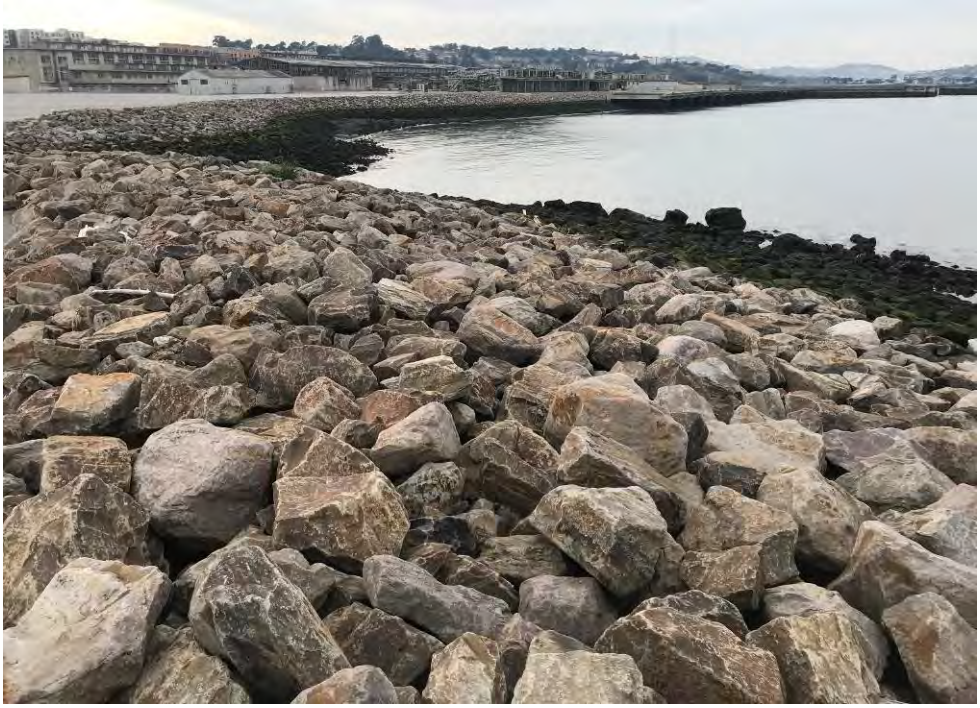

Photograph C4-9: View of shoreline revetment north of Building 140. Revetment is stable, with no evidence of settlement or movement. Facing west.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C4-10: Historic Building 140 secured to prevent access to foundation. Facing north.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C4-11: View of the Building 128 foundation. Building foundations (typical) intact and in good condition. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C4-12: All warning signs are intact and legible with current BRAC contact information. Fence is intact and in good condition. Facing northeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C4-13: Chain-link fence along Parcel B-1 boundary recently installed for basewide access control. Fence is intact and in good condition. Facing north.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C4-14: Chain-link fence along Parcel B-1 boundary recently installed for basewide access control. Fence is intact and in good condition. Facing west.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C4-15: Monitoring well completions (typical) intact and in good condition. Facing southwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C4-16: Survey monument (typical) intact and in good condition. Facing southwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

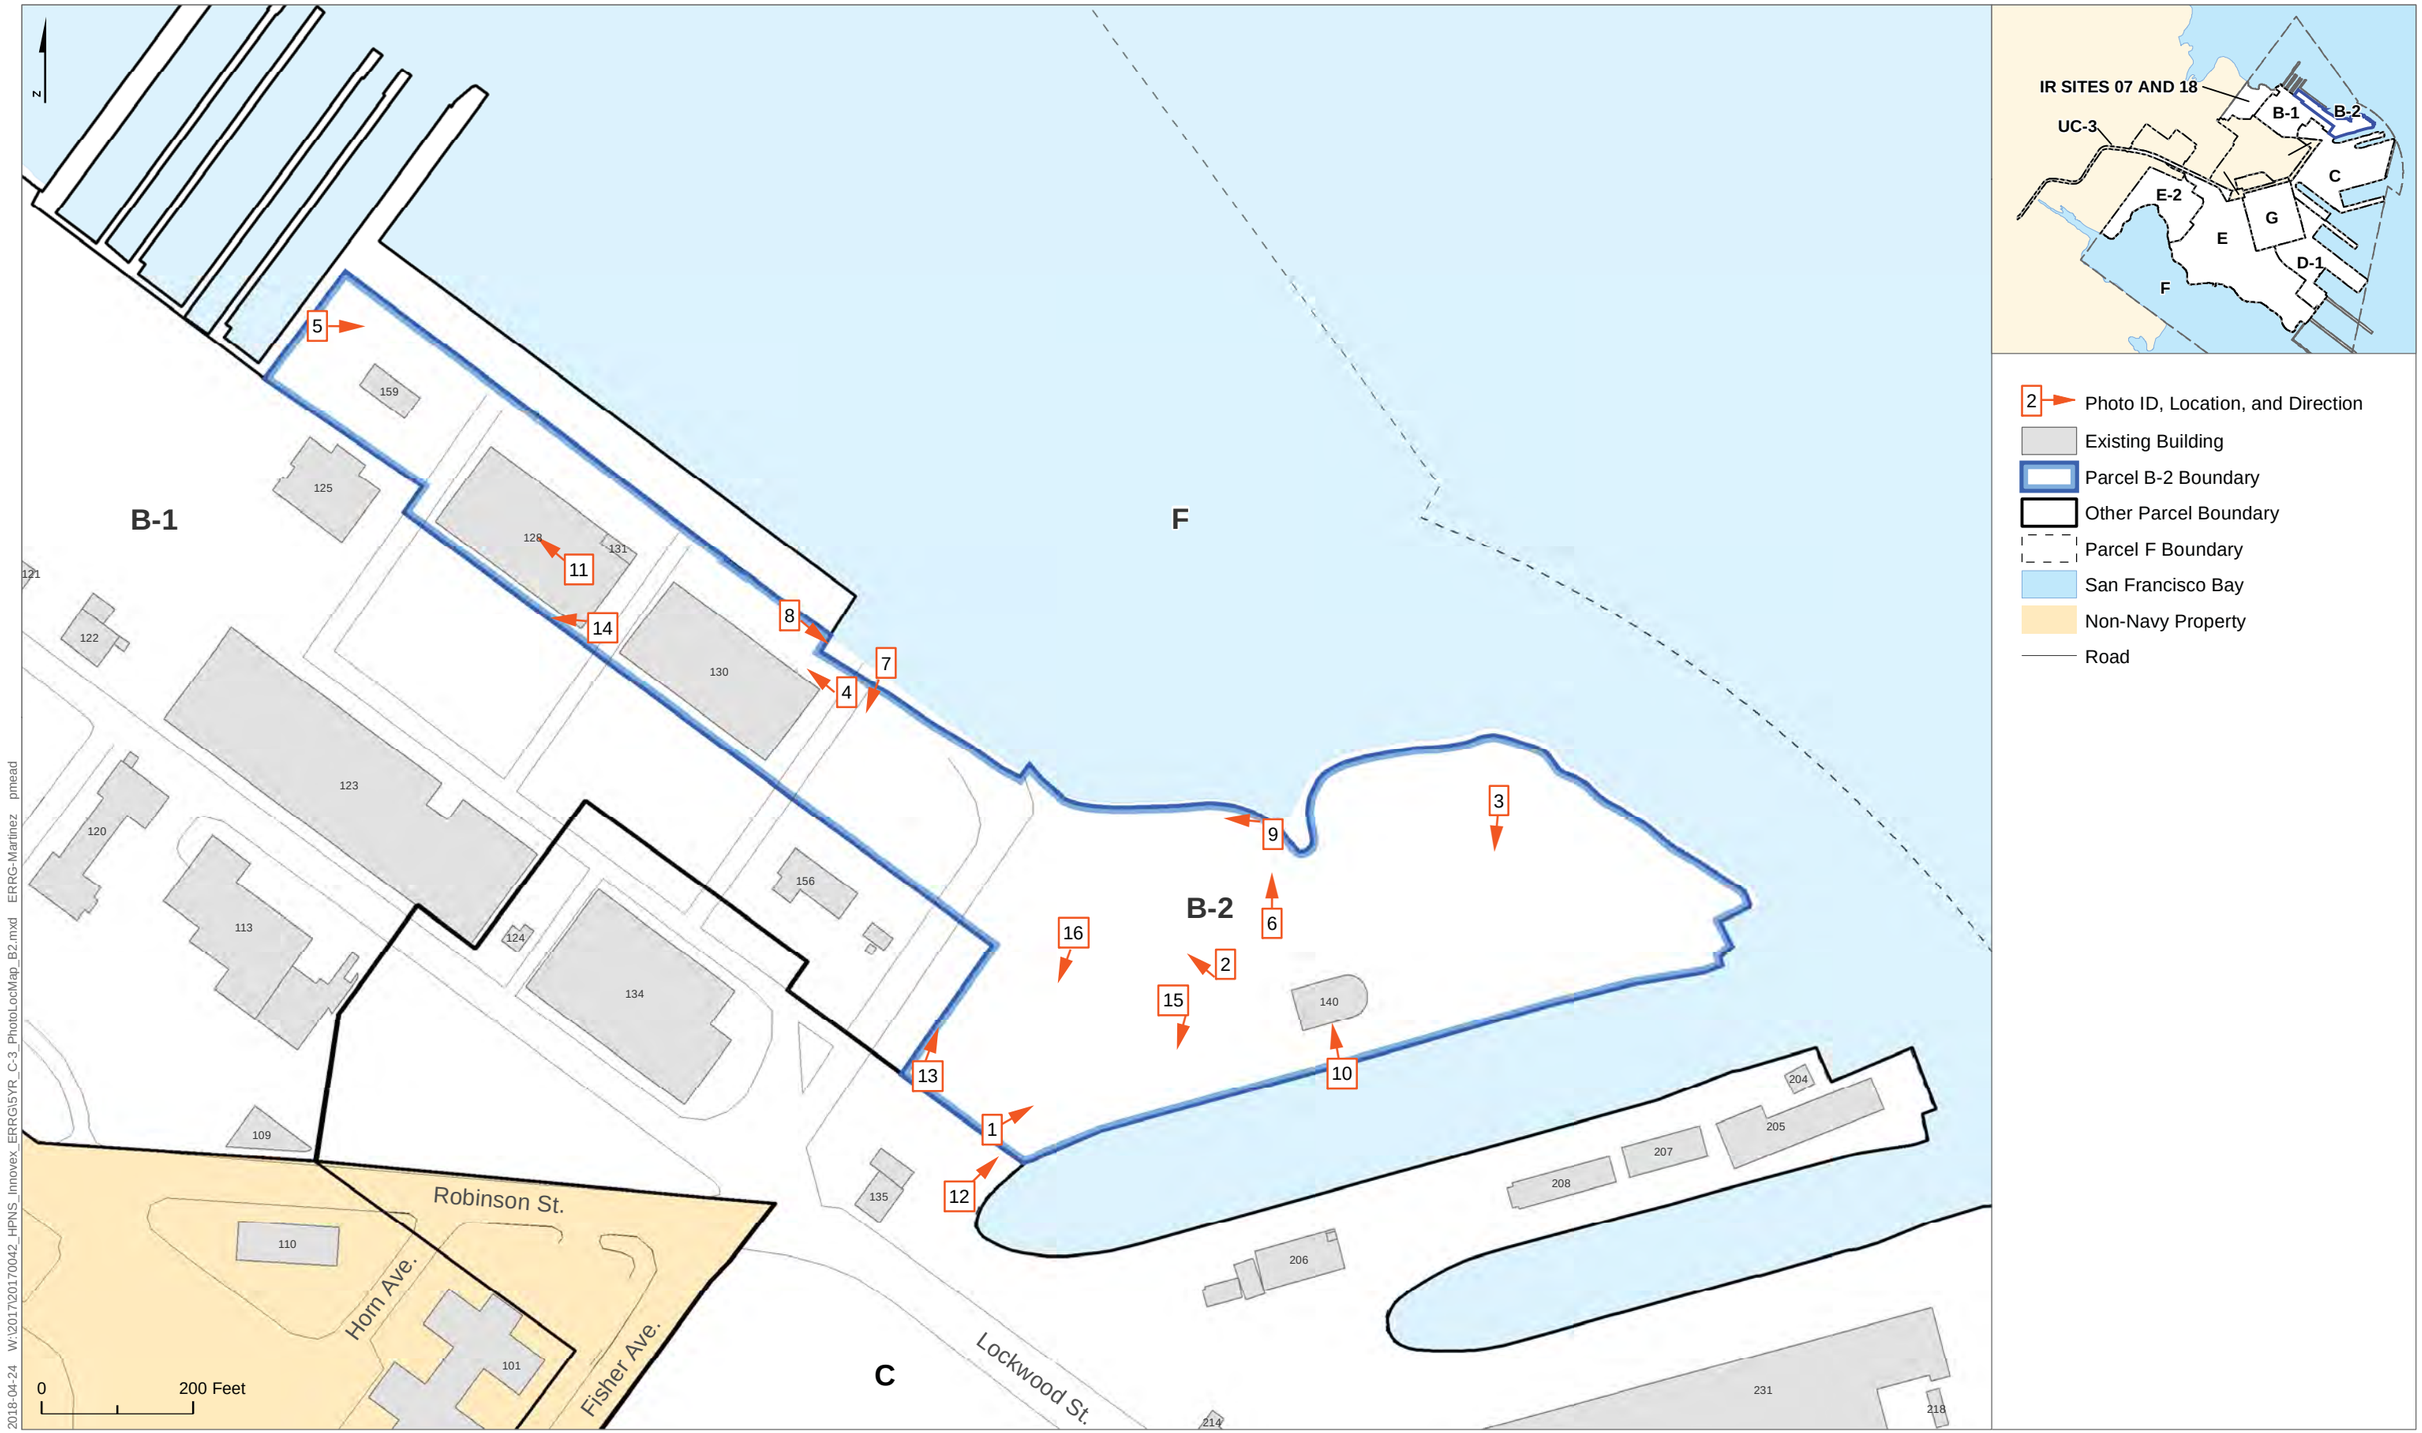

2018-04-24 W:\2017\20170042_HPNS_Innovex_ERRG\5YR_C-3_PhotoLocMap_B2.mxd ERRG-Martinez pmead

Figure C-3. Photo Location and View Map – Parcel B-2
Hunters Point Naval Shipyard, San Francisco, California

Appendix C5. Photographic Log, Parcel C

Photograph C5-1: View of durable asphaltic pavement cover near intersection of Robinson Street and Fisher Avenue. Cover is generally intact and in good condition. Facing southeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

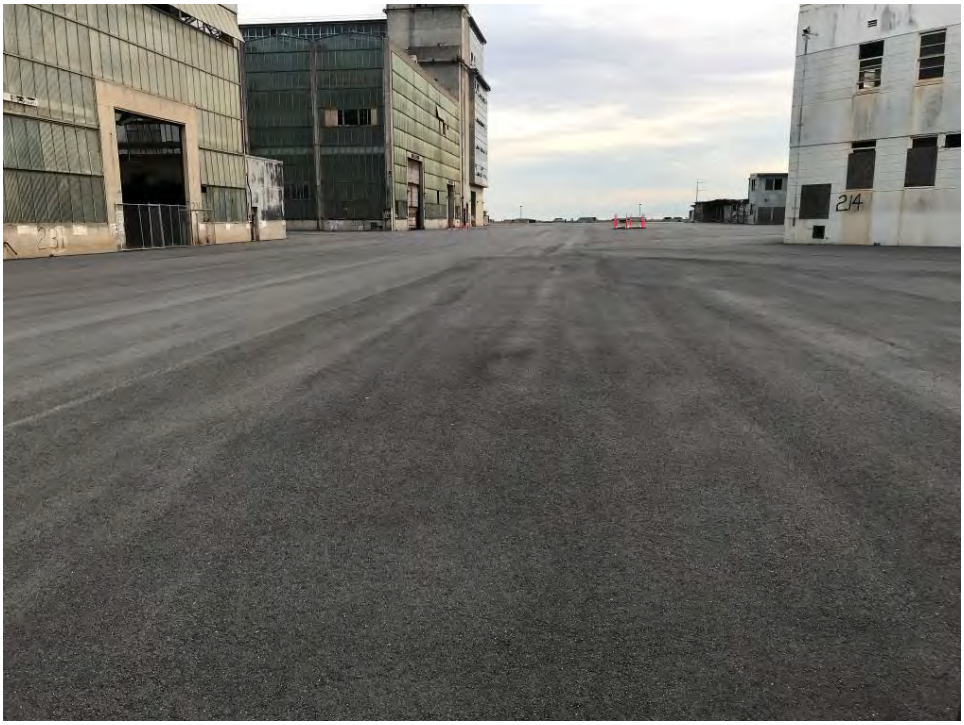

Photograph C5-2: View of durable asphaltic pavement cover west of Building 231. Cover is generally intact and in good condition. Facing south.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

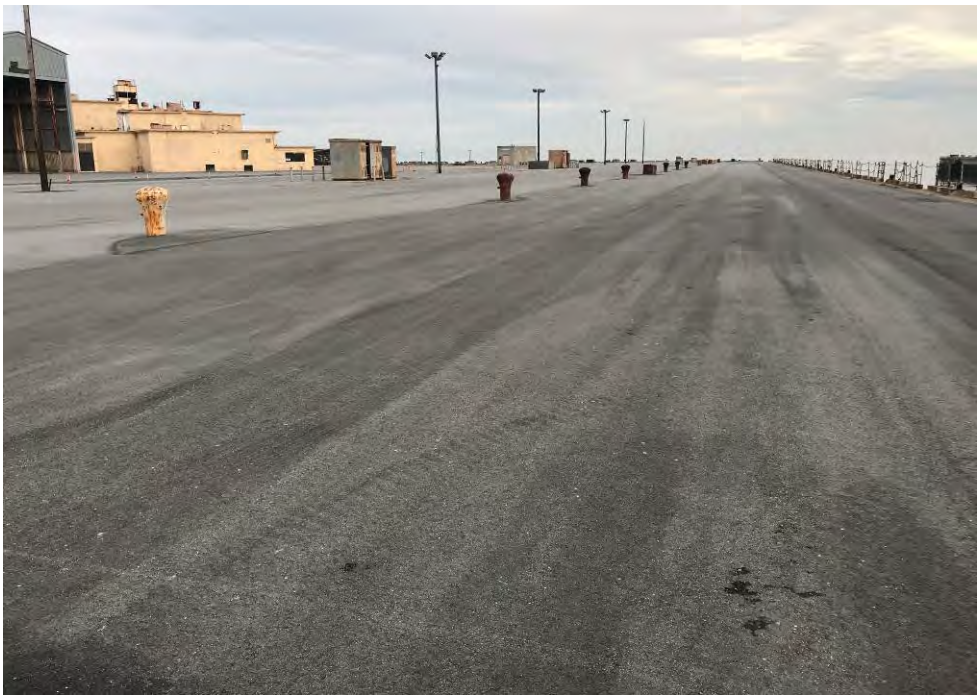

Photograph C5-3: View of durable asphaltic pavement cover north of Dry Dock 4. Cover is generally intact and in good condition. Facing southeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-4: View of durable asphaltic pavement cover north of Building 241. Cover is generally intact and in good condition. Facing northeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

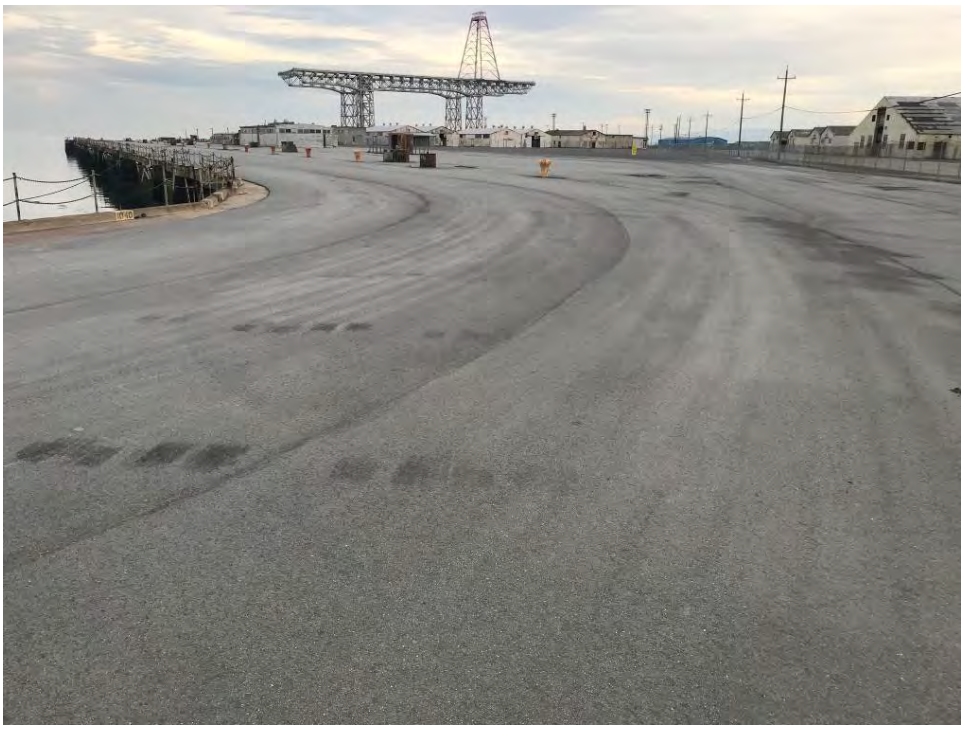

Photograph C5-5: View of durable asphaltic pavement cover south of Dry Dock 4. Cover is generally intact and in good condition. Facing south.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

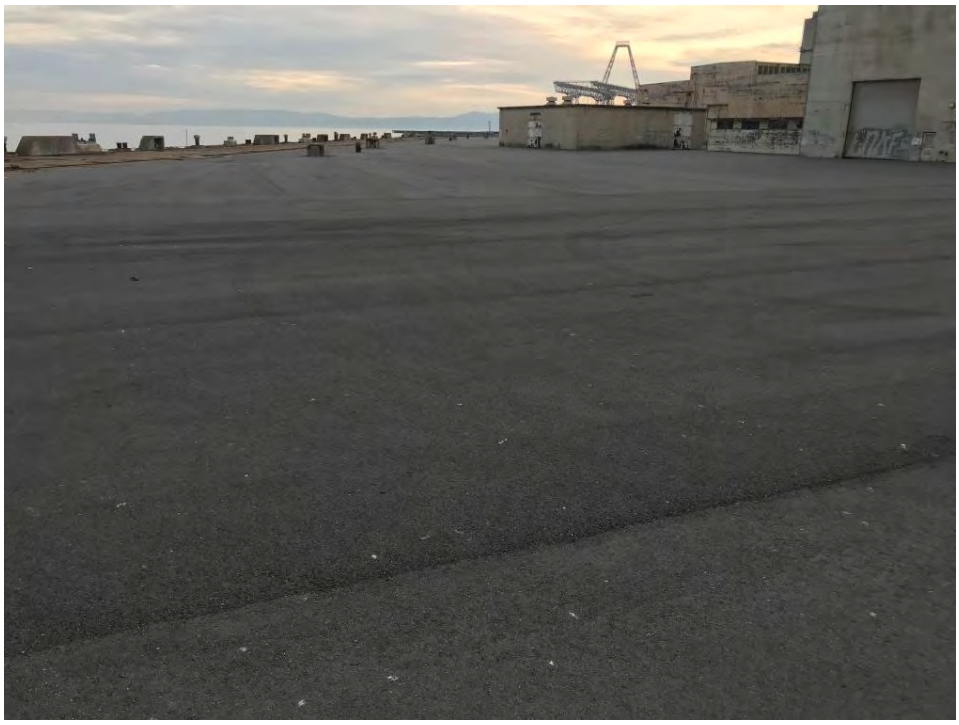

Photograph C5-6: View of durable asphaltic pavement cover at southeast end of Dry Dock 2. Cover is generally intact and in good condition. Facing south.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-7: View of drainage swale at east end of Spear Street. Cover is in good condition, and swale is free of debris. Check dams are intact and functioning as intended. Facing west.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-8: View of drainage swale west of Building 214. Cover is in good condition, and swale is free of debris. Check dams are intact and functioning as intended. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-9: View of swale outfall south of Building 230. Check dams are intact and functioning as intended. Facing east.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-10: BMPs around catch basins (typical) intact and free of sediment. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

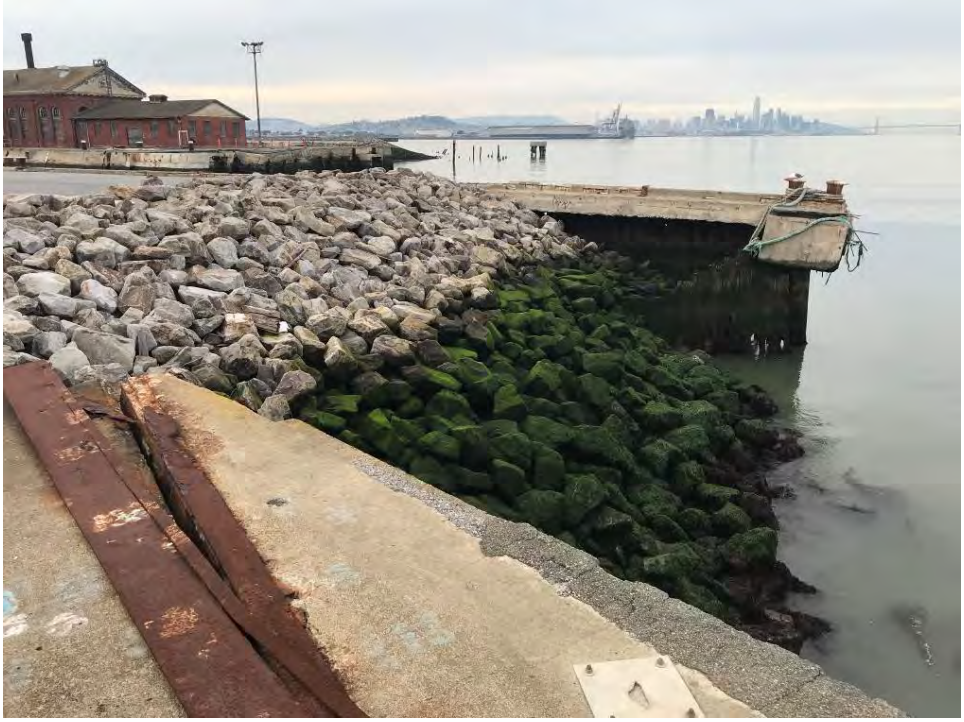

Photograph C5-11: View of shoreline armoring northeast of Building 231. Riprap armoring is stable, with no evidence of settlement or movement. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-12: Buildings secured (typical) to prevent access to foundation. Facing north.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-13: View of Building 231 foundation. Building foundations (typical) intact and in good condition. Facing northeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-14: View of soil cover west of Building 134. Cover vegetation is generally well established and in good condition. No evidence of erosion, subsidence, or settlement observed. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-15: View of soil cover west of Building 134. Minor areas of disturbed soil visible in foreground caused by burrowing rodents; typical of soil cover damage that has been documented and addressed during periodic O&M repair events. Facing southeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-16: West end of soil cover disturbed and fencing removed to permit redevelopment work by non-Navy contractor. Facing southeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-17: SVE treatment systems, wells, and conveyance piping and surrounding chain-link fencing intact with no signs of vandalism. Facing northeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-18: Entrance gate at intersection of Robinson Street and Fisher Avenue is intact and in good condition. All warning signs are intact and legible with current BRAC contact information. Facing southeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

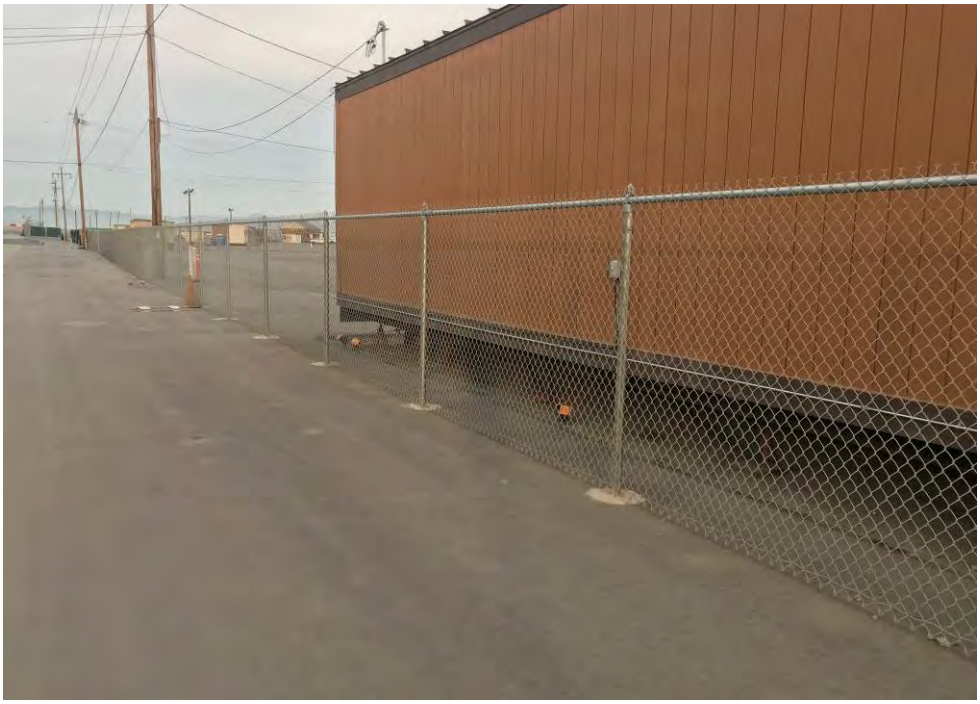

Photograph C5-19: Chain-link fence along Fisher Avenue is intact and in good condition. Facing northeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-20: Chain-link fence along Robinson Street is intact and in good condition. West end of fencing removed to permit site work by non-Navy contractor. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-21: Monitoring well completions (typical) intact and in good condition. Facing east.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C5-22: Survey monument 2 intact and in good condition. Survey monument 1 was demolished by non-Navy contractor to permit site work and will be replaced upon completion.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

2018-04-24 W:\2017\20170042_HPNS_Innovex_ERRG\5YR_C-4_PhotoLocMap_C.mxd ERRG-Martinez pmead

Figure C-4. Photo Location and View Map – Parcel C

Hunters Point Naval Shipyard, San Francisco, California

Appendix C6. Photographic Log, Parcel G

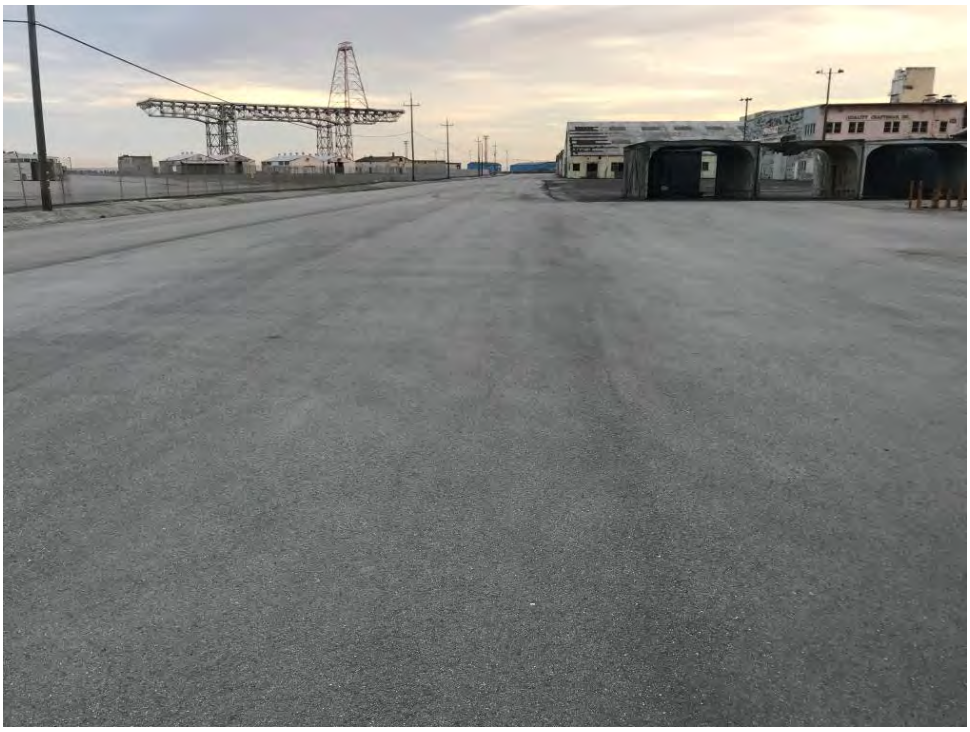

Photograph C6-1: View of durable asphaltic pavement cover east of Building 302. Cover is generally intact and in good condition. Facing south.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C6-2: View of durable asphaltic pavement cover north of Building 402. Cover is generally intact and in good condition. Facing west.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C6-3: View of durable asphaltic pavement cover north of Building 411. Cover is generally intact and in good condition. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C6-4: View of durable asphaltic pavement cover south of Building 404. Cover is generally intact and in good condition. Facing southeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C6-5: View of durable asphaltic pavement cover near intersection of Manseau Street and Morrell Street. Cover is generally intact and in good condition. Facing east.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C6-6: View of concrete utility corridor cover west of Building 351. Cover is generally intact and in good condition. Facing south.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C6-7: View of repaired concrete cover north of Building D-A. Cover is generally intact and in good condition. Facing west.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C6-8: View of seal coat cover east of Building 363. Cover has some minor cracking due to weeds, but it adequately prevents exposure to underlying soil. Facing north.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C6-9: View of swale outfall east of Building D-A. Check dams are intact and functioning as intended. Facing north.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C6-10: View of the Building 411 foundation. Building foundations (typical) intact and in good condition. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C6-11: Entrance gates (typical) are intact and in good condition. Facing northeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C6-12: K-rail barrier along H Street intact and in good condition. Facing southeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

Photograph C6-13: Chain-link fence along Parcel D-1 boundary is intact and in good condition. Facing southeast.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C6-14: Monitoring well completions (typical) intact and in good condition. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: Spencer Johnson, P.E. (IEJV) Date: January 29, 2018

Photograph C6-15: Survey monument (typical) intact and in good condition. Facing west.
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California
Photographed by: Steven Hoeft, P.E. (IEJV) Date: January 29, 2018

2018-04-24 W:\2017\20170042_HPNS_Innovex_ERRG\5YR_C-5_PhotoLocMap_G_10_4.mxd ERRG-Martinez pmead

Figure C-5. Photo Location and View Map – Parcel G

Hunters Point Naval Shipyard, San Francisco, California

Appendix C7. Photographic Log, Parcel UC-3

Photograph C7-1: View of durable asphaltic pavement cover at southern end of Crisp Road. Cover is generally intact and in good condition. Facing south.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-2: View of durable asphaltic pavement cover at southern end of Crisp Road. Cover is generally intact and in good condition. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-3: View of durable asphaltic pavement cover at southern end of Crisp Road. Area of damaged asphaltic concrete in roadway caused by heavy truck traffic. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-4: View of durable asphaltic pavement cover at southern end of Crisp Road. Cover is generally intact and in good condition. Facing west.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-5: View of concrete utility corridor cover at southern end of Crisp Road. Cover is generally intact and in good condition. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-6: View of durable asphaltic pavement cover at southern end of Crisp Road. Cover is generally intact and in good condition. Facing west.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-7: View of southernmost infiltration trench along Crisp Road. Trench is intact and in good condition. Functionality of the trench was not assessed. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-8: View of durable asphaltic pavement cover at southern end of Crisp Road. Area of damaged asphaltic concrete in roadway caused by heavy truck traffic. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-9: View of durable asphaltic pavement cover in central portion of Crisp Road. Cover is generally intact and in good condition. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-10: View of one of the northernmost infiltration trenches along Crisp Road. Trench is intact and in good condition. Functionality of the trench was not assessed. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-11: View of durable asphaltic pavement cover in northern portion of Crisp Road. Cover is generally intact and in good condition. Facing west.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-12: View of concrete sidewalk cover in northern portion of Crisp Road. Sidewalk is cracked and weathered, but it adequately prevents exposure of underlying soil. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-13: View of northernmost infiltration trench along Crisp Road. Trench is intact and in good condition. Functionality of the trench was not assessed. Facing northwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-14: Chain-link fence along Crisp Road recently installed for basewide access control. Fence is intact and in good condition. Facing south.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-15: Chain-link fence along Crisp Road recently installed for basewide access control. Fence is intact and in good condition. Facing southwest.
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California
Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-16: Monitoring well completions (typical) intact and in good condition.
Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California
Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-17: Chain-link fence along Crisp Road recently installed for basewide access control. Fence is intact and in good condition. Facing southwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

Photograph C7-18: Active utility vault covers integrated into durable cover and secured. Facing southwest.

Fourth Five-Year Review, Hunters Point Naval Shipyard, San Francisco, California

Photographed by: John Sourial, P.E. (IEJV) Date: January 29, 2018

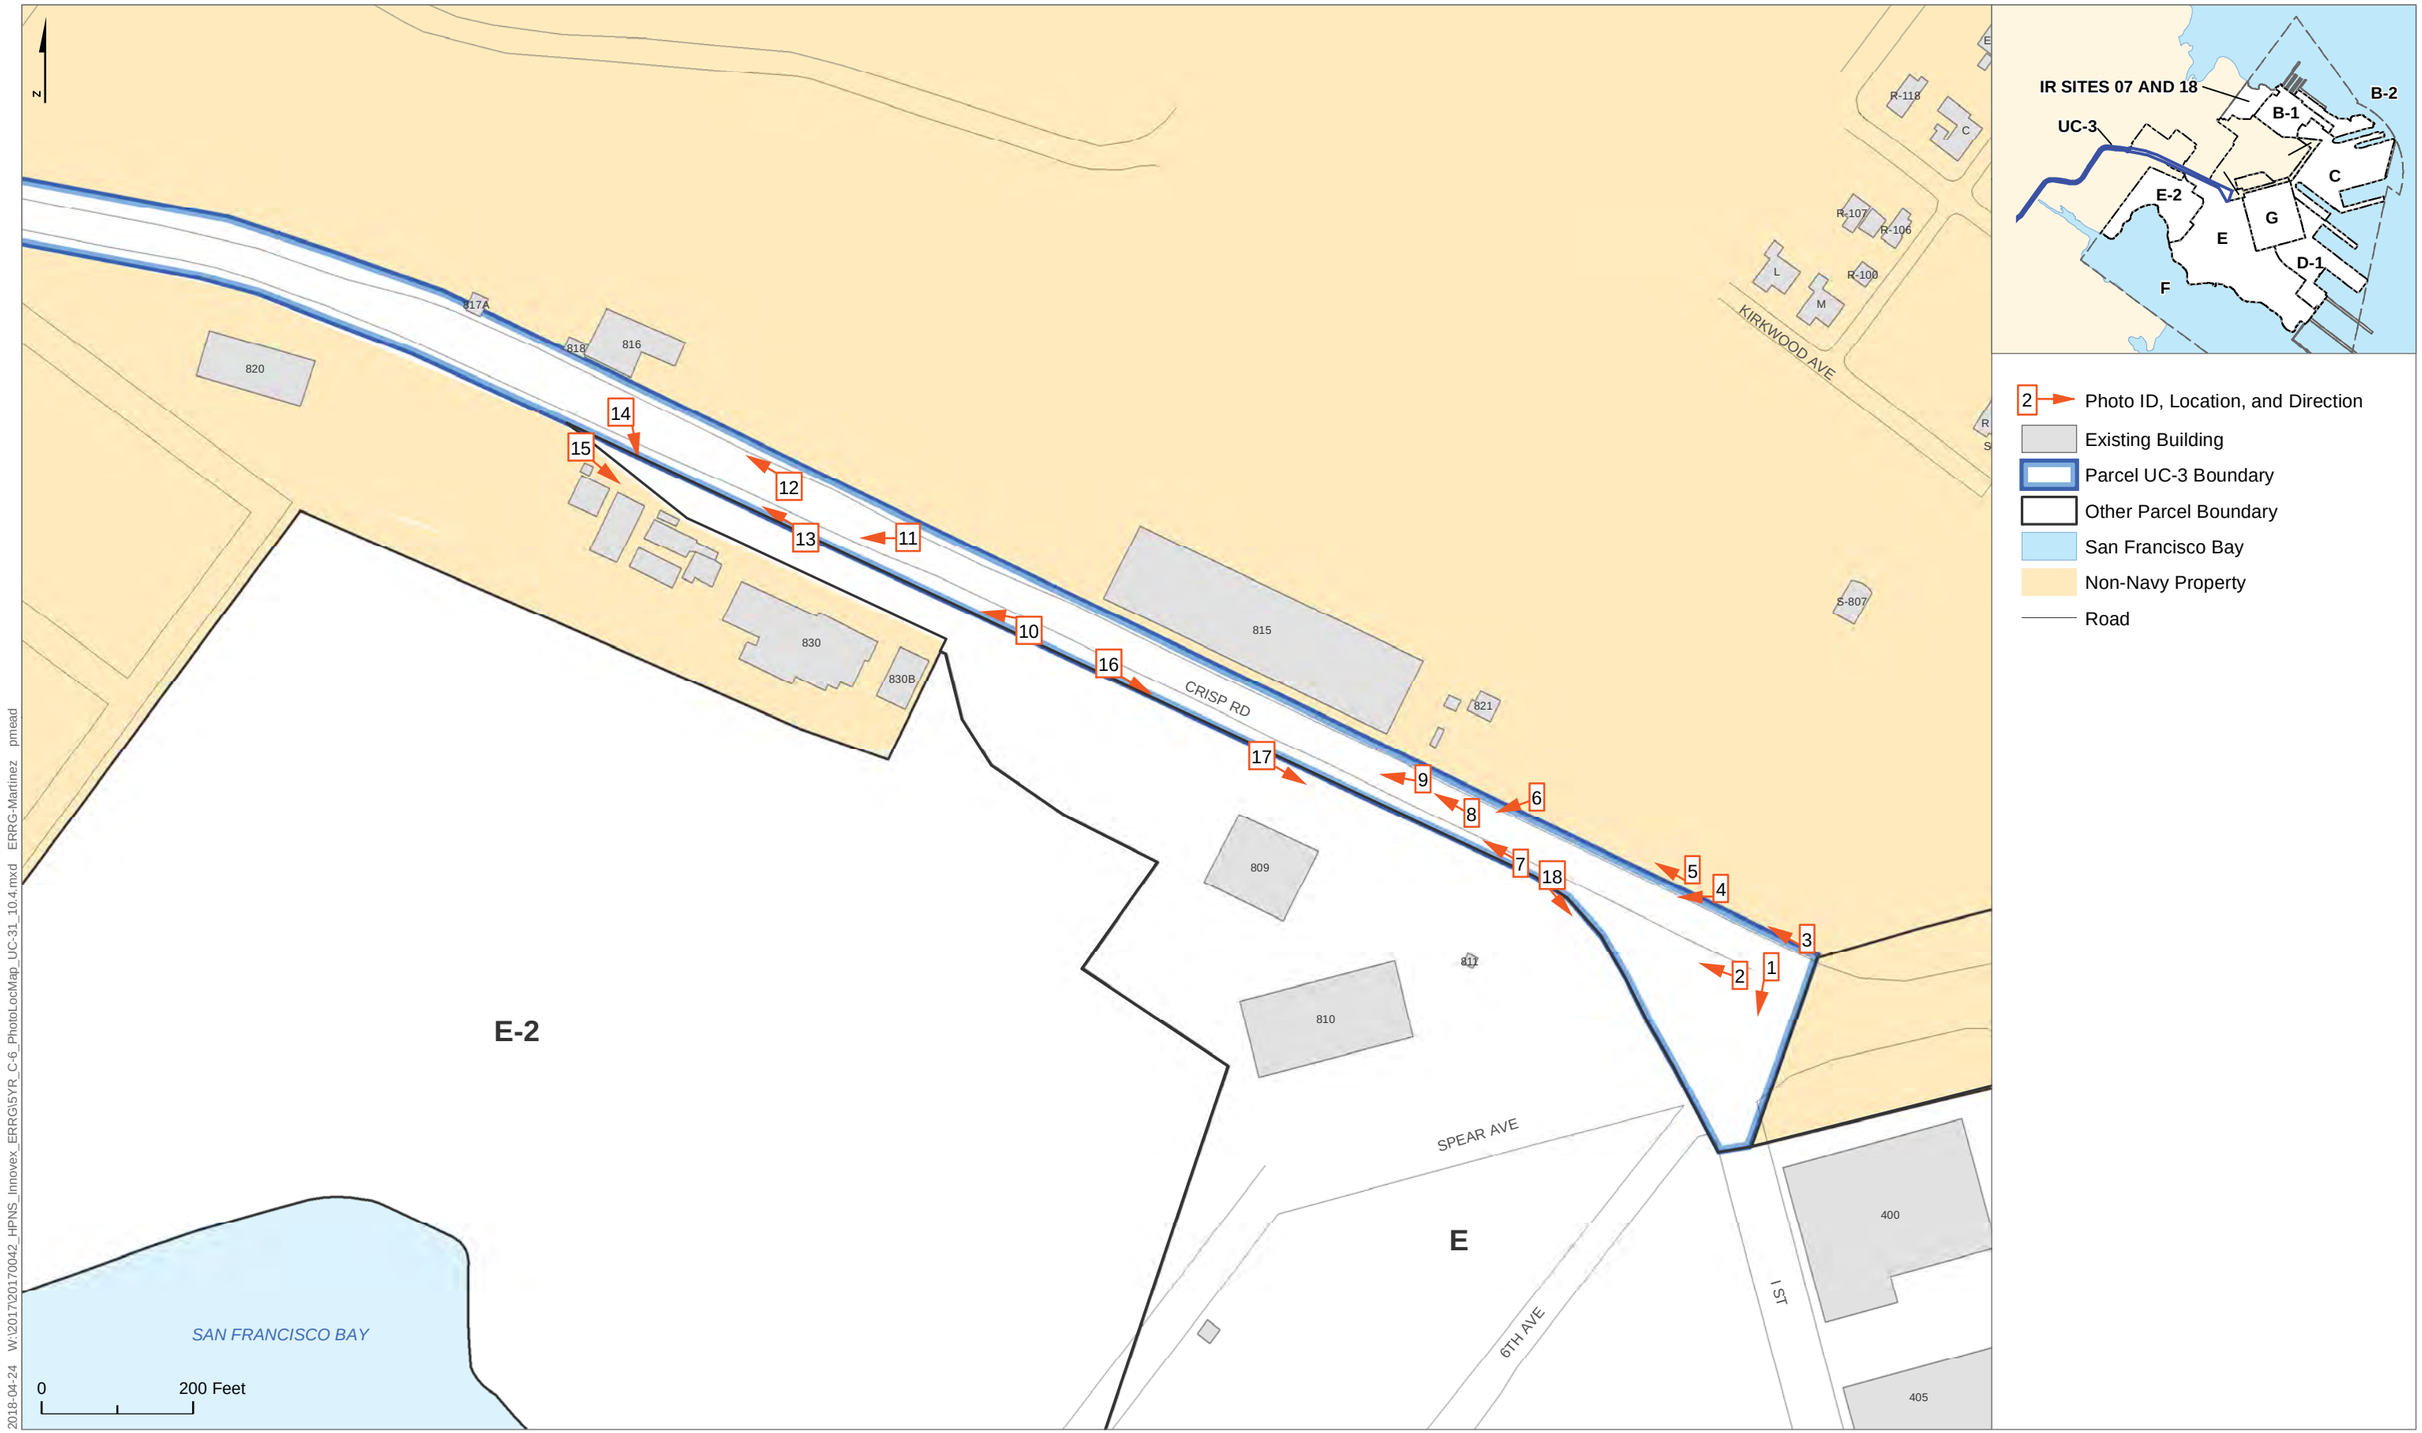

2018-04-24 W:\2017\201700042_HPNS_Innovex_ERRG\5YR_C-6_PhotoLocMap_UC-31_10.4.mxd ERRG-Martinez pmead

Figure C-6. Photo Location and View Map – Parcel UC-3

Hunters Point Naval Shipyard, San Francisco, California
